

Lake Forest Elementary School



Address: 3550 SW 48 AVENUE, PEMBROKE PARK 33023
 Location Num: 0831
 Board District: 1
 Board Member: Daniel P. Foganholi
 ADEFP Budget: \$3,923,117
 Total Facilities Budget (Sum of Projects): \$3,542,155

PRIMARY RENOVATIONS P.001484 Lake Forest ES - Repair Roof on Bldg 4

CURRENT PHASE

9-Closed

RISK LEVEL

No Risk

PROJECT UPDATE

PROJECT SCOPE


Re-roof of Building #4 in accordance with all applicable Codes and Standards.

BUDGET

	Current Budget	Actuals	Remaining Budget
Construction	\$279,249	\$279,249	\$0
Direct Purchase	\$56,945	\$56,945	\$0
Construction Mgmt	\$34,800	\$34,800	\$0
Project Total:	\$370,994	\$370,994	\$0

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING	■																																															
ACTIVE CONSTRUCTION	■	■	■	■	■	■	■	■																																								

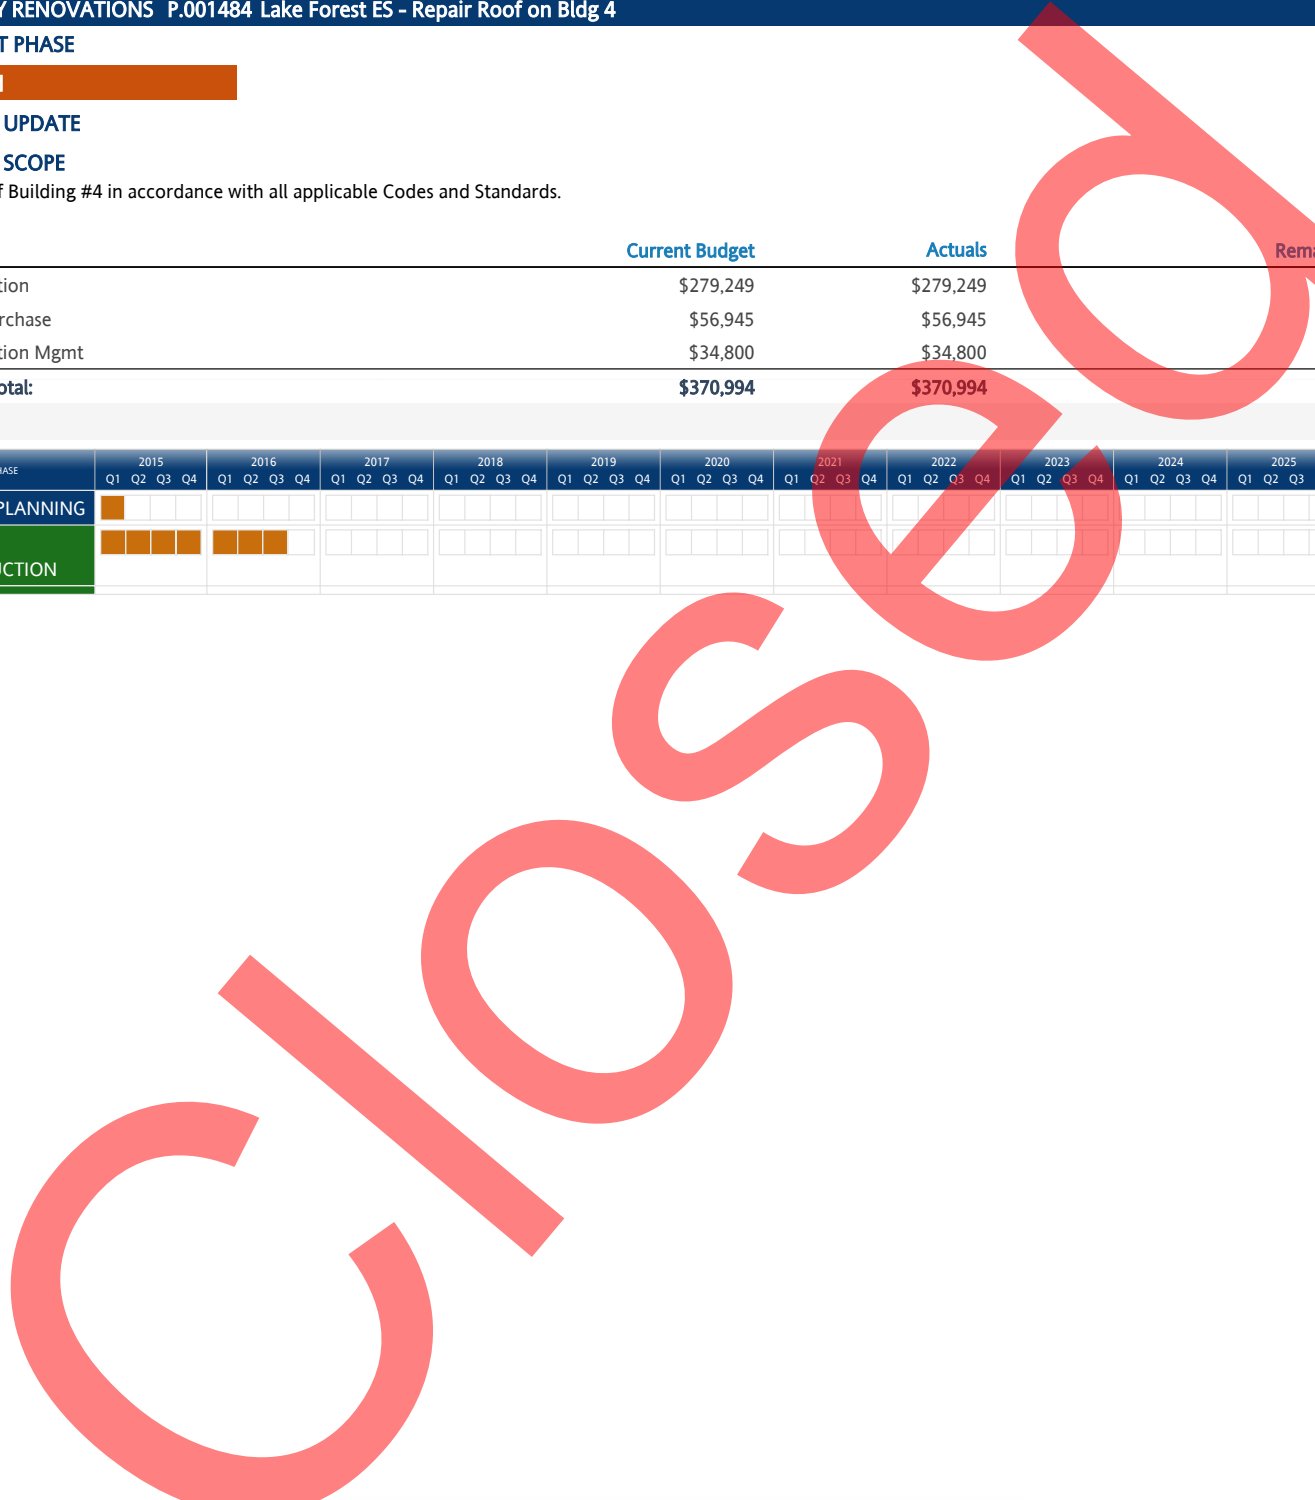

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Lake Forest Elementary School



Address: 3550 SW 48 AVENUE, PEMBROKE PARK 33023
 Location Num: 0831
 Board District: 1
 Board Member: Daniel P. Foganholi
 ADEFP Budget: \$3,923,117
 Total Facilities Budget (Sum of Projects): \$3,542,155

PRIMARY RENOVATIONS P.001886 Lake Forest ES - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

6-Substantial Completion



PROJECT UPDATE

The Construction Project Manager is processing PCO 11, that is cleared to go to Pre Corp.

PROJECT SCOPE

Reroofing: Buildings 01, 03, 05, 06, 07, 09, 10, & 13 HVAC Improvements: Controls, Condenser Units and Air Handlers to Buildings 01, 03, 04, 05, 06, & 07

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$304,979	\$295,833	\$9,146
Construction	\$2,181,440	\$1,986,637	\$194,803
Direct Purchase	\$197,031	\$195,530	\$1,501
Construction Mgmt	\$412,666	\$412,666	\$0
Contingency	\$67,744		\$67,744
Consultants	\$3,840		\$3,840
Utilities	\$3,461		\$3,461
Project Total:	\$3,171,161	\$2,890,666	\$280,495

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Projector, Cafeteria projection system, Teacher chairs, Blinds, Studio equipment, Office chairs, Traffic cones, Cone bars, Cone cart, Single cassette recorders, Headphones, Stools, Safety cones, Portable cooler, Canopy, Digital scanner, Desktops, Computer mice, Tablet, Benches/tables, Blinds, Web cams, Projector, Sanitizing electrostatic sprayer, Earthwalk Cart, Radio Accessories, Book cases, Two-Way Radios

BUDGET

\$100,000

IN PROGRESS

Two-Way Radios, Book cases

MUSIC

SCOPE

COMPLETE 608 Instruments delivered

TECHNOLOGY

SCOPE

COMPLETE 456 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.
