

Stranahan High School



Address: 1800 SW 5 PLACE, FORT LAUDERDALE 33312
 Location Num: 0211
 Board District: 3
 Board Member: Sarah Leonardi
 ADEFP Budget: \$47,183,091
 Total Facilities Budget (Sum of Projects): \$28,633,275

PRIMARY RENOVATIONS P.001683 Stranahan HS - SMART GOB Renovations

CURRENT PHASE

5B-Construction

RISK LEVEL

No Risk

PROJECT UPDATE

The Board terminated the CMAR on 8/8/23. The CMAR's construction trailer has been removed from the school. The remaining work will be completed by a CSMP contractor under P.001683-RC1 once funding is made available.

PROJECT SCOPE

-NTP: 8/31/18, SC: 1/15/21 -Roofing Replacement for Buildings 1, 2, 3, 4, 8, 9, 10, 11, 13, 14, 17,18, 20, 21, and 22. -Air Handler Replacements in Buildings 1, 2, 4, 5, 6, 7, 9, 10, 13, 14, 17, and 21. -Fire Alarm Complete Replacement of Campus. -Electrical Improvements to the main Switch Doghouses on-site. -Media Center (MC) and STEM lab improvements in Buildings 4, 6, 20, and 23. -Fire Sprinkler additions to Buildings 1, 2, and 9.

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$1,450,067	\$1,421,843	\$28,224
Construction	\$21,721,407	\$16,549,784	\$5,171,623
FF&E and Technology	\$385,172	\$375,825	\$9,347
Direct Purchase	\$2,680,016	\$2,649,041	\$30,975
Construction Mgmt	\$1,665,061	\$1,573,400	\$91,661
Contingency	\$313,485		\$313,485
Consultants	\$58,000	\$57,604	\$396
Misc Construction	\$15,508	\$15,508	\$0
Utilities	\$7,519		\$7,519
Project Total:	\$28,296,235	\$22,643,005	\$5,653,230

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4				
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

PRIMARY RENOVATIONS P.001683-HVC Stranahan HS - SMART Replace AC Units Room 101B and 101C

CURRENT PHASE

9-Closed

RISK LEVEL


No Risk

PROJECT UPDATE

PROJECT SCOPE

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4				
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

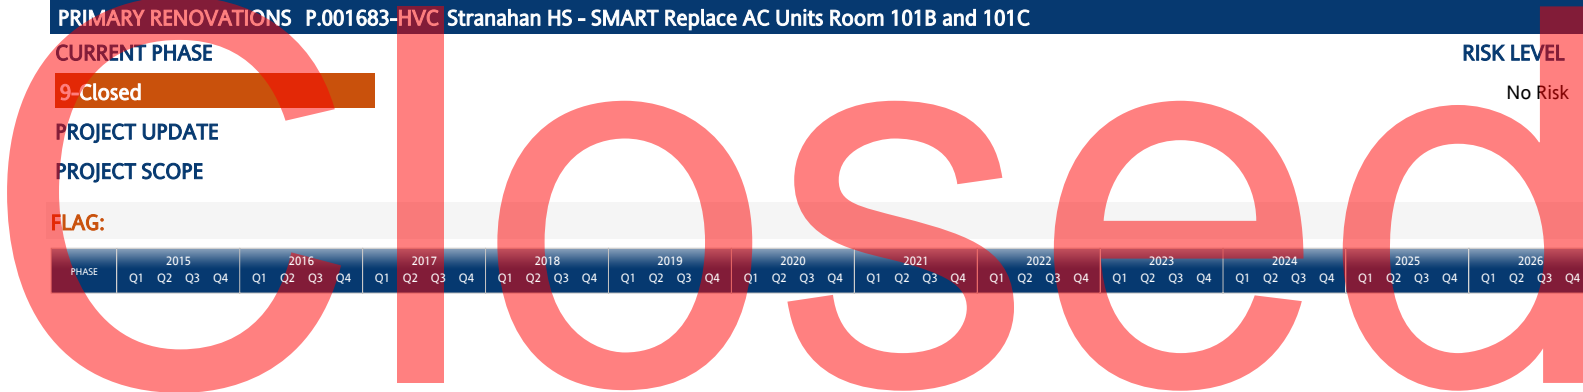

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



- HIGH:**
An issue that can impact the project's budget and/or schedule, a resolution is being determined.
- MEDIUM:**
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.
- LOW:**
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Stranahan High School



Address: 1800 SW 5 PLACE, FORT LAUDERDALE 33312
 Location Num: 0211
 Board District: 3
 Board Member: Sarah Leonardi
 ADEFP Budget: \$47,183,091
 Total Facilities Budget (Sum of Projects): \$28,633,275

PRIMARY RENOVATIONS P.001683-RC1 Stranahan HS - SMART Roofing Bldgs 2A, 2B, 2C, 8 & 9

CURRENT PHASE

RISK LEVEL

5A-Construction



PROJECT UPDATE

The Board terminated the former CMAR on 8/8/23. A new CSMP GC has been selected to complete the work. The NTP package has been prepared; however, funding is not currently available and has to be resolved by District Legal.

PROJECT SCOPE

Reroofing Bldgs 2A, 2B, 2C, 8, & 9; Demo/Construction of Bldg 6 Kiln Room; and Installation of the Bldg 4 exfiltration system. This is a new project to complete the remaining work that was not completed by the former CMAR.

BUDGET

	Current Budget	Actuals	Remaining Budget
Construction	\$300,000		\$300,000
Project Total:	\$300,000		\$300,000

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

50" TVs, outdoor picnic benches with umbrellas, projectors, document cameras, picnic tables, printers, scientific calculators, student laptops, column wraps, digital marquee, PA system, office furniture, Sisco STAR system IS machine, Laptops, High back black mock leather chairs, boat shaped conference tables, and slab table base, Indoor Furniture, Microphones

BUDGET

\$100,000

IN PROGRESS

Indoor Furniture, Microphones

ATHLETICS

SCOPE

COMPLETE Track, Weight Room

MUSIC

SCOPE

COMPLETE 271 Instruments Delivered

TECHNOLOGY

SCOPE

COMPLETE 723 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.
