

Boyd H. Anderson High School



Address: 3050 NW 41 STREET, LAUDERDALE LAKES 33309
 Location Num: 1741
 Board District: 5
 Board Member: Dr. Jeff Holness
 ADEFP Budget: \$12,820,525
 Total Facilities Budget (Sum of Projects): \$12,162,405

PRIMARY RENOVATIONS P.001360 Boyd Anderson HS - Media Ctr Remodeling

CURRENT PHASE

9-Closed

RISK LEVEL

No Risk

PROJECT UPDATE

PROJECT SCOPE


Renovation of the existing Media Center including select demolition, removal of existing interior stair, new interior wall, etc.

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$190,112	\$190,112	\$0
Construction	\$914,543	\$914,543	\$0
FF&E and Technology	\$181,090	\$181,090	\$0
Direct Purchase	\$33,769	\$33,769	\$0
Construction Mgmt	\$222,017	\$222,017	\$0
Consultants	\$28,770	\$28,770	\$0
Project Total:	\$1,570,301	\$1,570,301	\$0

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

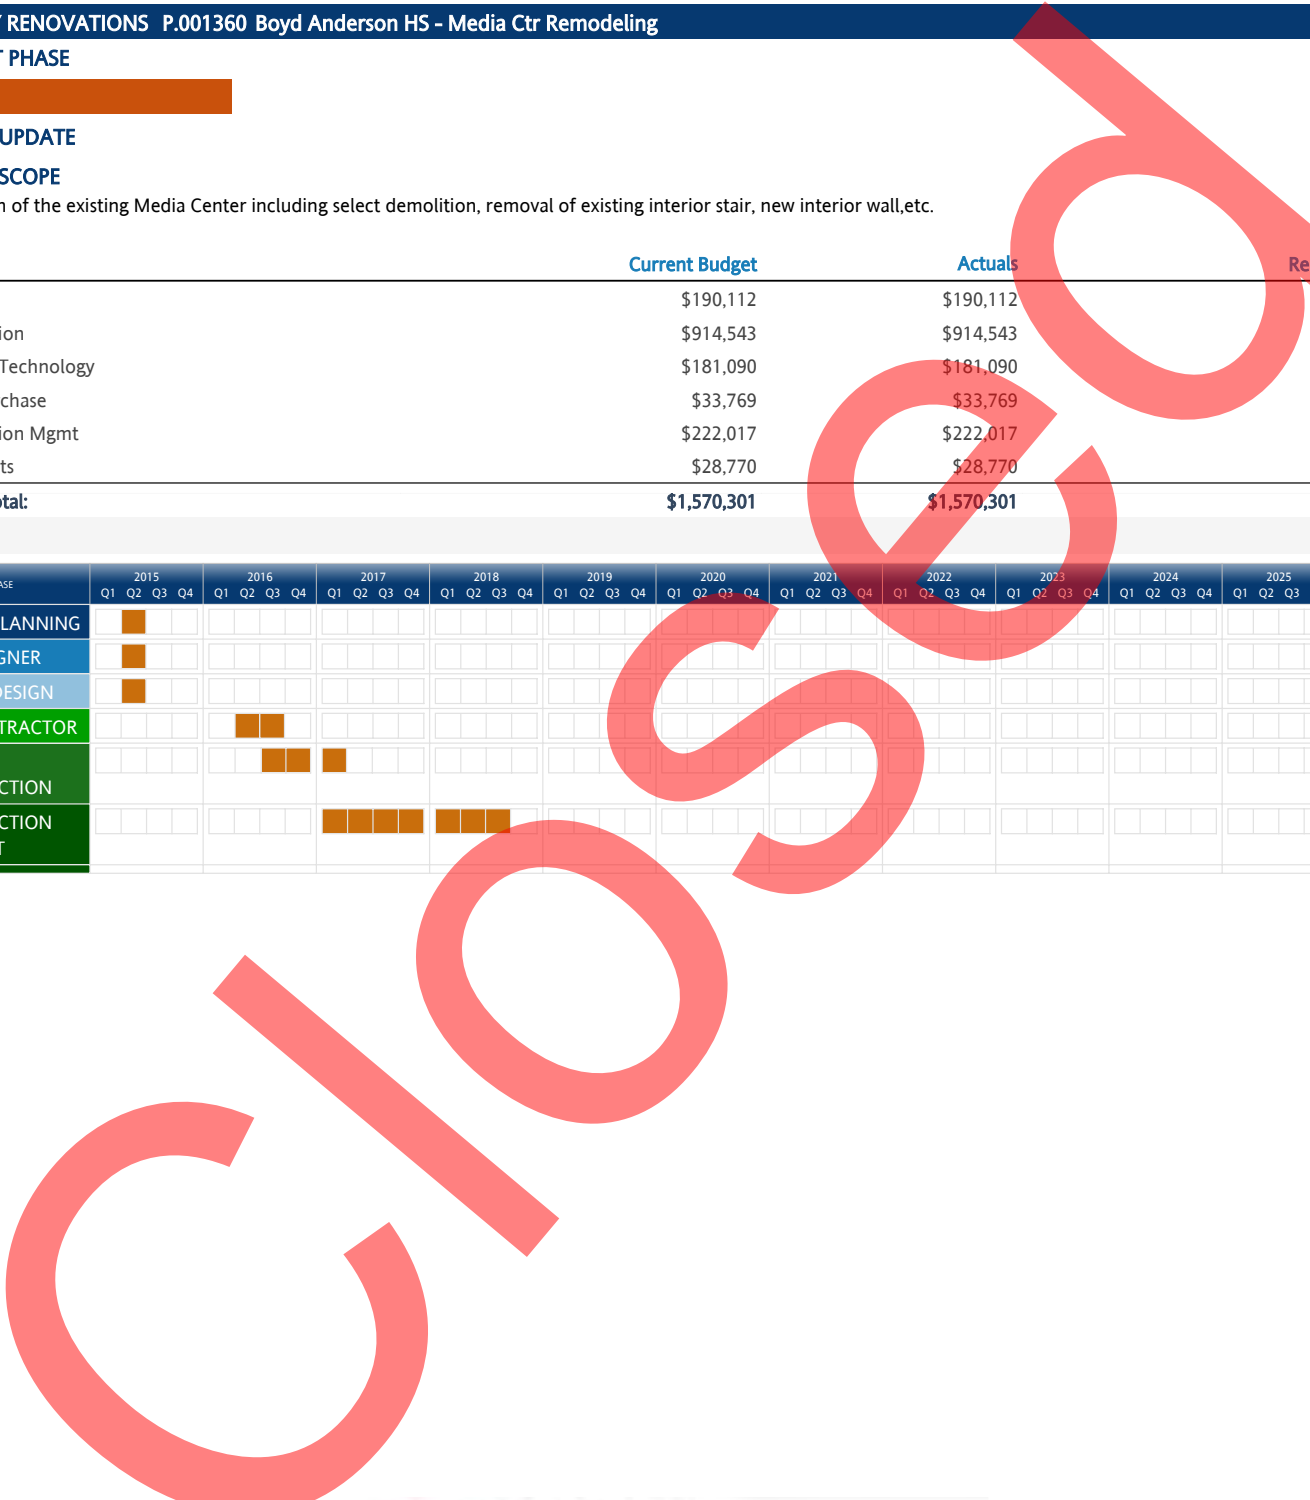

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



- HIGH:**
An issue that can impact the project's budget and/or schedule, a resolution is being determined.
- MEDIUM:**
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.
- LOW:**
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Boyd H. Anderson High School



Address: 3050 NW 41 STREET, LAUDERDALE LAKES 33309
 Location Num: 1741
 Board District: 5
 Board Member: Dr. Jeff Holness
 ADEFP Budget: \$12,820,525
 Total Facilities Budget (Sum of Projects): \$12,162,405

PRIMARY RENOVATIONS P.001846 Boyd H. Anderson HS - SMART Program Renovation

CURRENT PHASE

RISK LEVEL

5B-Construction



PROJECT UPDATE

This period the Contractor continued ongoing renovation work on Building No. 01, No. 02, 06, and Building No. 09 Work included Mechanical, Electrical, Plumbing Drainage Distribution, and Re-Reroofing scope. To-date the Contractor is currently 15 months beyond Contract Time for Substantial Completion. This period's Schedule Projections forecast the Project achieving Substantial Completion on or by March 3rd, 2024.

PROJECT SCOPE

Roofing: Buildings 1, 2, 3, 6, 8, 9, 10, 11, 12 & 13 ADA Restroom Renovations: Building 1: Rooms 102H, 102J, 106, and 166, and Building 2: Rooms 291 and 292 STEM Lab Renovations: Building 1: Business Technology Center (Rooms 223, 224, 225, and 227) and Aviation (Room 194) and Building 2: Health and Wellness (Room 2001 and 2002). 4) Safety and Security Upgrade: Exit Signs in - Buildings 1, 5, and 6

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$486,160	\$460,740	\$25,420
Construction	\$7,533,990	\$4,743,755	\$2,790,235
FF&E and Technology	\$196,177	\$191,382	\$4,795
Direct Purchase	\$1,313,146	\$454,622	\$858,524
Construction Mgmt	\$1,029,000	\$1,029,000	\$0
Consultants	\$33,631	\$25,270	\$8,361
Project Total:	\$10,592,104	\$6,904,769	\$3,687,335

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Recordex, Sound system for the Gymnasium, Laptop cart with 30 laptops, Portable sound system, Roof for visitor's dugout, lockers, Golf carts and Gym wall pads.

BUDGET

\$100,000

ATHLETICS

SCOPE

COMPLETE Weight Room

MUSIC

SCOPE

COMPLETE 284 Instruments Delivered

TECHNOLOGY

SCOPE

COMPLETE 580 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.
