

Coral Springs High School



Address: 7201 W SAMPLE ROAD, CORAL SPRINGS 33065
 Location Num: 1151
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$15,920,893
 Total Facilities Budget (Sum of Projects): \$14,927,900

PRIMARY RENOVATIONS P.001765 Coral Springs HS - SMART Program Renovations

CURRENT PHASE

5B-Construction

RISK LEVEL

No Risk

PROJECT UPDATE

1. Building 1 & 2- roof final inspection approved. 2. Home economics room 311- Floor tile installation completed final inspections pending. 4. Restrooms 630A and 630B asbestos abatement delayed work being scheduled for Spring break. 5. Main switchgear November 2023 delivery date. 6. Cooling tower, chiller and pump replacement to occur in summer of 2024.

PROJECT SCOPE

Provide additional Sprinkler heads in selected rooms of Building 1. RE-Roofing and related repairs to Buildings 1,2,4, and 10. Painting Exterior Walls on Buildings 2,4,10, and 11 Restroom renovations at 630a & 630b. Renovate STEM Labs and advanced Culinary Kitchen in Building 3. HVAC improvements and Chiller replacements Electrical improvements throughout.

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$1,005,157	\$989,391	\$15,766
Construction	\$9,887,272	\$8,228,397	\$1,658,875
FF&E and Technology	\$218,073	\$102,075	\$115,998
Direct Purchase	\$2,164,412	\$2,067,357	\$97,055
Construction Mgmt	\$1,611,278	\$1,611,278	\$0
Consultants	\$38,420	\$34,842	\$3,578
Misc Construction	\$3,288	\$3,288	\$0
Project Total:	\$14,927,900	\$13,036,628	\$1,891,272

FLAG: BUDGET, Reason: Budget Adjustment

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

ThinkPad's, earth walk carts, printers & projectors

BUDGET

\$100,000

ATHLETICS

SCOPE

COMPLETE Weight Room

MUSIC

COMPLETE SCOPE
88 Instruments Delivered

TECHNOLOGY

COMPLETE SCOPE
659 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Coral Springs Middle School



Address: 10300 W WILES ROAD, CORAL SPRINGS 33076
 Location Num: 2561
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$21,853,406
 Total Facilities Budget (Sum of Projects): \$19,426,965

PRIMARY RENOVATIONS P.001979 Coral Springs MS - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

5B-Construction



PROJECT UPDATE

Occupancy was granted in Areas 3-4 FSH 187, 187A, B, C, 190, 193, 194, 194A, B, C, D, E, 189, 189A, B, C. AHU 1-8 serving the gym is being replaced. New feeders were pulled for the new chiller.

PROJECT SCOPE

Re-roofing at Building 1. Re-painting at Buildings 1,3,4,5, and 6. HVAC Improvements- Component Replacement at Buildings 1,4 and 5. Media Center Improvements & ADA Restrooms Renovations at Building 1.

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$755,000	\$671,093	\$83,907
Construction	\$12,982,793	\$4,885,620	\$8,097,173
FF&E and Technology	\$66,000		\$66,000
Direct Purchase	\$3,007,106	\$2,142,315	\$864,791
Construction Mgmt	\$1,572,963	\$1,572,963	\$0
Contingency	\$988,694		\$988,694
Consultants	\$54,409	\$44,833	\$9,576
Project Total:	\$19,426,965	\$9,316,824	\$10,110,141

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Recordex, Student laptops, Adapters, carts, Aiphone, Golf cart, Digital marquee, Laptops, Adapters, Printers, Document Cameras

BUDGET

\$100,000

MUSIC

SCOPE

COMPLETE 33 Instruments Delivered

TECHNOLOGY

SCOPE

COMPLETE 597 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Coral Springs Pre-K - 8 (f.k.a. Coral Springs Elementary)



Address: 3601 NW 110 AVENUE, CORAL SPRINGS 33065
 Location Num: 2551
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$4,626,544
 Total Facilities Budget (Sum of Projects): \$6,468,320

PRIMARY RENOVATIONS P.001982 Coral Springs Pre K-8 – SMART Program Renovations

CURRENT PHASE

RISK LEVEL

5B-Construction



PROJECT UPDATE

- Ductwork: rooms 129-132, 137-140 in progress. - Media Center renovation: framing, electrical wiring/conduits, ductwork, carpet insulation was completed as scheduled for winter break. - Paint: Building 3 and 6 in progress. Building 4 and 78 completed.

PROJECT SCOPE

Building Envelope Improvements- Re-roofing at Buildings 2, 4 & 5. Building Envelope Improvements- Exterior painting at Building 1,3,4,6, & 78. HVAC Improvements at Buildings 1,3,6 & 85. Media Center Improvements at Building 1.

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$218,000	\$142,935	\$75,065
Construction	\$4,801,428	\$1,596,677	\$3,204,751
Direct Purchase	\$354,751	\$27,588	\$327,163
Construction Mgmt	\$555,000	\$555,000	\$0
Contingency	\$210,160		\$210,160
Consultants	\$10,000	\$6,986	\$3,014
Project Total:	\$6,149,339	\$2,329,186	\$3,820,153

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Coral Springs Pre-K - 8 (f.k.a. Coral Springs Elementary)



Address: 3601 NW 110 AVENUE, CORAL SPRINGS 33065
 Location Num: 2551
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$4,626,544
 Total Facilities Budget (Sum of Projects): \$6,468,320

PRIMARY RENOVATIONS P.001982-RC1 Coral Springs Pre K-8 - Roofing Building 2, 4, 5, 78 - SMART Program

CURRENT PHASE

RISK LEVEL

9-Closed

No Risk

PROJECT UPDATE

PROJECT SCOPE

Roofs carve-out, Bldgs. 2, 4, 5, 78 and their associated Mechanical Rooftop units.

BUDGET

	Current Budget	Actuals	Remaining Budget
Construction	\$318,981	\$318,981	\$0
Project Total:	\$318,981	\$318,981	\$0

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Color Poster Maker, Chairs, Promethean Boards, Poster Maker, Document Cameras, die Cut Machine, ThinkPads, Laptops, Office Furniture, iPads Mini

BUDGET

\$100,000

IN PROGRESS

Office Furniture

MUSIC

SCOPE

COMPLETE

667 Instruments Delivered

TECHNOLOGY

SCOPE

COMPLETE

194 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Country Hills Elementary School



Address: 10550 WESTVIEW DRIVE, CORAL SPRINGS 33076
 Location Num: 3111
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$6,508,219
 Total Facilities Budget (Sum of Projects): \$5,777,500

PRIMARY RENOVATIONS P.002063 Country Hills ES - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

5B-Construction



PROJECT UPDATE

1) Awaiting submittal for new Air Handler Unit #3. 2) Fan coil units building #5 rooms 509-510 will be completed and operational. FISH Rooms 506 & 507 FCU currently being replaced

PROJECT SCOPE

Building Envelope Improvements (Roof, Window, Ext Wall, etc.) Fire Sprinklers HVAC Improvements

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$407,000	\$323,282	\$83,718
Construction	\$3,822,559	\$3,556,175	\$266,384
Direct Purchase	\$694,815	\$631,078	\$63,737
Construction Mgmt	\$645,000	\$645,000	\$0
Contingency	\$189,040		\$189,040
Consultants	\$10,086	\$9,727	\$359
Utilities	\$9,000		\$9,000
Project Total:	\$5,777,500	\$5,165,262	\$612,238

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Motorola Two-way radios, Radio batteries, Tables, Aiphone, Window Wraps, Cafeteria Sound System Marquee, Projector

BUDGET

\$100,000

IN PROGRESS

MUSIC

✓ **SCOPE**

COMPLETE 208 Instruments Delivered

TECHNOLOGY

✓ **SCOPE**

COMPLETE 385 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Forest Glen Middle School



Address: 6501 TURTLE RUN BOULEVARD, CORAL SPRINGS 33067
 Location Num: 3051
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$9,790,800
 Total Facilities Budget (Sum of Projects): \$9,047,800

PRIMARY RENOVATIONS P.001865 Forest Glen MS - SMART Program Renovation

CURRENT PHASE

RISK LEVEL

5B-Construction



PROJECT UPDATE

Contractor remobilized and completed three air handlers. Test and Balance is on-going

PROJECT SCOPE

Campus-Wide HVAC Improvements, Electrical Improvements, Re-roofing, and Exterior Painting

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$425,000	\$358,646	\$66,354
Construction	\$5,760,362	\$5,740,388	\$19,974
Direct Purchase	\$1,581,417	\$1,581,417	\$0
Construction Mgmt	\$1,085,736	\$1,085,736	\$0
Contingency	\$185,885		\$185,885
Consultants	\$9,400		\$9,400
Project Total:	\$9,047,800	\$8,766,187	\$281,613

FLAG: SCHEDULE, Reason: Owner Delays / AE Delays

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Murals, computer lab furniture, TV Studio equipment, Library Remodeling & Gym bleachers

BUDGET

\$100,000

TECHNOLOGY

✓ COMPLETE

SCOPE

636 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Forest Hills Elementary School



Address: 3100 NW 85 AVENUE, CORAL SPRINGS 33065
 Location Num: 2631
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$4,544,826
 Total Facilities Budget (Sum of Projects): \$6,819,830

PRIMARY RENOVATIONS P.000827 Forest Hills ES - HVAC Upgrade/Rplcmnt

CURRENT PHASE

9-Closed

RISK LEVEL

No Risk

PROJECT UPDATE

PROJECT SCOPE


Replace existing air handling units with new equipment, etc.

BUDGET

	Current Budget	Actuals	Remaining Budget
Construction	\$809,063	\$809,063	\$0
Direct Purchase	\$115,300	\$115,300	\$0
Construction Mgmt	\$89,950	\$89,950	\$0
Consultants	\$6,216	\$6,216	\$0
Project Total:	\$1,020,529	\$1,020,529	\$0

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
HIRE DESIGNER	■	■	■	■	■	■	■	■	■																																							
ACTIVE CONSTRUCTION	■	■	■	■	■	■	■	■	■	■	■	■																																				

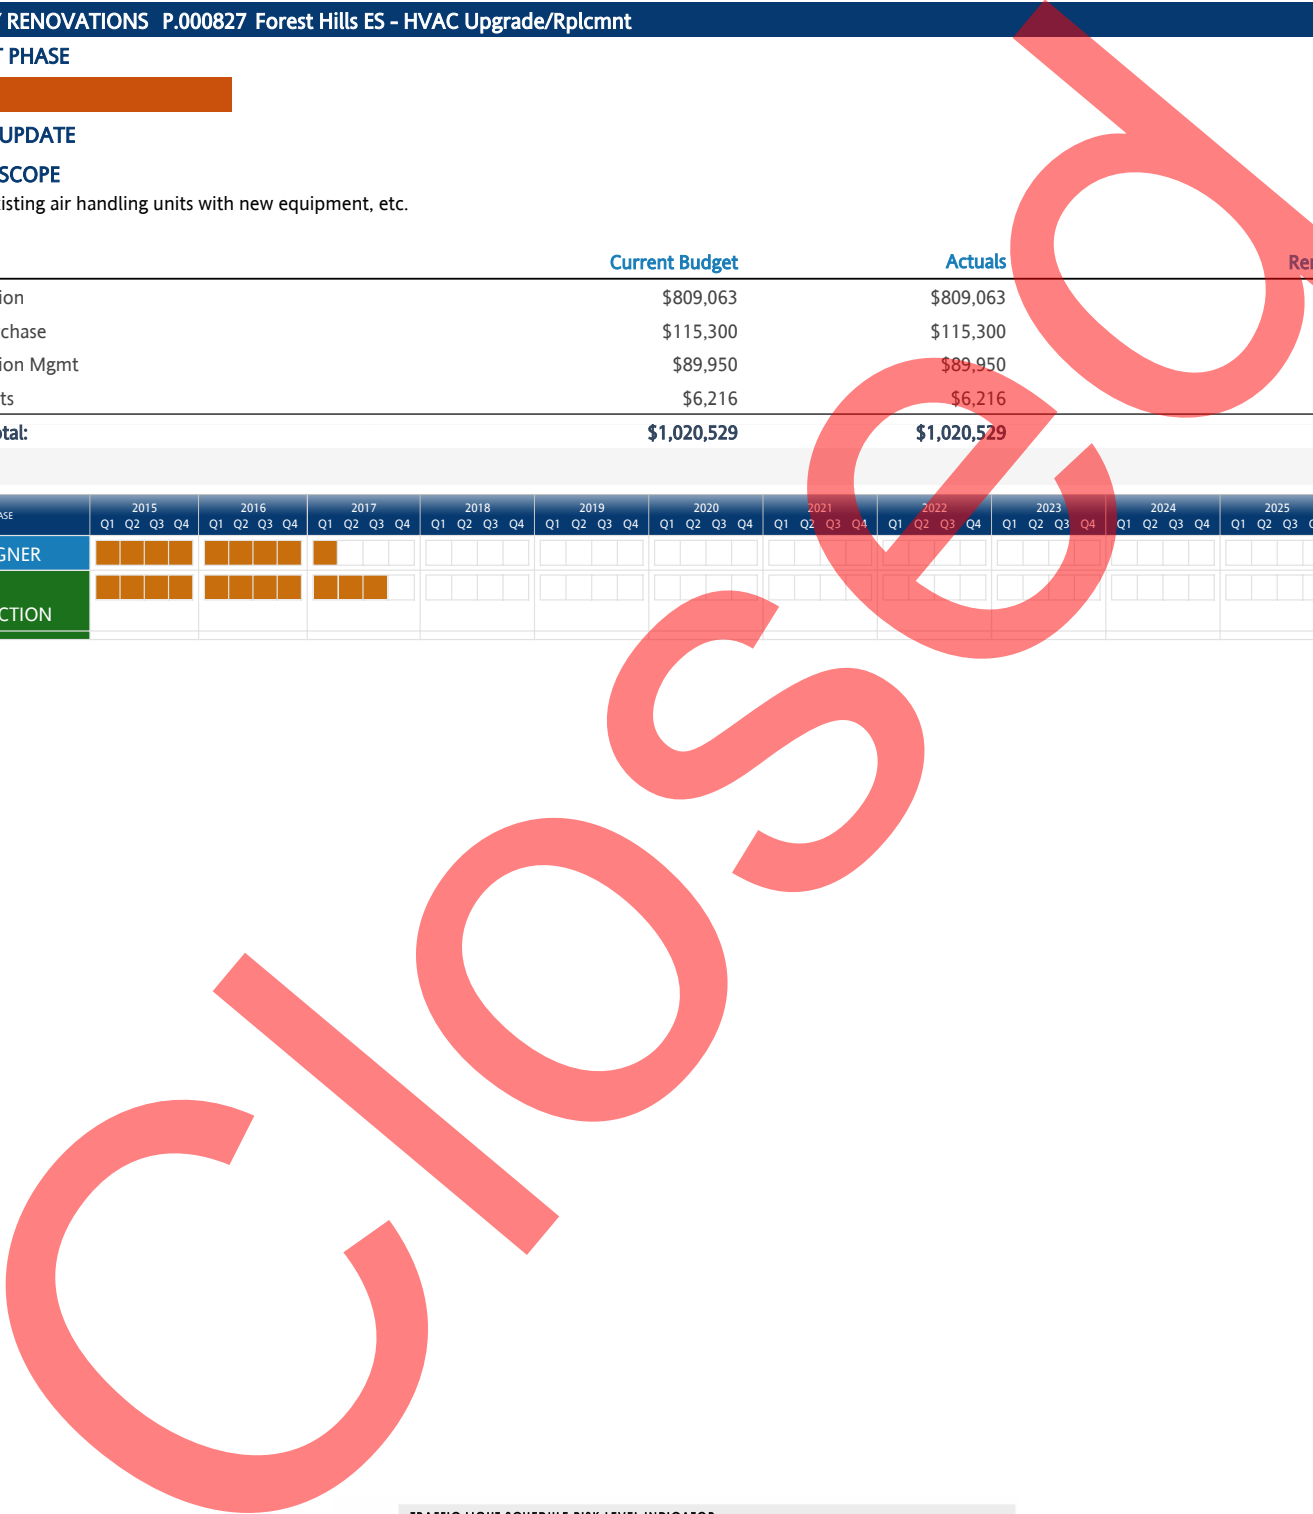

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

J.P. Taravella High School



Address: 10600 RIVERSIDE DRIVE, CORAL SPRINGS 33071
 Location Num: 2751
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$18,298,349
 Total Facilities Budget (Sum of Projects): \$15,699,000

PRIMARY RENOVATIONS P.001942 J.P. Taravella HS - SMART Program Renovations

CURRENT PHASE

5B-Construction

RISK LEVEL



PROJECT UPDATE

1. Room 525 Isimet system installation in progress 2. AHU1-4 duct heaters delivered coordinated installation for mid January.

PROJECT SCOPE

Fire Sprinklers Safety / Security Upgrade Window Replacement: Building 4 Re-roofing Buildings 1 and 7 HVAC and Electrical Improvements: Buildings 1, (25 Air Handling Units, 3 Window AC units, New DDC Controls, Test & Balance, and 25 Exit Signs), 2 (4 exhaust fans with new roof curbs and back draft dampers, 3 air handler units, and new DDC controls), 3 (3-circulating pumps, 6-new pumps, DDC controls, and 2-chillers and new chilled water piping), 4 (1 -AHU, new DDC controls, 1-exhaust fan, provide roof curb and back draft damper, and Test & Balance), 5 (3-AHU, remove existing air-cooled chiller and associated components, prep existing chilled water pipes, to remain, for a new connection to the chilled water system, and Test & Balance), 8 (new connection to the chilled water system, and Test & Balance) Media Center Improvements School Choice Enhancement STEM Lab Improvements: Building 1 (1st Floor Rooms 203 & 205, 312 & 312A and 2nd Floor Rooms 516, 525 & 526) Science Lab (Room 525): Demo all sinks and associated piping, provide new sinks with water & gas piping; provide acid waste piping to new lab sinks; and emergency eyewash shower (Building 10 - 1st Floor Rooms 1016 & 1018)

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$766,272	\$704,600	\$61,672
Construction	\$10,561,296	\$9,865,167	\$696,129
FF&E and Technology	\$268,230	\$213,871	\$54,359
Direct Purchase	\$1,711,835	\$1,711,835	\$0
Construction Mgmt	\$1,634,525	\$1,634,525	\$0
Contingency	\$666,842		\$666,842
Consultants	\$80,000	\$70,880	\$9,120
Utilities	\$10,000		\$10,000
Project Total:	\$15,699,000	\$14,200,878	\$1,498,122

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Technology, floor machine, facilities equipment, student desks, outdoor benches, cafeteria tables, door strikes, water bottle filling stations, Students' Laptops

BUDGET

\$100,000

ATHLETICS

SCOPE

COMPLETE Track,Weight Room

MUSIC

SCOPE

COMPLETE 125 Instruments delivered

TECHNOLOGY

SCOPE

COMPLETE 1,295 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



- HIGH:** An issue that can impact the project's budget and/or schedule, a resolution is being determined.
- MEDIUM:** An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.
- LOW:** A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

James S. Hunt Elementary School



Address: 7800 NW 35 COURT, CORAL SPRINGS 33065
 Location Num: 1971
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$9,737,258
 Total Facilities Budget (Sum of Projects): \$9,303,620

PRIMARY RENOVATIONS P.002059 James S. Hunt ES - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

5B-Construction



PROJECT UPDATE

Mechanical demolition work was successfully completed in Building #6; Installation of new ductwork and Air Handling Units has started. Fire alarm work continued.

PROJECT SCOPE

Re-roofing: Buildings 2, 5, 6 & 7. Exterior Painting: Building 1. Doors Replacement: Building 5, 6, & 7. Fire Sprinklers: Building 1. ADA Restrooms Improvements: Building 1. Fire Alarm System Replacement: Campus-wide. HVAC Improvements: Buildings 1, 5, 6, 7, and chiller yard.

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$425,000	\$358,511	\$66,489
Construction	\$6,603,423	\$5,893,115	\$710,308
FF&E and Technology	\$146,637	\$96,419	\$50,218
Direct Purchase	\$944,265	\$484,852	\$459,413
Construction Mgmt	\$701,000	\$701,000	\$0
Contingency	\$473,295		\$473,295
Consultants	\$10,000	\$5,751	\$4,249
Project Total:	\$9,303,620	\$7,539,648	\$1,763,972

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Document cameras, two-way radios with earpieces, projectors, power adaptors, student laptops, staff and admin laptops, laptop carts, laptop cart wiring & laptop carrying case, Printers, iPad Wi-Fi, Printers

BUDGET

\$100,000

IN PROGRESS

Earbuds

MUSIC

SCOPE

COMPLETE 435 Instruments delivered

TECHNOLOGY

SCOPE

COMPLETE 320 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Maplewood Elementary School



Address: 9850 RAMBLEWOOD DRIVE, CORAL SPRINGS 33071
 Location Num: 2741
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$5,418,347
 Total Facilities Budget (Sum of Projects): \$4,989,616

PRIMARY RENOVATIONS P.001639 Maplewood ES - SMART Building Renovations

CURRENT PHASE

RISK LEVEL

5B-Construction



PROJECT UPDATE

Fire Alarm scope of work is on-going but pending two change orders for additional fire alarm devices and Time Impact Analysis.

PROJECT SCOPE

ADA Restrooms Fire Sprinklers Improvements: Building 1 Roof Replacement: Building 1, 2, 4, 5, 6, & 80, Fire Alarm Improvements: Campus-wide.

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$413,914	\$408,017	\$5,897
Construction	\$3,485,277	\$3,374,763	\$110,514
FF&E and Technology	\$37,436	\$37,434	\$2
Direct Purchase	\$215,521	\$215,521	\$0
Construction Mgmt	\$452,067	\$452,067	\$0
Consultants	\$23,401	\$23,339	\$62
Project Total:	\$4,627,616	\$4,511,141	\$116,475

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Maplewood Elementary School



Address: 9850 RAMBLEWOOD DRIVE, CORAL SPRINGS 33071
 Location Num: 2741
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$5,418,347
 Total Facilities Budget (Sum of Projects): \$4,989,616

PRIMARY RENOVATIONS P.001998 Maplewood ES - SMART HVAC & Media Center

CURRENT PHASE

RISK LEVEL

6-Substantial Completion

No Risk

PROJECT UPDATE

The Change Order is in the General Contractor court pending negotiations with the District. If the Change Order is approved the request for the Certificate of Final Completion (Form 209) will be processed. A combined walkthrough occurred on December 21, 2023 December 2023. The request to start on the closeout documents was sent with the request for the demonstration and training recordings for the HVAC unit.

PROJECT SCOPE

HVAC Improvements Campus-wide with Test and Balance and Media Center Improvements in Building 1

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$51,000	\$32,881	\$18,119
Construction	\$199,791	\$198,023	\$1,768
FF&E and Technology	\$55,079	\$10,082	\$44,997
Construction Mgmt	\$46,875	\$46,875	\$0
Contingency	\$9,105		\$9,105
Consultants	\$150	\$128	\$22
Project Total:	\$362,000	\$287,989	\$74,011

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Stage sound system, projector & playground shade structure & PIP

BUDGET

\$100,000

IN PROGRESS

(2) Lenovo 500w Gen3; (2) Laptop delivery and Deployment

MUSIC

✓ **SCOPE**

COMPLETE 237 Instruments delivered

TECHNOLOGY

✓ **SCOPE**

COMPLETE 229 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Park Springs Elementary School



Address: 800 NW 66 TERRACE, CORAL SPRINGS 33067
 Location Num: 3171
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$10,344,499
 Total Facilities Budget (Sum of Projects): \$9,771,200

PRIMARY RENOVATIONS P.002062 Park Springs ES - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

5B-Construction



PROJECT UPDATE

Building 5: Four FCU's installation ongoing. Rm 504 (FCU 5-1), Rm 505 (FCU 5-2), Rm 506 (FCU 5-3), Rm 507 (FCU 5-4) Bldg(s) 4,5,6 Rough FA installation completed. Bldg 1 ongoing.
 Building 2: Art room paint, flooring, cabinetry/millwork, plumbing(new Art sink) - ongoing

PROJECT SCOPE

Re-roofing: Buildings 1, 2, 3, 4, 5, 6, 8, 9, & 10. Exterior Door Hardware Replacement: Buildings 1, 2, 3, 4, 5, 6, & 8. Fire Sprinklers: Building 2. HVAC System Replacement: Buildings 1, 2, 3, 4, 5, & 6. Replace exterior cooling tower. New DDC control system. Music Room and Art Lab Renovation: Building 2 New Foundation and Pad for Cooling Tower. Fire Alarm Voice Evacuation System Replacement: Campus-wide.

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$435,000	\$345,395	\$89,605
Construction	\$6,376,806	\$4,571,605	\$1,805,201
FF&E and Technology	\$41,905		\$41,905
Direct Purchase	\$1,555,864	\$1,548,550	\$7,314
Construction Mgmt	\$882,530	\$882,530	\$0
Contingency	\$458,095		\$458,095
Consultants	\$11,000	\$7,248	\$3,752
Utilities	\$10,000		\$10,000
Project Total:	\$9,771,200	\$7,355,328	\$2,415,872

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Floor scrubber, murals, laptop computers, K-2 playground upgrade, file cabinets, Office furniture

BUDGET

\$100,000

MUSIC

SCOPE

COMPLETE 408 Instruments Delivered

TECHNOLOGY

SCOPE

COMPLETE 462 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Parkside Elementary School



Address: 10257 NW 29 STREET, CORAL SPRINGS 33065
 Location Num: 3631
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$2,927,168
 Total Facilities Budget (Sum of Projects): \$2,505,175

PRIMARY RENOVATIONS P.002082 Parkside ES - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

6-Substantial Completion

No Risk

PROJECT UPDATE

The 110B Certificate of Completion was approved by the BD on 8/24/2023 and fully executed on 9/13/2023. This project has five pending PCO's, and once they are processed, a (209) Certificate of Final Inspection will be requested

PROJECT SCOPE

Reroofing: Buildings 1 & 2 Test and Balance: Buildings 1 & 3

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$114,000	\$91,134	\$22,866
Construction	\$1,571,163	\$1,228,758	\$342,405
Direct Purchase	\$446,004	\$345,559	\$100,445
Construction Mgmt	\$278,000	\$270,980	\$7,020
Contingency	\$90,008		\$90,008
Consultants	\$6,000	\$4,179	\$1,821
Project Total:	\$2,505,175	\$1,940,610	\$564,565

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Digital Marquee, Morning Show Equipment, Strike, & Access Card Reader at Microwaves the SPE, Indoor furniture, Student Laptops, Promethean Board, Computer Accessories, Cafeteria Tables, Classroom Furniture

BUDGET

\$100,000

IN PROGRESS

MUSIC

SCOPE

COMPLETE

137 Instruments Delivered

TECHNOLOGY

SCOPE

COMPLETE

236 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Ramblewood Elementary School



Address: 8950 SHADOW WOOD BOULEVARD, CORAL SPRINGS 33071
 Location Num: 2721
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$4,848,649
 Total Facilities Budget (Sum of Projects): \$4,740,130

PRIMARY RENOVATIONS P.001725 Ramblewood ES – SMART Program Renovations

CURRENT PHASE

RISK LEVEL

5B-Construction



PROJECT UPDATE

The surety is in coordination with the subs to complete the remaining scope and punch list items.

PROJECT SCOPE

Doors and Hardware: Buildings 1, 2, & 80 Electrical System Renovation: Buildings 1, 2, & 80 Exterior Windows: Buildings 1 & 2 Fire Sprinkler: Buildings 1, HVAC System Replacement: Buildings 1, 2, 3, 80, & 85 Interior Finishes & Improvements: Building 1, 2, & 80 Media Center Improvements: Re-roofing: Building 85 Roof Repairs: Building 3 Stucco Repairs: Building 3

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$374,889	\$380,006	(\$5,117)
Construction	\$3,703,732	\$3,315,336	\$388,396
FF&E and Technology	\$16,014	\$10,124	\$5,890
Direct Purchase	\$299,681	\$294,081	\$5,600
Construction Mgmt	\$329,086	\$329,086	\$0
Consultants	\$16,728	\$11,865	\$4,863
Project Total:	\$4,740,130	\$4,340,498	\$399,632

FLAG: BUDGET, Reason: Budget Adjustment

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Digital marquee, Playground upgrades, chairs, laptops, document cameras, projectors, USB 3.0 ethernet adapter, Lenovo 45W standard AC adapter

BUDGET

\$100,000

IN PROGRESS

MUSIC

SCOPE

COMPLETE 348 Instruments Delivered

TECHNOLOGY

SCOPE

COMPLETE 282 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Ramblewood Middle School



Address: 8505 W ATLANTIC BOULEVARD, CORAL SPRINGS 33071
 Location Num: 2711
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$5,026,860
 Total Facilities Budget (Sum of Projects): \$6,878,242

PRIMARY RENOVATIONS P.001867 Ramblewood MS - SMART Program Renovation

CURRENT PHASE

RISK LEVEL

5B-Construction



PROJECT UPDATE

Roof Electrical Inspections are 95% complete, Pending Electrical Panel Schedules from Electrical Sub-contractor. Emergency Generator Electrical Final Inspection was passed, Now Pending start-up. Bollard installation is pending around the generator enclosure. Restroom 117/118 Punch list items completion is in progress. Restroom 106/107 Wall Tile Installation is 100% Complete.

PROJECT SCOPE

ADA Restroom, Renovations: Building 1 Rooms 117/118 and 106/107. Electrical Panel, Switch Gear and Transformer Replacement: Building 1 Emergency Generator Replacement: Building 1 Existing Fire Alarm Recertification: Campus-wide Exterior Lighting Replacement Media Center Renovation: Building 1 Reroofing: Building 1 Test & Balance: Building 1

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$350,000	\$298,749	\$51,251
Construction	\$4,432,825	\$4,183,209	\$249,616
FF&E and Technology	\$48,545	\$48,254	\$291
Direct Purchase	\$854,994	\$854,994	\$0
Construction Mgmt	\$756,606	\$756,606	\$0
Contingency	\$415,272		\$415,272
Consultants	\$20,000	\$12,856	\$7,144
Project Total:	\$6,878,242	\$6,154,668	\$723,574

FLAG: SCHEDULE, Reason: Unforeseen Condition/ Errors and Omissions

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Printers, TVs for the cafeteria, Projector for the cafeteria sound system, cafeteria sound, LCD projectors, 3D Printer, digital marquee, SPE Signage

BUDGET

\$100,000

MUSIC

SCOPE

COMPLETE 34 Instruments Delivered

TECHNOLOGY

SCOPE

COMPLETE 443 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Riverside Elementary School



Address: 11450 RIVERSIDE DRIVE, CORAL SPRINGS 33071
 Location Num: 3031
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$2,740,499
 Total Facilities Budget (Sum of Projects): \$2,224,500

PRIMARY RENOVATIONS P.002039 Riverside ES - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

5B-Construction



PROJECT UPDATE

Fire alarm certification in progress.

PROJECT SCOPE

Re-roofing: Buildings 11, & 85. Fire Alarm System Replacement: Campus-wide. Fire Sprinklers: Building 4 HVAC Improvements- Component Replacement: Buildings at 11, & 85. HVAC Improvements- Test and Balance: Buildings 1 through 10. Media Center Improvements & ADA Restroom Improvements: Building 3.

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$215,990	\$147,022	\$68,968
Construction	\$1,581,410	\$1,447,011	\$134,399
FF&E and Technology	\$57,440	\$40,240	\$17,200
Direct Purchase	\$61,850	\$61,850	\$0
Construction Mgmt	\$231,260	\$231,260	\$0
Contingency	\$63,550		\$63,550
Consultants	\$10,000	\$7,975	\$2,025
Utilities	\$3,000		\$3,000
Project Total:	\$2,224,500	\$1,935,358	\$289,142

FLAG:

PHASE	2015			2016			2017			2018			2019			2020			2021			2022			2023			2024			2025			2026		
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
PROJECT PLANNING																																				
HIRE DESIGNER																																				
PROJECT DESIGN																																				
HIRE CONTRACTOR																																				
ACTIVE CONSTRUCTION																																				
CONSTRUCTION CLOSEOUT																																				

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Multi drying steel rack, Art & PE Enhancements (racks, furniture, book drop carts, etc.), outdoor PA speaker system upgrade, Ukulele Storage racks & tables, Basketball Court, Computer Accessories, Chairs, Laptops & Accessories

BUDGET

\$100,000

MUSIC

SCOPE

COMPLETE 217 Instruments Delivered

TECHNOLOGY

SCOPE

COMPLETE 214 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Sawgrass Springs Middle School



Address: 12500 W SAMPLE ROAD, CORAL SPRINGS 33065
 Location Num: 3431
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$6,984,970
 Total Facilities Budget (Sum of Projects): \$13,484,640

PRIMARY RENOVATIONS P.001841 Sawgrass Springs MS - SMART Program Renovation

CURRENT PHASE

RISK LEVEL

5B-Construction



PROJECT UPDATE

(1) Installation of Fire Alarm Conduits Throughout Buildings #1, #2, #3, #4 & #5 including wiring and inspections. In Progress with conduit install and wiring is 75% complete. Currently Coordinating With Bass United For Antenna Locations & TKE For Elevator Access. An FM-Workorder has been generated to assist the GC with the elevator shaft access. (2) TKE via PPO in coordination with the GC has coordinated the above work of having access to the elevator shaft for F/A for Jan 20 thru the 22 of 2024 so GC can complete their F/A scope in this area. (3) Air Handler Units 5-2 & AHU 3-4 will be replaced. (4) Fire Alarm Work In Progress Throughout- 55% (5) Electrical Work In Progress Throughout - 75%

PROJECT SCOPE

Building Envelope Improvement- Roof replacement at Buildings 1, 2, 3, 4, 5, 6, & 7. Building Envelope Improvement- Exterior painting at Buildings 1, 2, 3, 4, 5, & 6. Building Envelope Improvement- Windows replacement at Buildings 2, 3, 4 & 5. Building Envelope Improvements- Cleaning the Aluminum covered walkways. HVAC Improvements- Equipment and controls in Buildings 1 to 6 and 9. Test & Balance in Buildings 1-6 and 9. Fire Sprinklers in Buildings 4. Fire Alarm System Replacement Throughout the Campus. NTP: 8/31/2022
 Substantial Completion: 2/9/2022

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$459,495	\$393,322	\$66,173
Construction	\$9,793,774	\$8,803,034	\$990,740
FF&E and Technology	\$6,200	\$1,924	\$4,276
Direct Purchase	\$1,562,683	\$1,262,961	\$299,722
Construction Mgmt	\$1,071,600	\$1,071,600	\$0
Contingency	\$544,888		\$544,888
Consultants	\$35,000	\$11,459	\$23,541
Utilities	\$11,000		\$11,000
Project Total:	\$13,484,640	\$11,544,300	\$1,940,340

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Laptops & TV production sound system

BUDGET

\$100,000

IN PROGRESS

MUSIC

✓ **SCOPE**

COMPLETE 135 Instruments Delivered

TECHNOLOGY

✓ **SCOPE**

COMPLETE 433 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Westchester Elementary School



Address: 12405 ROYAL PALM BOULEVARD, CORAL SPRINGS 33065
 Location Num: 2681
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$3,527,931
 Total Facilities Budget (Sum of Projects): \$3,101,398

PRIMARY RENOVATIONS P.001823 Westchester ES - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

5B-Construction



PROJECT UPDATE

Fire Alarm rough and device installation is on-going.

PROJECT SCOPE

Campus-Wide Fire Alarm Replacement Fire Sprinkler Upgrades and Supply to Building 1 Entire Building, Electrical panel replacements in Building 1 Re-Roofing of Building 3, 8, and Portables 85 & 86 Civil Improvements for roof drainage of Building 1 Media Center Renovation including ADA Restroom Improvements.

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$315,217	\$294,350	\$20,867
Construction	\$2,476,592	\$2,318,437	\$158,155
FF&E and Technology	\$38,385	\$35,745	\$2,640
Direct Purchase	\$32,808	\$32,808	\$0
Construction Mgmt	\$235,872	\$217,089	\$18,783
Consultants	\$2,524	\$2,311	\$213
Project Total:	\$3,101,398	\$2,900,740	\$200,658

FLAG: BUDGET, Reason: Budget Adjustment SCHEDULE, Reason: Owner Delays / Errors and Omissions / Contractor Delays

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Digital marquee, access control card reader system, Aiphone at the SPE and Strike, computer lab conversion, Laptop

BUDGET

\$100,000

MUSIC

✓ **SCOPE**

COMPLETE 105 Instruments Delivered

TECHNOLOGY

✓ **SCOPE**

COMPLETE 309 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Westglades Middle School



Address: 11000 HOLMBERG ROAD, PARKLAND 33076
 Location Num: 3871
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$6,281,232
 Total Facilities Budget (Sum of Projects): \$4,407,040

PRIMARY RENOVATIONS P.002131 Westglades MS - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

5B-Construction

No Risk

PROJECT UPDATE

1. All roof inspections finals obtained. 2. Punch list items in progress.

PROJECT SCOPE

Scope of Work: 1) HVAC: Building 1, 2, 3, & 4 2) Roof: Building 1, 2, 3, & 4 3) Building Envelope Improvements include wall cracks and stucco repair. 4) Structural steel column replacement 5) Louvers at Building 3

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$272,000	\$201,348	\$70,652
Construction	\$3,129,911	\$3,047,021	\$82,890
Direct Purchase	\$317,364		\$317,364
Construction Mgmt	\$485,000	\$485,000	\$0
Contingency	\$194,765		\$194,765
Consultants	\$8,000	\$1,418	\$6,582
Project Total:	\$4,407,040	\$3,734,787	\$672,253

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

BUDGET

COMPLETE

\$100,000

DELIVERED

Classroom Projectors, student laptops, carts, administrative laptops, teacher laptops & cart wiring

MUSIC

✓ COMPLETE **SCOPE**

56 Instruments Delivered

TECHNOLOGY

✓ COMPLETE **SCOPE**

758 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.
