

Gulfstream Academy of Hallandale Beach K-8 (f.k.a. Hallandale Elementary)



Address: 900 SW 8TH STREET, HALLANDALE 33009
 Location Num: 0131
 Board District: 1
 Board Member: Daniel P. Foganholi
 ADEFP Budget: \$2,788,977
 Total Facilities Budget (Sum of Projects): \$2,586,361

PRIMARY RENOVATIONS P.001616 Gulfstream Academy of Hallandale Beach K-8 - Roof Replace 9 & 13

CURRENT PHASE

9-Closed

RISK LEVEL

No Risk

PROJECT UPDATE

PROJECT SCOPE


Re-Roof Buildings #13 & 14

BUDGET

	Current Budget	Actuals	Remaining Budget
Construction	\$339,858	\$339,858	\$0
Construction Mgmt	\$11,682	\$11,682	\$0
Project Total:	\$351,540	\$351,540	\$0

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
ACTIVE																																																
CONSTRUCTION																																																

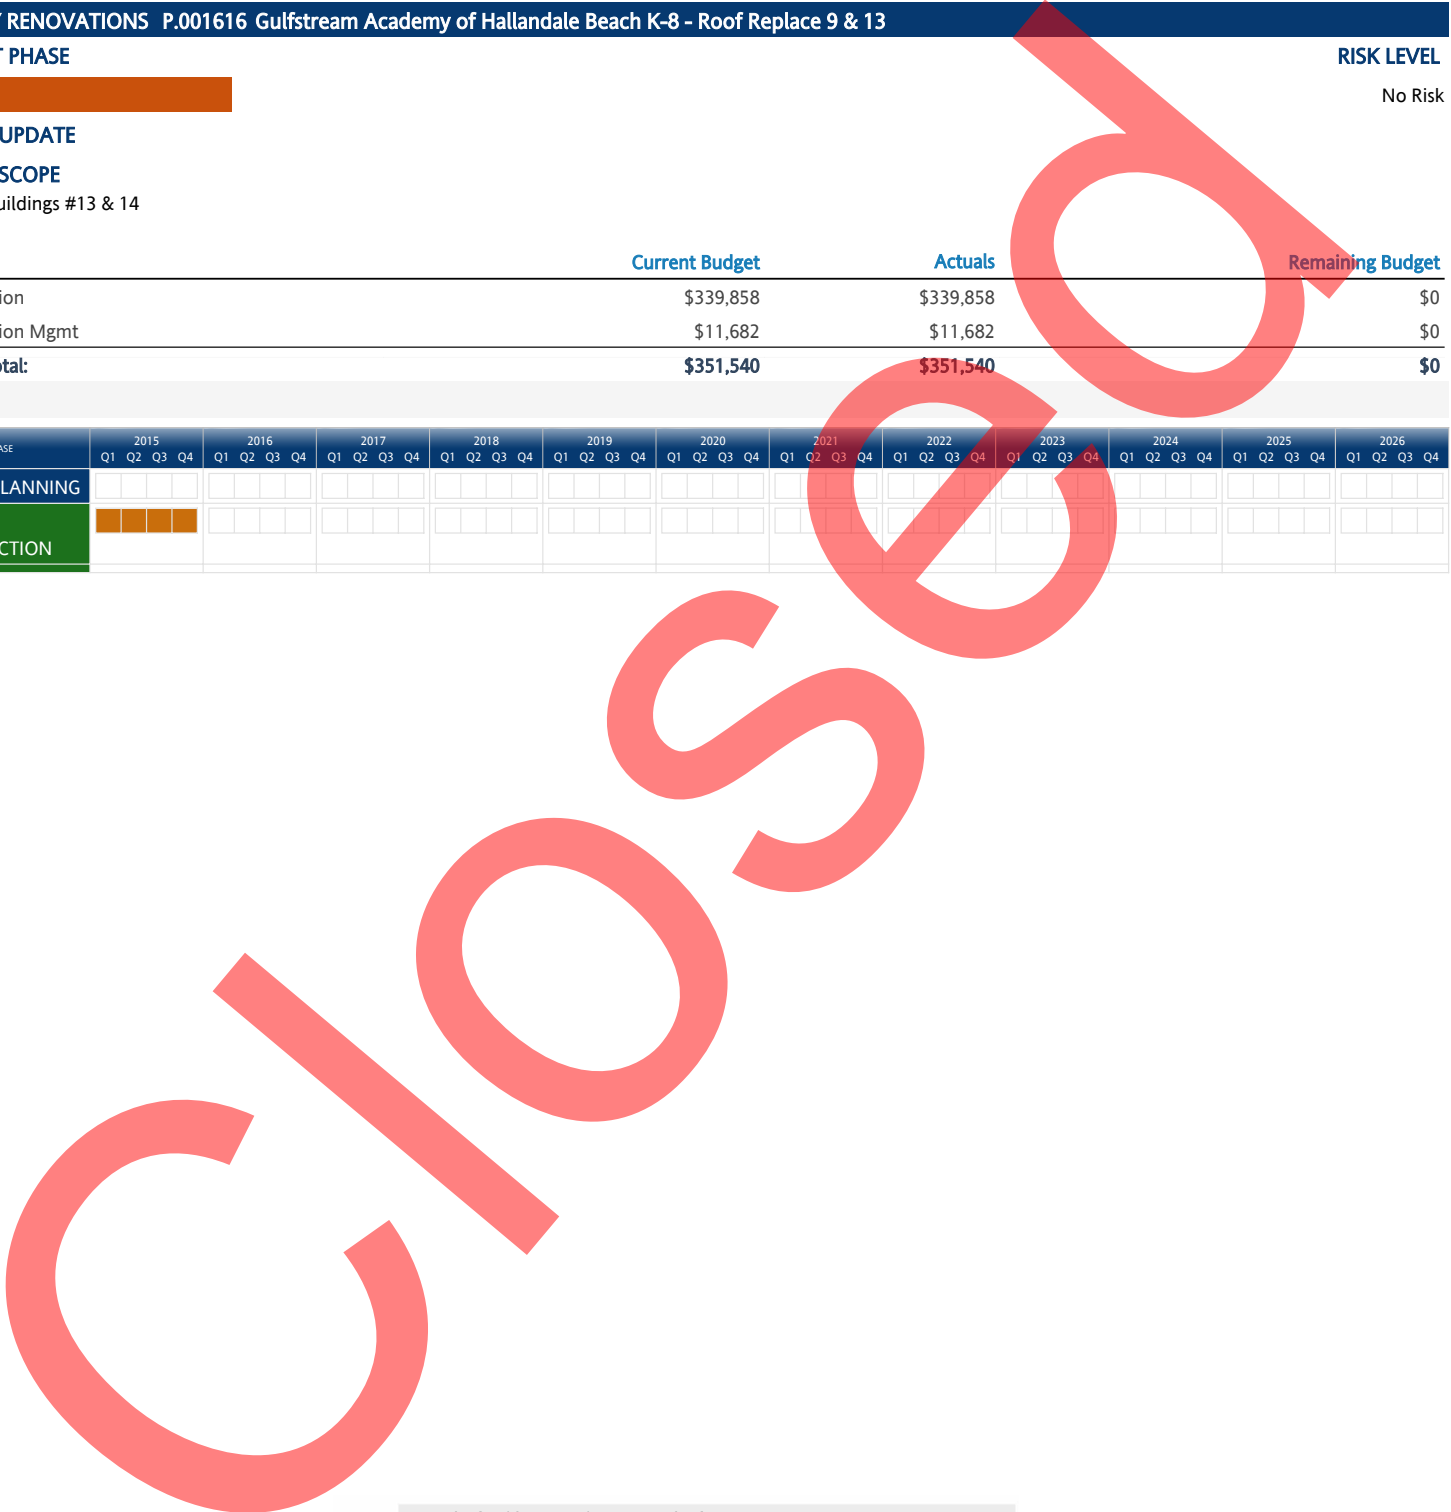

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



- HIGH:**
An issue that can impact the project's budget and/or schedule, a resolution is being determined.
- MEDIUM:**
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.
- LOW:**
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Gulfstream Academy of Hallandale Beach K-8 (f.k.a. Hallandale Elementary)



Address: 900 SW 8TH STREET, HALLANDALE 33009
 Location Num: 0131
 Board District: 1
 Board Member: Daniel P. Foganholi
 ADEFP Budget: \$2,788,977
 Total Facilities Budget (Sum of Projects): \$2,586,361

PRIMARY RENOVATIONS P.002072 Gulfstream Academy of Hallandale Beach K-8 (South) - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

6-Substantial Completion

No Risk

PROJECT UPDATE

The closeout purchase order approval was submitted to the General Contractor to financially close out this process. The change order is still pending in the GC's court as a revision and resubmit. Once the change order is complete, we will request the Certificate of Final Inspection, form 209.

PROJECT SCOPE

Exterior Stucco Repair: Building 1 HVAC improvements: Buildings 1, 2 & 3 Reroofing: Buildings 1 & 3

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$137,000	\$101,811	\$35,189
Construction	\$1,579,400	\$1,212,677	\$366,723
Direct Purchase	\$185,269	\$179,535	\$5,734
Construction Mgmt	\$250,180	\$237,730	\$12,450
Contingency	\$64,472	\$64,472	\$0
Consultants	\$18,500	\$18,076	\$424
Project Total:	\$2,234,821	\$1,749,829	\$484,992

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.
