

Gulfstream Academy of Hallandale Beach K-8 (f.k.a. Hallandale Elementary)



Address: 900 SW 8TH STREET, HALLANDALE 33009
 Location Num: 0131
 Board District: 1
 Board Member: Daniel P. Foganholi
 ADEFP Budget: \$2,788,977
 Total Facilities Budget (Sum of Projects): \$2,586,361

PRIMARY RENOVATIONS P.001616 Gulfstream Academy of Hallandale Beach K-8 - Roof Replace 9 & 13

CURRENT PHASE

9-Closed

RISK LEVEL

No Risk

PROJECT UPDATE

PROJECT SCOPE


Re-Roof Buildings #13 & 14

BUDGET

	Current Budget	Actuals	Remaining Budget
Construction	\$339,858	\$339,858	\$0
Construction Mgmt	\$11,682	\$11,682	\$0
Project Total:	\$351,540	\$351,540	\$0

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
ACTIVE																																																
CONSTRUCTION																																																

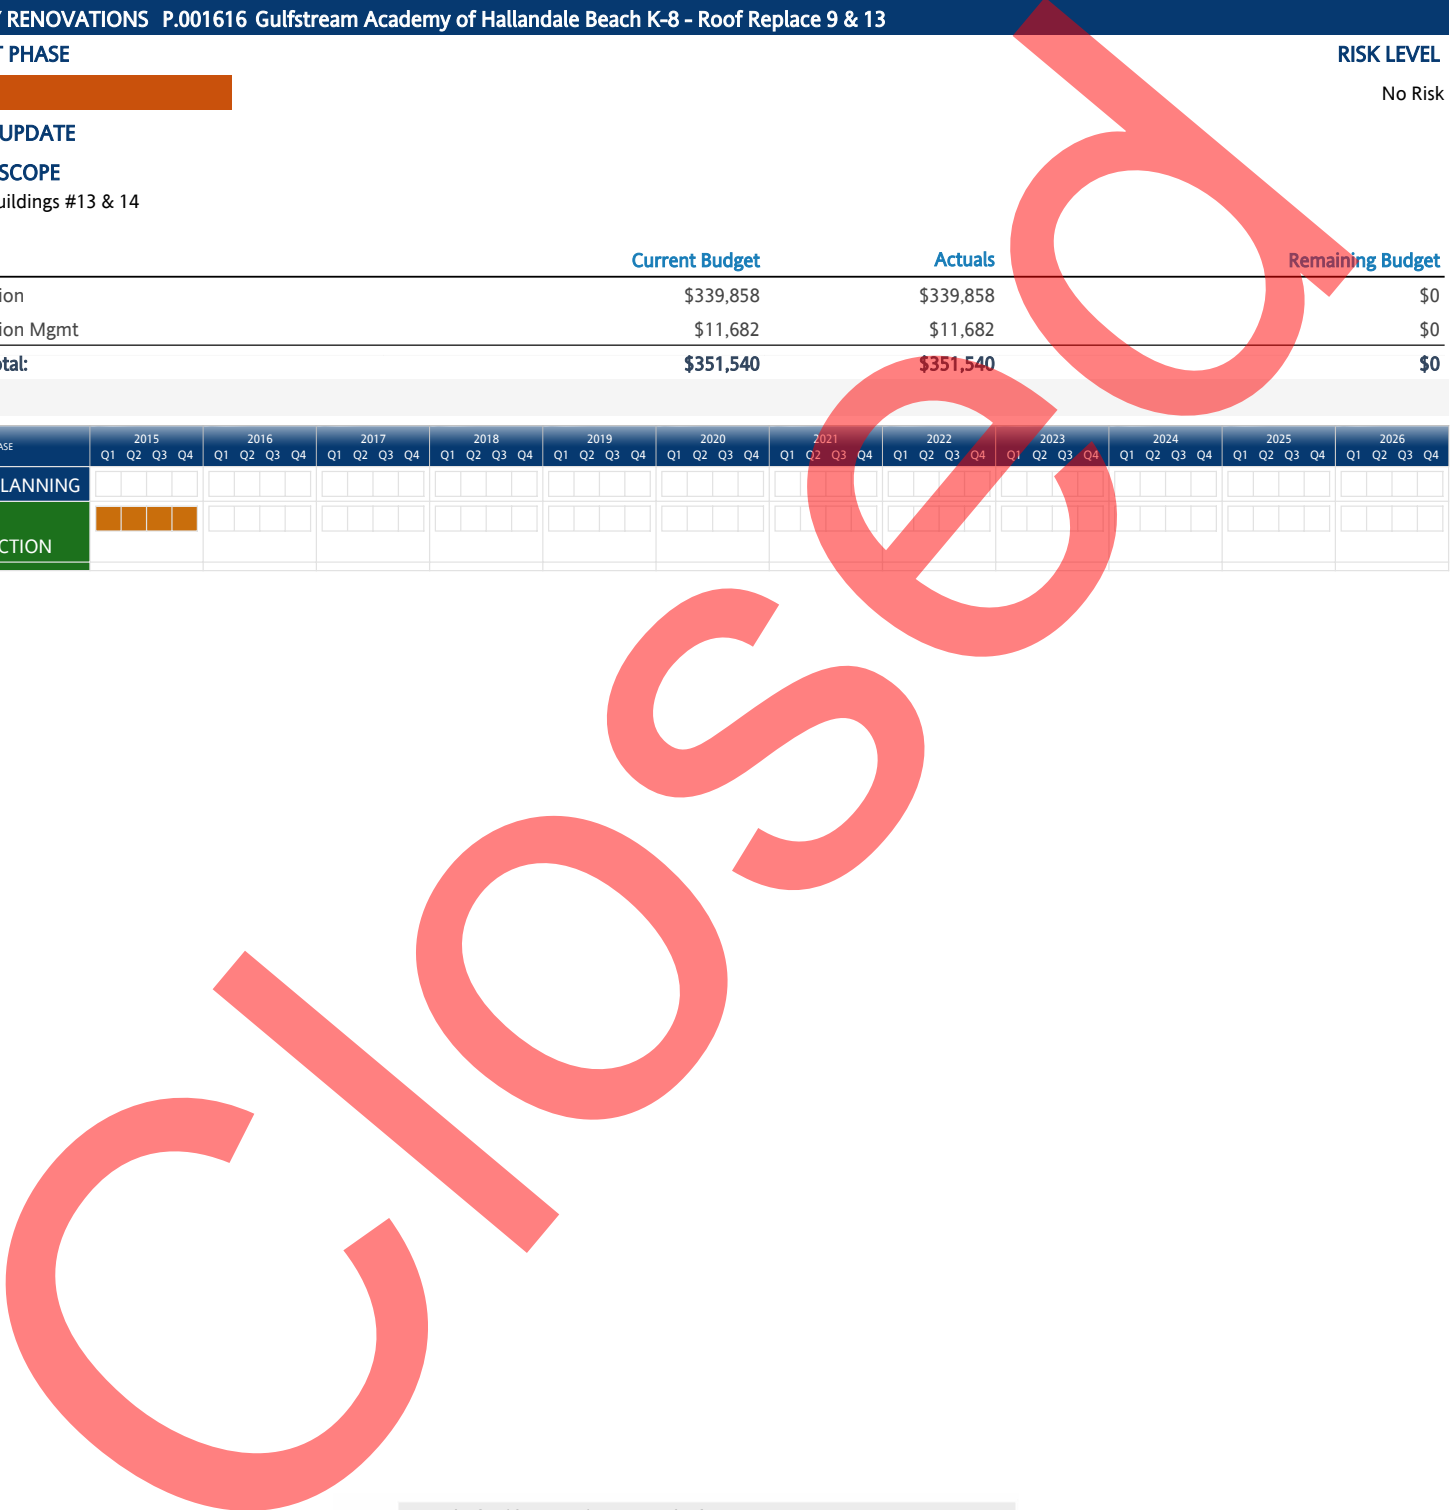

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



- HIGH:**
An issue that can impact the project's budget and/or schedule, a resolution is being determined.
- MEDIUM:**
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.
- LOW:**
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Gulfstream Academy of Hallandale Beach K-8 (f.k.a. Hallandale Elementary)



Address: 900 SW 8TH STREET, HALLANDALE 33009
 Location Num: 0131
 Board District: 1
 Board Member: Daniel P. Foganholi
 ADEFP Budget: \$2,788,977
 Total Facilities Budget (Sum of Projects): \$2,586,361

PRIMARY RENOVATIONS P.002072 Gulfstream Academy of Hallandale Beach K-8 (South) - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

6-Substantial Completion

No Risk

PROJECT UPDATE

The closeout purchase order approval was submitted to the General Contractor to financially close out this process. The change order is still pending in the GC's court as a revision and resubmit. Once the change order is complete, we will request the Certificate of Final Inspection, form 209.

PROJECT SCOPE

Exterior Stucco Repair: Building 1 HVAC improvements: Buildings 1, 2 & 3 Reroofing: Buildings 1 & 3

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$137,000	\$101,811	\$35,189
Construction	\$1,579,400	\$1,212,677	\$366,723
Direct Purchase	\$185,269	\$179,535	\$5,734
Construction Mgmt	\$250,180	\$237,730	\$12,450
Contingency	\$64,472		\$64,472
Consultants	\$18,500	\$18,076	\$424
Project Total:	\$2,234,821	\$1,749,829	\$484,992

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



- HIGH:**
An issue that can impact the project's budget and/or schedule, a resolution is being determined.
- MEDIUM:**
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.
- LOW:**
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Gulfstream Early Learning Center of Excellence (f.k.a. Gulfstream Middle School)



Address: 120 SW 4 AVENUE, HALLANDALE 33009
 Location Num: 3931
 Board District: 1
 Board Member: Daniel P. Foganholi
 ADEFP Budget: \$6,713,492
 Total Facilities Budget (Sum of Projects): \$6,397,696

PRIMARY RENOVATIONS P.002055 Gulfstream Early Learning Center - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

6-Substantial Completion

No Risk

PROJECT UPDATE

The project received 110b on October 6, 2023. The 110b was fully executed on 10/30/2023. The GC is working on final punch list items.

PROJECT SCOPE

HVAC Improvements: Buildings 1-5,7-9, 11-13 New Fire Alarm System: Campus-wide Re-roofing: Buildings 1-5,7-9, 11-13, 85 Restrooms Renovations: Building 4 Window Improvement: Building 85 Bathroom Renovation: Building 9 (School Choice Project)

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$300,000	\$183,053	\$116,947
Construction	\$4,944,969	\$4,792,472	\$152,497
FF&E and Technology	\$10,908	\$10,908	\$0
Direct Purchase	\$443,819	\$441,758	\$2,061
Construction Mgmt	\$648,000	\$648,000	\$0
Consultants	\$50,000	\$26,945	\$23,055
Project Total:	\$6,397,696	\$6,103,136	\$294,560

FLAG: BUDGET, Reason: Budget Adjustment

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Gators, Outdoor picnic benches, Two-way radios, Bathroom renovations

BUDGET

\$100,000

TECHNOLOGY

SCOPE

83 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Hallandale Magnet High School (f.k.a. Hallandale High School)



Address: 720 NW 9 AVENUE, HALLANDALE 33009
 Location Num: 0403
 Board District: 1
 Board Member: Daniel P. Foganholi
 ADEFP Budget: \$9,127,438
 Total Facilities Budget (Sum of Projects): \$8,013,731

PRIMARY RENOVATIONS P.002115 Hallandale Magnet HS - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

5B-Construction



PROJECT UPDATE

Building 01 Level 01 & 02 Fire Protection installation is 100% complete, pending final trim installation. Fire protection FDC was installed, Inspection were Passed. Building 01 level 01 Fire Alarm Device Installation is in Progress 50% Complete. Building 01 level 02 Fire Alarm Rough and Box is 100% complete, Wire Installation is 100% complete. Exterior Light pole and fixture replacement is complete, Rewiring per approved Change Order is 25% Complete, final inspection is Pending. Restroom 903A/903B Renovations are 100% completed, Substantial Completion Inspection is pending. Restroom 300/302 Renovations are 100% completed, Substantial Completion Inspection is pending. Restroom 626/627 Demolition was started and is 50% Complete. Fume Hood Installations are complete, pending final inspections.

PROJECT SCOPE

Scope of work consist of the following: Fire Alarm Replacement: Campus wide Canopy Lighting Replacement: Buildings 1 & 2 Electrical Transformer Replacement: Buildings 1 & 2 Mounted Building Lighting Replacement: Buildings 1, 2, 3, 5, & 6 Pole Light Replacement: Building 1 HVAC Renovations in Buildings 1, 2 & 3 Electrical Renovations: Building 1, 2, 3 & 4 Fire Sprinkler Installation: Building 1 Media Center Renovation: Building 1 Restroom Renovations: Buildings 1 & 2 Stem Lab Renovations: Buildings 1 & 2 Chemistry Fume Hood Replacement: Building 1 Exterior Door Repair: Buildings 4 & 6 Exterior Painting: Building 4 Aluminum Window Replacement: Building 4 Air Terminal Replacement: Building 2 Architectural Life Safety Upgrades: Building 1. 2nd Floor, Science Department Area

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$530,600	\$409,931	\$120,669
Construction	\$5,573,657	\$4,451,741	\$1,121,916
FF&E and Technology	\$221,416	\$59,862	\$161,554
Direct Purchase	\$539,434	\$431,072	\$108,362
Construction Mgmt	\$882,000	\$882,000	\$0
Contingency	\$221,624		\$221,624
Consultants	\$30,000	\$18,952	\$11,048
Utilities	\$15,000		\$15,000
Project Total:	\$8,013,731	\$6,253,558	\$1,760,173

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Gym floor covering, smart TV's prometean bundle, ActivPanels, golf cart, jazz band instruments, Basketball gym scoreboards, Lenovo ThinkPads

BUDGET

\$100,000

ATHLETICS

SCOPE

Track,Weight Room

MUSIC

SCOPE

272 Instruments delivered

TECHNOLOGY

SCOPE

569 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.
