

Annabel C. Perry Pre K - 8 (f.k.a. Annabel C. Perry Elementary)



Address: 6850 SW 34 STREET, MIRAMAR 33023
 Location Num: 1631
 Board District: 1
 Board Member: Daniel P. Foganholi
 ADEFP Budget: \$6,069,166
 Total Facilities Budget (Sum of Projects): \$5,597,431

CURRENT PHASE

9-Closed

RISK LEVEL

No Risk

PROJECT UPDATE

PROJECT SCOPE

Roofing Replacement HVAC Upgrades Electrical Switchgear Replacement Fire Alarm Replacement

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$175,882	\$175,882	\$0
Construction	\$4,228,226	\$4,228,226	\$0
FF&E and Technology	\$12,667	\$12,667	\$0
Construction Mgmt	\$488,602	\$488,602	\$0
Consultants	\$11,554	\$11,554	\$0
Project Total:	\$4,916,931	\$4,916,931	\$0

FLAG:

PHASE	2015			2016			2017			2018			2019			2020			2021			2022			2023			2024			2025			2026		
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
PROJECT PLANNING																																				
HIRE DESIGNER																																				
PROJECT DESIGN																																				
HIRE CONTRACTOR																																				
ACTIVE CONSTRUCTION																																				
CONSTRUCTION CLOSEOUT																																				

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Annabel C. Perry Pre K - 8 (f.k.a. Annabel C. Perry Elementary)



Address: 6850 SW 34 STREET, MIRAMAR 33023
 Location Num: 1631
 Board District: 1
 Board Member: Daniel P. Foganholi
 ADEFP Budget: \$6,069,166
 Total Facilities Budget (Sum of Projects): \$5,597,431

PRIMARY RENOVATIONS P.001728-MCI Annabel C. Perry Pre K-8 - GOB Renovations (Media Center Improvements)

CURRENT PHASE

9-Closed

RISK LEVEL

No Risk


PROJECT UPDATE

PROJECT SCOPE

Media Center improvements

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

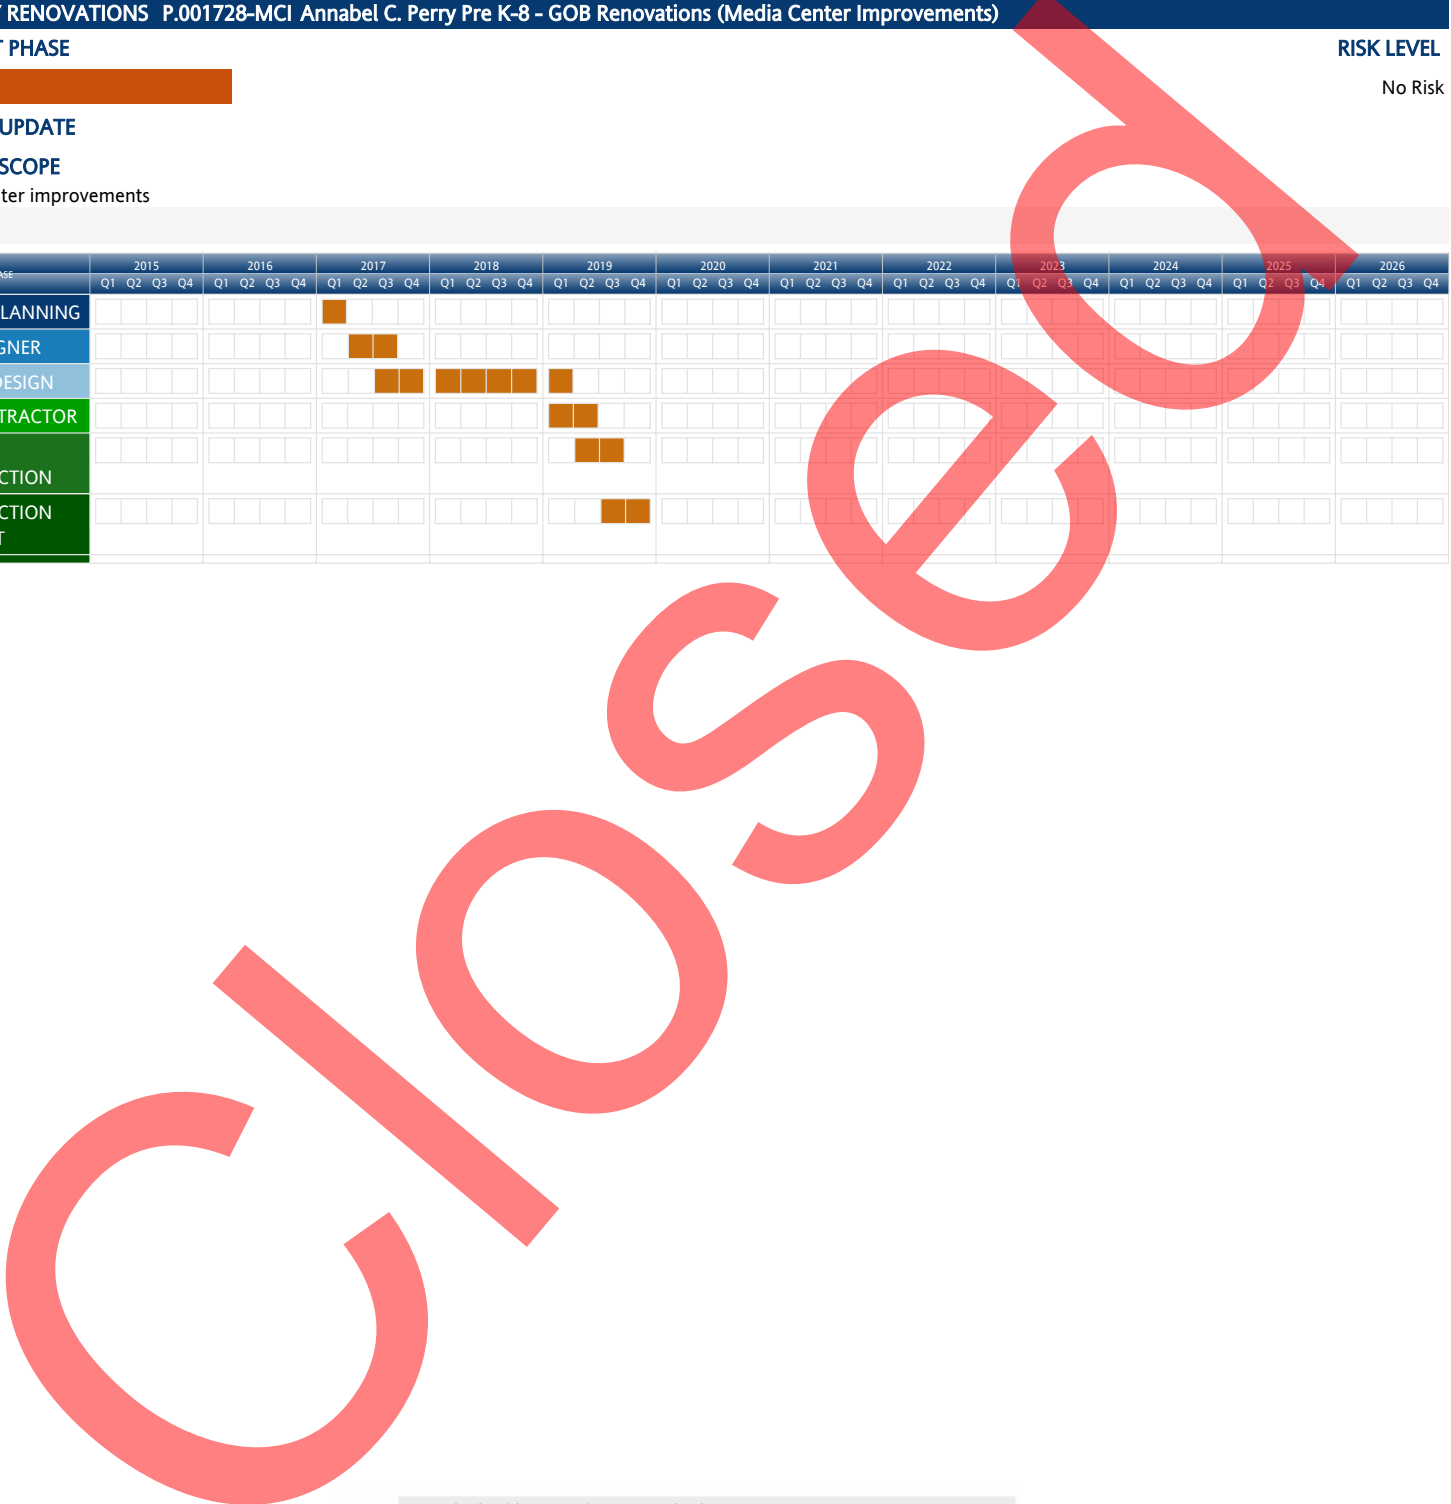

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Coconut Palm Elementary School



Address: 13601 MONARCH LAKES BOULEVARD, MIRAMAR 33027
 Location Num: 3741
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$3,243,215
 Total Facilities Budget (Sum of Projects): \$2,700,300

PRIMARY RENOVATIONS P.002088 Coconut Palm ES - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

5B-Construction



PROJECT UPDATE

Fire Alarm shop drawings for CCD 2 were resubmitted for a second time to the Building Department, and received back with comments to address. No work was done onsite during December. During OAC meetings the PMOR/CC have been telling the GC they have to complete pending non-CCD work that is still pending: backdraft dampers replacements and tie down the roof equipment. Another notice will be sent to the GC regarding contract time and failure to complete the CCD in a timely manor.

PROJECT SCOPE

Electrical Improvements: Building 1 Fascia Repair: Buildings 1, Testing and Balancing: Buildings 1 Reroofing: Building 1

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$141,000	\$111,755	\$29,245
Construction	\$2,036,646	\$1,973,474	\$63,172
Direct Purchase	\$218,387		\$218,387
Construction Mgmt	\$283,850	\$283,850	\$0
Contingency	\$18,267		\$18,267
Consultants	\$2,150	\$1,794	\$356
Project Total:	\$2,700,300	\$2,370,873	\$329,427

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

PIP rubber surfacing, Basketball shade structure, Aiphone submaster station, Recordex, (2) AC adapters & Laptops

BUDGET

\$100,000

MUSIC

SCOPE

COMPLETE 372 Instruments Delivered

TECHNOLOGY

SCOPE

COMPLETE 300 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Coral Cove Elementary School



Address: 5100 SW 148 AVENUE, MIRAMAR 33027
 Location Num: 2011
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$694,303
 Total Facilities Budget (Sum of Projects): \$34,296

PRIMARY RENOVATIONS P.002122 Coral Cove ES - SMART HVAC Improvements

CURRENT PHASE

9-Closed

RISK LEVEL

No Risk

PROJECT UPDATE

PROJECT SCOPE

HVAC Improvements

BUDGET

	Current Budget	Actuals	Remaining Budget
Construction	\$22,796	\$22,796	\$0
Construction Mgmt	\$11,500	\$11,500	\$0
Project Total:	\$34,296	\$34,296	\$0

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

(46) LCD projectors ceiling mounted

BUDGET

\$100,000

MUSIC

SCOPE

COMPLETE

311 Instruments Delivered

TECHNOLOGY

SCOPE

COMPLETE

536 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Dolphin Bay Elementary School



Address: 16450 MIRAMAR PARKWAY, MIRAMAR 33027
 Location Num: 3751
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$300,718
 Total Facilities Budget (Sum of Projects): \$

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE **BUDGET**
 COMPLETE \$100,000
DELIVERED

Projectors, Morning Announcement Studio Equipment, Recordex, Laptops,
 New Playground Equipment Pre-K

MUSIC

✓ **SCOPE**
 COMPLETE 655 Instruments Delivered

TECHNOLOGY

✓ **SCOPE**
 COMPLETE 208 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
 An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
 An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
 A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Everglades High School



Address: 17100 SW 48 COURT, MIRAMAR 33027
 Location Num: 3731
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$7,625,580
 Total Facilities Budget (Sum of Projects): \$5,948,885

PRIMARY RENOVATIONS P.001985 Everglades HS - SMART Program Renovations

CURRENT PHASE

9-Closed

RISK LEVEL

No Risk

PROJECT UPDATE

PROJECT SCOPE

Building Envelope Improvements (Roof, Window, Ext Wall, etc.), HVAC Improvements

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$246,836	\$246,836	\$0
Construction	\$4,102,865	\$4,102,865	\$0
Direct Purchase	\$949,247	\$949,247	\$0
Construction Mgmt	\$649,937	\$649,937	\$0
Project Total:	\$5,948,885	\$5,948,885	\$0

FLAG:

PHASE	2015			2016			2017			2018			2019			2020			2021			2022			2023			2024			2025			2026		
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
PROJECT PLANNING																																				
HIRE DESIGNER																																				
PROJECT DESIGN																																				
HIRE CONTRACTOR																																				
ACTIVE CONSTRUCTION																																				
CONSTRUCTION CLOSEOUT																																				

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Laptops, (6) Printers, Aiphone & Strike

BUDGET

\$100,000

ATHLETICS

✓ COMPLETE **SCOPE**
Weight Room

MUSIC

✓ COMPLETE **SCOPE**
327 Instruments delivered

TECHNOLOGY

✓ COMPLETE **SCOPE**
1,312 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Fairway Elementary School



Address: 7850 FAIRWAY BOULEVARD, MIRAMAR 33023
 Location Num: 1641
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$7,891,469
 Total Facilities Budget (Sum of Projects): \$7,510,899

PRIMARY RENOVATIONS P.001785 Fairway ES - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

6-Substantial Completion

No Risk

PROJECT UPDATE

The Project Time Extension request pending board approval is ongoing. The Architect Created a CCD copied off of PCO 19. The 209 is still pending.

PROJECT SCOPE

Aluminum Covered Walkway Repairs Re-roofing to Buildings 1, 2, 3, 4, 5, 6, 7, 8, & 75 Mechanical Improvements: Buildings 1 (1 AHU), 2 (2 AHU & 10 VAV), 3 (4 AHU), 4 (1 AHU), 5 (2 AHU), 6 (1 AHU), 7 (1 AHU& 1 RTU), and 75 & 78 (2 BARD units, 2 AHU) Fire Alarm System Replacement: Campus-wide Emergency Lighting & Exit Signage Replacement: Campus-wide Building, Canopy, and Pole Lighting Replacement: Campus-wide Media Center Improvements

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$592,889	\$550,372	\$42,517
Construction	\$5,740,702	\$5,725,380	\$15,322
FF&E and Technology	\$30,999	\$30,999	\$0
Direct Purchase	\$438,499	\$438,499	\$0
Construction Mgmt	\$551,960	\$551,960	\$0
Contingency	\$141,844		\$141,844
Consultants	\$14,006	\$14,006	\$0
Project Total:	\$7,510,899	\$7,311,216	\$199,683

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Color poster, Two-way radios, Projectors, Document cameras, Morning show equipment, Sound stage projector, Cafeteria sound system, microphones for the sound system, laptops, Digital marquee, Adaptors, TV installation, Desktop

BUDGET

\$100,000

MUSIC

✓ **SCOPE**

COMPLETE 450 Instruments delivered

TECHNOLOGY

✓ **SCOPE**

COMPLETE 202 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Glades Middle School



Address: 16700 SW 48 COURT, MIRAMAR 33027
 Location Num: 2021
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$891,995
 Total Facilities Budget (Sum of Projects): \$386,000

PRIMARY RENOVATIONS P.001968 Glades MS - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

1-Planning

No Risk

PROJECT UPDATE

PPO managed project.

PROJECT SCOPE

Building Envelope Improvements (Roof, Window, Ext Wall, etc.), HVAC Improvements

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$49,000	\$31,826	\$17,174
Construction	\$263,500	\$112	\$263,388
Construction Mgmt	\$42,460	\$42,460	\$0
Contingency	\$23,540		\$23,540
Consultants	\$7,500	\$1,882	\$5,618
Project Total:	\$386,000	\$76,280	\$309,720

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Apple iPads, books, tablets, Recordex, laptops, P.E. Equipment, camera for TV Production system, technology supplies & HDMI cables

BUDGET

\$100,000

MUSIC

SCOPE

COMPLETE 78 Instruments delivered

TECHNOLOGY

SCOPE

COMPLETE 680 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Henry D. Perry Education Center



Address: 3400 WILDCAT WAY, MIRAMAR 33023
 Location Num: 1011
 Board District: 1
 Board Member: Daniel P. Foganholi
 ADEFP Budget: \$9,720,580
 Total Facilities Budget (Sum of Projects): \$9,308,580

PRIMARY RENOVATIONS P.001986 Henry D. Perry Education Center - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

8-Financial Closeout

No Risk

PROJECT UPDATE

The Architect has a remaining balance for basic services and was advised to submit their final invoice. A walkthrough was performed in December and the Architect and General Contractor will be reviewing the deficiencies found. A meeting is scheduled for January 2024 with the Mechanical Engineer to address the issues found. The Architect was informed that they have pending financial commitments, which they responded to and will follow up in 2024.

PROJECT SCOPE

Fire Alarm System: Campus-wide Fire Sprinklers: Building 4 HVAC Improvements: Buildings 1, 2, 3, 4, 5 & 6 Reroofing: Buildings 1, 2, 3, 4, 5 & 6

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$548,746	\$471,972	\$76,774
Construction	\$6,408,254	\$6,403,158	\$5,096
Direct Purchase	\$950,583	\$950,583	\$0
Construction Mgmt	\$1,210,115	\$1,210,115	\$0
Contingency	\$178,882		\$178,882
Consultants	\$12,000		\$12,000
Project Total:	\$9,308,580	\$9,035,828	\$272,752

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Indoor furniture, cafeteria tables, students chairs, desks, laptop carts

BUDGET

\$100,000

MUSIC

✓ **SCOPE**

COMPLETE 26 Instruments delivered

TECHNOLOGY

✓ **SCOPE**

COMPLETE 71 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Miramar Elementary School



Address: 6831 SW 26 STREET, MIRAMAR 33023
 Location Num: 0531
 Board District: 1
 Board Member: Daniel P. Foganholi
 ADEFP Budget: \$6,539,934
 Total Facilities Budget (Sum of Projects): \$5,920,758

PRIMARY RENOVATIONS P.001727 Miramar ES - SMART GOB Renovations

CURRENT PHASE

9-Closed

RISK LEVEL

No Risk

PROJECT UPDATE

PROJECT SCOPE

Chiller Replacement, Replacement of FCUs, AHUs for Classrooms, Kitchen, and Main Office, Envelope Improvements of Roofing and door replacement for office access.

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$399,011	\$399,011	\$0
Construction	\$4,576,306	\$4,576,306	\$0
Direct Purchase	\$300,000	\$300,000	\$0
Construction Mgmt	\$644,154	\$644,154	\$0
Utilities	\$1,287	\$1,287	\$0
Project Total:	\$5,920,758	\$5,920,758	\$0

FLAG: BUDGET, Reason: Financial Closeout

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Student laptops, safety cones, document cameras, stage curtains, cafeteria sound system, picnic tables, cafeteria blinds, office furniture & digital marquee

BUDGET

\$100,000

MUSIC

✓ **SCOPE**

COMPLETE 224 Instruments delivered

TECHNOLOGY

✓ **SCOPE**

COMPLETE 335 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Miramar High School



Address: 3601 SW 89 AVENUE, MIRAMAR 33025
 Location Num: 1751
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$23,199,935
 Total Facilities Budget (Sum of Projects): \$21,538,560

PRIMARY RENOVATIONS P.002003 Miramar HS - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

5B-Construction



PROJECT UPDATE

The Art room renovation is in progress The Girls locker room renovation is in Progress The Fire sprinkler and fire alarm work is in progress campus wide. The band room renovation is 99% complete Mill work installation was complete, the GC received occupancy, coordination for the Ribbon cutting ceremony The roof work is in 99% complete, pending final inspections The aviation lab renovation is in progress, interior windows have been installed, bathroom was completed, paint complete, pending flooring Electrical panels replacement is in progress AHUs replacement is in progress The ASI addressing the MDPs clearance issues has been approved by the building department.

PROJECT SCOPE

Fire Alarm System: Campus-wide, Fire Sprinklers Building 2, Re-Roofing Buildings 2, 3, 9, & 10, Rooftop Cabling Buildings 1, 2, 4, 5, 7, 8, and 14. Window replacement Building 4 & 12, Door replacement Buildings 1, 4, 9, & 12. Restroom renovations Buildings 2 & 4, Remodel of Band Room. Media Center, & Art Room Building 1. Repair of Fume Hoods Building 7. HVAC Improvements: Campus-wide. Electrical Improvements Building 7 & 8.

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$854,075	\$758,055	\$96,020
Construction	\$14,559,000	\$8,797,971	\$5,761,029
FF&E and Technology	\$310,000	\$264,883	\$45,117
Direct Purchase	\$3,267,258	\$3,025,455	\$241,803
Construction Mgmt	\$2,121,800	\$2,121,800	\$0
Contingency	\$348,427		\$348,427
Consultants	\$55,000	\$13,945	\$41,055
Utilities	\$23,000		\$23,000
Project Total:	\$21,538,560	\$14,982,109	\$6,556,451

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

BUDGET

\$100,000

DELIVERED

Golf cart, security cameras, scrubber machine, protective mats for gym floor, canopy fabric, auditorium painting and signage for gym & stadium, additional parking spaces

ATHLETICS

✓ **SCOPE**
COMPLETE Track, Weight Room

MUSIC

✓ **SCOPE**
COMPLETE 656 Instruments delivered

TECHNOLOGY

✓ **SCOPE**
COMPLETE 1,035 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

New Renaissance Middle School



Address: 10701 MIRAMAR BOULEVARD, MIRAMAR 33027
 Location Num: 3911
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$4,045,999
 Total Facilities Budget (Sum of Projects): \$9,254,400

PRIMARY RENOVATIONS P.002143 New Renaissance MS - SMART Program Renovations

CURRENT PHASE

5B-Construction

RISK LEVEL

No Risk

PROJECT UPDATE

The Project manager working with the CSMP to prepare the NTP. HB Hoffman waiting for stucco contractor to provide the surety bond letter to proceed with the NTP package. NTP package has been submitted to procurement for processing on 12/13/2023.

PROJECT SCOPE

Exterior stucco repair - Bldg 1, 2, 3, and 4. Exterior painting - Bldg 1, 2, 3, and 4. HVAC component replacement - Bldg 1, 2, 3, and 4. HVAC test and balance - Bldg 1, 2, and 3.

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$296,150	\$226,343	\$69,807
Construction	\$3,860,000	\$2,711	\$3,857,289
Construction Mgmt	\$778,250	\$778,250	\$0
Contingency	\$221,000		\$221,000
Consultants	\$20,000	\$1,008	\$18,992
Project Total:	\$5,175,400	\$1,008,312	\$4,167,088

FLAG: BUDGET, Reason: Budget Adjustment

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4				
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

New Renaissance Middle School



Address: 10701 MIRAMAR BOULEVARD, MIRAMAR 33027
 Location Num: 3911
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$4,045,999
 Total Facilities Budget (Sum of Projects): \$9,254,400

PRIMARY RENOVATIONS P.002143-RC1 New Renaissance MS - SMART Roof Carve Out

CURRENT PHASE

RISK LEVEL

5B-Construction

No Risk

PROJECT UPDATE

- Contractor's re-submittal of the design-binders (R02) to the Building Department is ongoing.

PROJECT SCOPE

This Roof Carve Out project consists of the removal and replacement of the existing roofs on the Buildings # 1, 2, 3, & 4, and the related roof top mechanical equipment. GC Engineer: Omar Khan, PE # 75524

BUDGET

	Current Budget	Actuals	Remaining Budget
Construction	\$3,979,000		\$3,979,000
Contingency	\$100,000		\$100,000
Project Total:	\$4,079,000		\$4,079,000

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Aiphone and Strike, Locks replacement, Digital Marquee, Printer, Apple Chargers, Media Furniture, Projectors

BUDGET

\$100,000

MUSIC

✓ **SCOPE**

COMPLETE 158 Instruments Delivered

TECHNOLOGY

✓ **SCOPE**

COMPLETE 447 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Sea Castle Elementary School



Address: 9600 MIRAMAR BOULEVARD, MIRAMAR 33025
 Location Num: 2871
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$4,767,829
 Total Facilities Budget (Sum of Projects): \$4,319,154

PRIMARY RENOVATIONS P.001632 Sea Castle ES - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

5B-Construction



PROJECT UPDATE

General Contractor is finalizing Fire Alarm scope of work. Change order to relocate fan coils in Building 4,5 and 6 is in progress.

PROJECT SCOPE

HVAC Improvements inclusive of (42) FCUs, (9) AHUs, and RTU replacements, Campus-wide Fire Alarm Replacement, Building Envelope Improvements inclusive of reroofing of bldg. 80 and exterior painting, ADA chair lift installation.

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$287,252	\$273,155	\$14,097
Construction	\$3,100,350	\$3,045,728	\$54,622
FF&E and Technology	\$890	\$890	\$0
Direct Purchase	\$309,354	\$308,883	\$471
Construction Mgmt	\$468,202	\$442,178	\$26,024
Contingency	\$139,606		\$139,606
Consultants	\$13,500	\$6,004	\$7,496
Project Total:	\$4,319,154	\$4,076,838	\$242,316

FLAG: SCHEDULE, Reason: Owner Delays / A/E Delays

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Furniture, office furniture, digital marquee, shade structure, science tables, projector, cafeteria sound system, laptops chargers, High Back Executive Chair

BUDGET

\$100,000

MUSIC

SCOPE

COMPLETE 131 Instruments Delivered

TECHNOLOGY

SCOPE

COMPLETE 420 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Silver Lakes Elementary School



Address: 2300 SW 173 AVENUE, MIRAMAR 33029
 Location Num: 3371
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$2,788,779
 Total Facilities Budget (Sum of Projects): \$2,252,383

PRIMARY RENOVATIONS P.002009 Silver Lakes ES - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

9-Closed

No Risk

PROJECT UPDATE

PROJECT SCOPE

Building Envelope Improvements (Roof, Window, Ext Wall, etc.), HVAC Improvements

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$162,736	\$162,736	\$0
Construction	\$1,636,846	\$1,636,846	\$0
Direct Purchase	\$218,873	\$218,873	\$0
Construction Mgmt	\$233,928	\$233,928	\$0
Project Total:	\$2,252,383	\$2,252,383	\$0

FLAG:

PHASE	2015			2016			2017			2018			2019			2020			2021			2022			2023			2024			2025			2026		
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
PROJECT PLANNING																																				
HIRE DESIGNER																																				
PROJECT DESIGN																																				
HIRE CONTRACTOR																																				
ACTIVE CONSTRUCTION																																				
CONSTRUCTION CLOSEOUT																																				

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

New Pre k-2 playground with shade and PIP surfacing

BUDGET

\$100,000

IN PROGRESS

MUSIC

SCOPE

634 Instruments Delivered

TECHNOLOGY

SCOPE

260 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Silver Shores Elementary School



Address: 1701 SW 160 AVENUE, MIRAMAR 33027
 Location Num: 3581
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$2,610,522
 Total Facilities Budget (Sum of Projects): \$2,202,546

PRIMARY RENOVATIONS P.001906 Silver Shores ES - SMART Program Renovations

CURRENT PHASE

9-Closed

RISK LEVEL

No Risk

PROJECT UPDATE

PROJECT SCOPE

Building Envelope Improvements (Roof, Window, Ext Wall, etc.), HVAC Improvements

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$148,839	\$148,839	\$0
Construction	\$1,804,496	\$1,804,496	\$0
Construction Mgmt	\$249,211	\$249,211	\$0
Project Total:	\$2,202,546	\$2,202,546	\$0

FLAG: BUDGET, Reason: Financial Closeout

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Student laptops, classroom furniture, furniture for computer lab and related arts, electric strike and proximity pad, Shades & Student furniture for the media center, Computer Accessories, Think Center

BUDGET

\$100,000

IN PROGRESS

Think Center

MUSIC

SCOPE

COMPLETE

155 Instruments Delivered

TECHNOLOGY

SCOPE

COMPLETE

202 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Sunset Lakes Elementary School



Address: 18400 SW 25 STREET, MIRAMAR 33027
 Location Num: 3661
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$3,235,007
 Total Facilities Budget (Sum of Projects): \$2,799,009

PRIMARY RENOVATIONS P.001971 Sunset Lakes ES - SMART Program Renovations

CURRENT PHASE

9-Closed

RISK LEVEL

No Risk

PROJECT UPDATE

PROJECT SCOPE

Building Envelope Improvements (Roof, Window, Ext Wall, etc.), HVAC Improvements

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$91,778	\$91,778	\$0
Construction	\$1,959,145	\$1,959,145	\$0
Direct Purchase	\$452,083	\$452,083	\$0
Construction Mgmt	\$296,003	\$296,003	\$0
Project Total:	\$2,799,009	\$2,799,009	\$0

FLAG:

PHASE	2015			2016			2017			2018			2019			2020			2021			2022			2023			2024			2025			2026		
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
PROJECT PLANNING																																				
HIRE DESIGNER																																				
PROJECT DESIGN																																				
HIRE CONTRACTOR																																				
ACTIVE CONSTRUCTION																																				
CONSTRUCTION CLOSEOUT																																				

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

New PreK-2 playground, shades for 3-5 play area & fencing to separate the two play areas

BUDGET

\$100,000

IN PROGRESS

MUSIC

SCOPE

COMPLETE 228 Instruments Delivered

TECHNOLOGY

SCOPE

COMPLETE 549 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Sunshine Elementary School



Address: 7737 W LASALLE BOULEVARD, MIRAMAR 33023
 Location Num: 1171
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$4,382,232
 Total Facilities Budget (Sum of Projects): \$3,948,449

PRIMARY RENOVATIONS P.002079 Sunshine ES - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

5B-Construction

No Risk

PROJECT UPDATE

The Contractor this period has made advancements in Building No. 01 Mechanical work renovations. Other work included successful replacement of the Facility's Main Fire Alarm Control Panel and some exterior site improvements. To-Date, Project work remains ongoing and six-months past Contract Time for Substantial Completion. However, the Contractor is wrapping up final scope and Substantial Completion is expected to be achieved next month by February 26th, 2024.

PROJECT SCOPE

Fire Alarm Panel Replacement HVAC Improvements: Buildings 1 (AHU, Controls, & Distribution System), 2 (Exhaust Fan), 4 (Backdraft Dampers)8 (Exhaust Fan), 9 (Exhaust Fans, & HVAC Controls), & 14 (Exhaust Fan). Demolish Building: Building 3 (Bid alternate 1). Roofing Roof: Building 4, 10, 11, and 13. Fire Sprinkler System: Building 4. Building Expansion Joint Replacement: Building 4.

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$158,000	\$130,443	\$27,557
Construction	\$3,245,349	\$2,886,033	\$359,316
FF&E and Technology	\$5,104	\$5,104	\$0
Direct Purchase	\$104,459	\$104,459	\$0
Construction Mgmt	\$264,090	\$262,490	\$1,600
Contingency	\$148,599		\$148,599
Consultants	\$20,848	\$15,034	\$5,814
Utilities	\$2,000		\$2,000
Project Total:	\$3,948,449	\$3,403,563	\$544,886

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Poster maker, headphones, laminator, classrooms rugs, portable blowers, laptops, Earthwalk cart, staff desktop, student desktop, student chairs, shelving, bookcase, pro pencil sharpeners, Ellison machine, Recordex, Athletic Equipment, Indoor Furniture, Projectors

BUDGET

\$100,000

IN PROGRESS

Projectors

MUSIC

SCOPE

COMPLETE 438 Instruments Delivered

TECHNOLOGY

SCOPE

COMPLETE 335 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Whispering Pines Education Center



Address: 3609 SW 89TH AVENUE, MIRAMAR 33025
 Location Num: 1752
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$5,599,046
 Total Facilities Budget (Sum of Projects): \$4,849,580

PRIMARY RENOVATIONS P.002089 Whispering Pines Education Center - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

5B-Construction

No Risk

PROJECT UPDATE

1.Fire Protection piping: Buildings 2, 3, 4,5,6 2.Fire Alarm conduit. 3. Building 3 installed AHU.

PROJECT SCOPE

Exterior Stucco Painting: Buildings 1, 2 & 3 Exterior Stucco Repair: Buildings 1, 2 & 3 Fire Alarm System: Campus-wide Fire Sprinklers: Building 2 Fire Main for New Fire Sprinkler System HVAC Improvements: Buildings 1 & 2 Reroofing: Covered Walkway, Buildings 1, 2 & 3 Test & Balance: Buildings 1, 2 & 3

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$237,000	\$182,407	\$54,593
Construction	\$3,726,109	\$1,996,156	\$1,729,953
Direct Purchase	\$192,539	\$132,564	\$59,975
Construction Mgmt	\$464,000	\$459,000	\$5,000
Contingency	\$209,432		\$209,432
Consultants	\$14,410	\$8,441	\$5,969
Utilities	\$6,090		\$6,090
Project Total:	\$4,849,580	\$2,778,568	\$2,071,012

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

K-2 sand replacement with PIP, Media Center Furniture

BUDGET

\$100,000

IN PROGRESS

Media Center Furniture, PIP

MUSIC

✓ COMPLETE **SCOPE**

No Program

TECHNOLOGY

✓ COMPLETE **SCOPE**

No Items

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.
