

Broadview Elementary School



Address: 1800 SW 62 AVENUE, NORTH LAUDERDALE 33068
 Location Num: 0811
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$6,064,806
 Total Facilities Budget (Sum of Projects): \$5,475,130

PRIMARY RENOVATIONS P.001638 Broadview ES - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

5B-Construction



PROJECT UPDATE

Panel boards need to be installed in the system panel and final connections made. Programming will then be performed for inspection, There are several PCO's pending for additional work needed to complete the roofing / RTU replacement portion of this project

PROJECT SCOPE

Electrical Panel Replacements: Building 1 Fire Alarm: Building 1 Conversion of Cafetorium to Music Room: Building 1 Existing Art Lab Renovation: Building 1 Existing Media Center Renovation: Building 1. HVAC Replacement: Building 1 Test & Balance: Buildings J, 2, 5, 7, 8 & 85, Electrical Panels Replacement: Building 1 Reroofing: Buildings 1, 2 & 85

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$404,720	\$393,156	\$11,564
Construction	\$3,924,284	\$3,071,254	\$853,030
FF&E and Technology	\$31,981	\$31,981	\$0
Direct Purchase	\$491,562	\$390,644	\$100,918
Construction Mgmt	\$428,101	\$428,101	\$0
Contingency	\$141,962		\$141,962
Consultants	\$52,520	\$35,363	\$17,157
Project Total:	\$5,475,130	\$4,350,499	\$1,124,631

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Digital marquee, Classroom rugs, Playground upgrades & equipment, Laptops, HDMI, Adapters

BUDGET

\$100,000

MUSIC

SCOPE

COMPLETE 334 Instruments Delivered

TECHNOLOGY

SCOPE

COMPLETE 338 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Morrow Elementary School



Address: 408 SW 76 TERRACE, NORTH LAUDERDALE 33068
 Location Num: 2691
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$2,228,583
 Total Facilities Budget (Sum of Projects): \$2,817,583

PRIMARY RENOVATIONS P.001996 Morrow ES – SMART Program Renovations

CURRENT PHASE

RISK LEVEL

6-Substantial Completion

No Risk

PROJECT UPDATE

All work has been completed, two PCO's are being processed.

PROJECT SCOPE

Fire Alarm System Replacement Media Center Associated Restroom Renovation Building 1: Electrical: Replace main distribution panel and transformer in electrical room 163, canopy lighting, damaged pole lights, the motor control center in room 165, exterior dry type transformer, and existing transformer in room 150. Mechanical: T&B. Fire Protection Building 2: Electrical: Replace exterior canopy lights and exterior building-mounted lights. Mechanical: T&B. Replace existing DDC controls. Fire Protection: Install new fire sprinklers Building 3: Electrical: Replace exterior canopy lights and building-mounted lights. Mechanical: T&B. Replace existing DDC Controls. Fire Protection: Install new fire protection Building 5: Electrical: Replace exterior building mounted lights. Building 6: Electrical: Replace exterior building mounted lights. Mechanical: T&B Fire Protection: Install New Fire Protection. Building 80: Replace exterior canopy lights. Mechanical: Replace existing DDC Controls

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$227,127	\$184,581	\$42,546
Construction	\$1,230,030	\$942,876	\$287,154
FF&E and Technology	\$54,859	\$54,859	\$0
Construction Mgmt	\$200,220	\$200,220	\$0
Contingency	\$203,493		\$203,493
Consultants	\$1,854		\$1,854
Project Total:	\$1,917,583	\$1,382,536	\$535,047

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

North Lauderdale Pre K - 8 (f.k.a. North Lauderdale Elementary)



Address: 7500 KIMBERLY BOULEVARD, NORTH LAUDERDALE 33068
 Location Num: 2231
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$2,933,349
 Total Facilities Budget (Sum of Projects): \$3,541,349

PRIMARY RENOVATIONS P.001903 North Lauderdale ES - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

5A-Construction

No Risk

PROJECT UPDATE

All scopes are in the following P numbers (no work remains in P.001903) Phase 1 - Fire Sprinklers: Building 1 (P.001903-FSP) status LOR - Fire Alarm Replacement: Building 1 (P.001903-FA1) - in award stage - ADA Restroom Upgrades: Building 1 (Rooms 155 and 156) (P.001903-ADA) in award stage - Test & Balance: Buildings 1, 5, 75, and 78. (P.001903-HVC) in bid phase

PROJECT SCOPE

All scopes are in the following P numbers (no work remains in P.001903) Phase 1 - Fire Sprinklers: Building 1 (P.001903-FSP) status LOR - Fire Alarm Replacement: Building 1 (P.001903-FA1) - in award stage - ADA Restroom Upgrades: Building 1 (Rooms 155 and 156) (P.001903-ADA) in award stage - Test & Balance: Buildings 1, 5, 75, and 78. (P.001903-HVC) in bid phase

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$183,551	\$130,866	\$52,685
Construction	\$809,019		\$809,019
Construction Mgmt	\$233,764	\$233,764	\$0
Contingency	\$31,735		\$31,735
Consultants	\$5,000	\$106	\$4,894
Project Total:	\$1,263,069	\$364,736	\$898,333

FLAG: BUDGET, Reason: Budget Adjustment

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

North Lauderdale Pre K - 8 (f.k.a. North Lauderdale Elementary)



Address: 7500 KIMBERLY BOULEVARD, NORTH LAUDERDALE 33068
 Location Num: 2231
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$2,933,349
 Total Facilities Budget (Sum of Projects): \$3,541,349

PRIMARY RENOVATIONS P.001903-ADA North Lauderdale ES - SMART ADA Restrooms

CURRENT PHASE

RISK LEVEL

5A-Construction

No Risk

PROJECT UPDATE

The Project Manager is negotiating with a CSMP for an agreeable cost, narrative (scope of work), and schedule to be completed in January 2024.

PROJECT SCOPE

ADA Restroom Upgrades: Building 1 (Rooms 155 and 156)

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

North Lauderdale Pre K - 8 (f.k.a. North Lauderdale Elementary)



Address: 7500 KIMBERLY BOULEVARD, NORTH LAUDERDALE 33068
 Location Num: 2231
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$2,933,349
 Total Facilities Budget (Sum of Projects): \$3,541,349

PRIMARY RENOVATIONS P.001903-FA1 North Lauderdale ES - SMART Fire Alarm

CURRENT PHASE

RISK LEVEL

5A-Construction

No Risk

PROJECT UPDATE

Additional funding is required, this request is scheduled for the January 2024 board meeting. Meanwhile, the NTP/PO package has been prepared.

PROJECT SCOPE

Design Build for the replacement of the campus-wide fire alarm system

BUDGET

	Current Budget	Actuals	Remaining Budget
Construction	\$1,010,000		\$1,010,000
Contingency	\$55,000		\$55,000
Project Total:	\$1,065,000		\$1,065,000

FLAG: BUDGET, Reason: Budget Adjustment

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

North Lauderdale Pre K - 8 (f.k.a. North Lauderdale Elementary)



Address: 7500 KIMBERLY BOULEVARD, NORTH LAUDERDALE 33068
Location Num: 2231
Board District: 4
Board Member: Lori Alhadeff
ADEFP Budget: \$2,933,349
Total Facilities Budget (Sum of Projects): \$3,541,349

PRIMARY RENOVATIONS P.001903-FSP North Lauderdale ES - SMART Fire Sprinklers

CURRENT PHASE

5B-Construction

RISK LEVEL

No Risk

PROJECT UPDATE

Building department review complete. Waiting on city of North Lauderdale permit for work in their jurisdiction. After receipt of N. Lauderdale permit BCPS will issue building permit

PROJECT SCOPE

Scope of work - Design Build North Lauderdale ES Building 1 install Fire Sprinklers (59,956 SF). Action Item: 1. Design Build - Fire Sprinklers Building #1 (59,956 SF) and connection to City water. 2. Prepare and submit a City of North Lauderdale Plumbing /Civil application for the permit: a. 2 signed and sealed Civil drawings sets

BUDGET

	Current Budget	Actuals	Remaining Budget
Construction	\$770,000	\$54,530	\$715,470
Project Total:	\$770,000	\$54,530	\$715,470

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

North Lauderdale Pre K - 8 (f.k.a. North Lauderdale Elementary)



Address: 7500 KIMBERLY BOULEVARD, NORTH LAUDERDALE 33068
 Location Num: 2231
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$2,933,349
 Total Facilities Budget (Sum of Projects): \$3,541,349

PRIMARY RENOVATIONS P.001903-HVC North Lauderdale ES - SMART HVAC Improvements

CURRENT PHASE

RISK LEVEL

5A-Construction

No Risk

PROJECT UPDATE

The 800A is out for bid with a current BSSC CSPM contractor - the team is meeting with the CSPM and visiting sites together information is needed to prepare their 800B, narratives, and draft schedule. PM is Working with CSMP to complete their quote documentation.

PROJECT SCOPE

Test and Balance Building #3

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



- HIGH:**
An issue that can impact the project's budget and/or schedule, a resolution is being determined.
- MEDIUM:**
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.
- LOW:**
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

North Lauderdale Pre K - 8 (f.k.a. North Lauderdale Elementary)



Address: 7500 KIMBERLY BOULEVARD, NORTH LAUDERDALE 33068
 Location Num: 2231
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$2,933,349
 Total Facilities Budget (Sum of Projects): \$3,541,349

PRIMARY RENOVATIONS P.001903-MCI North Lauderdale ES - SMART Media Center Improvements

CURRENT PHASE

RISK LEVEL

9-Closed

No Risk

PROJECT UPDATE

PROJECT SCOPE


Media Center improvements

BUDGET

	Current Budget	Actuals	Remaining Budget
Construction	\$71,932	\$71,932	\$0
FF&E and Technology	\$43,348	\$43,348	\$0
Project Total:	\$115,280	\$115,280	\$0

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

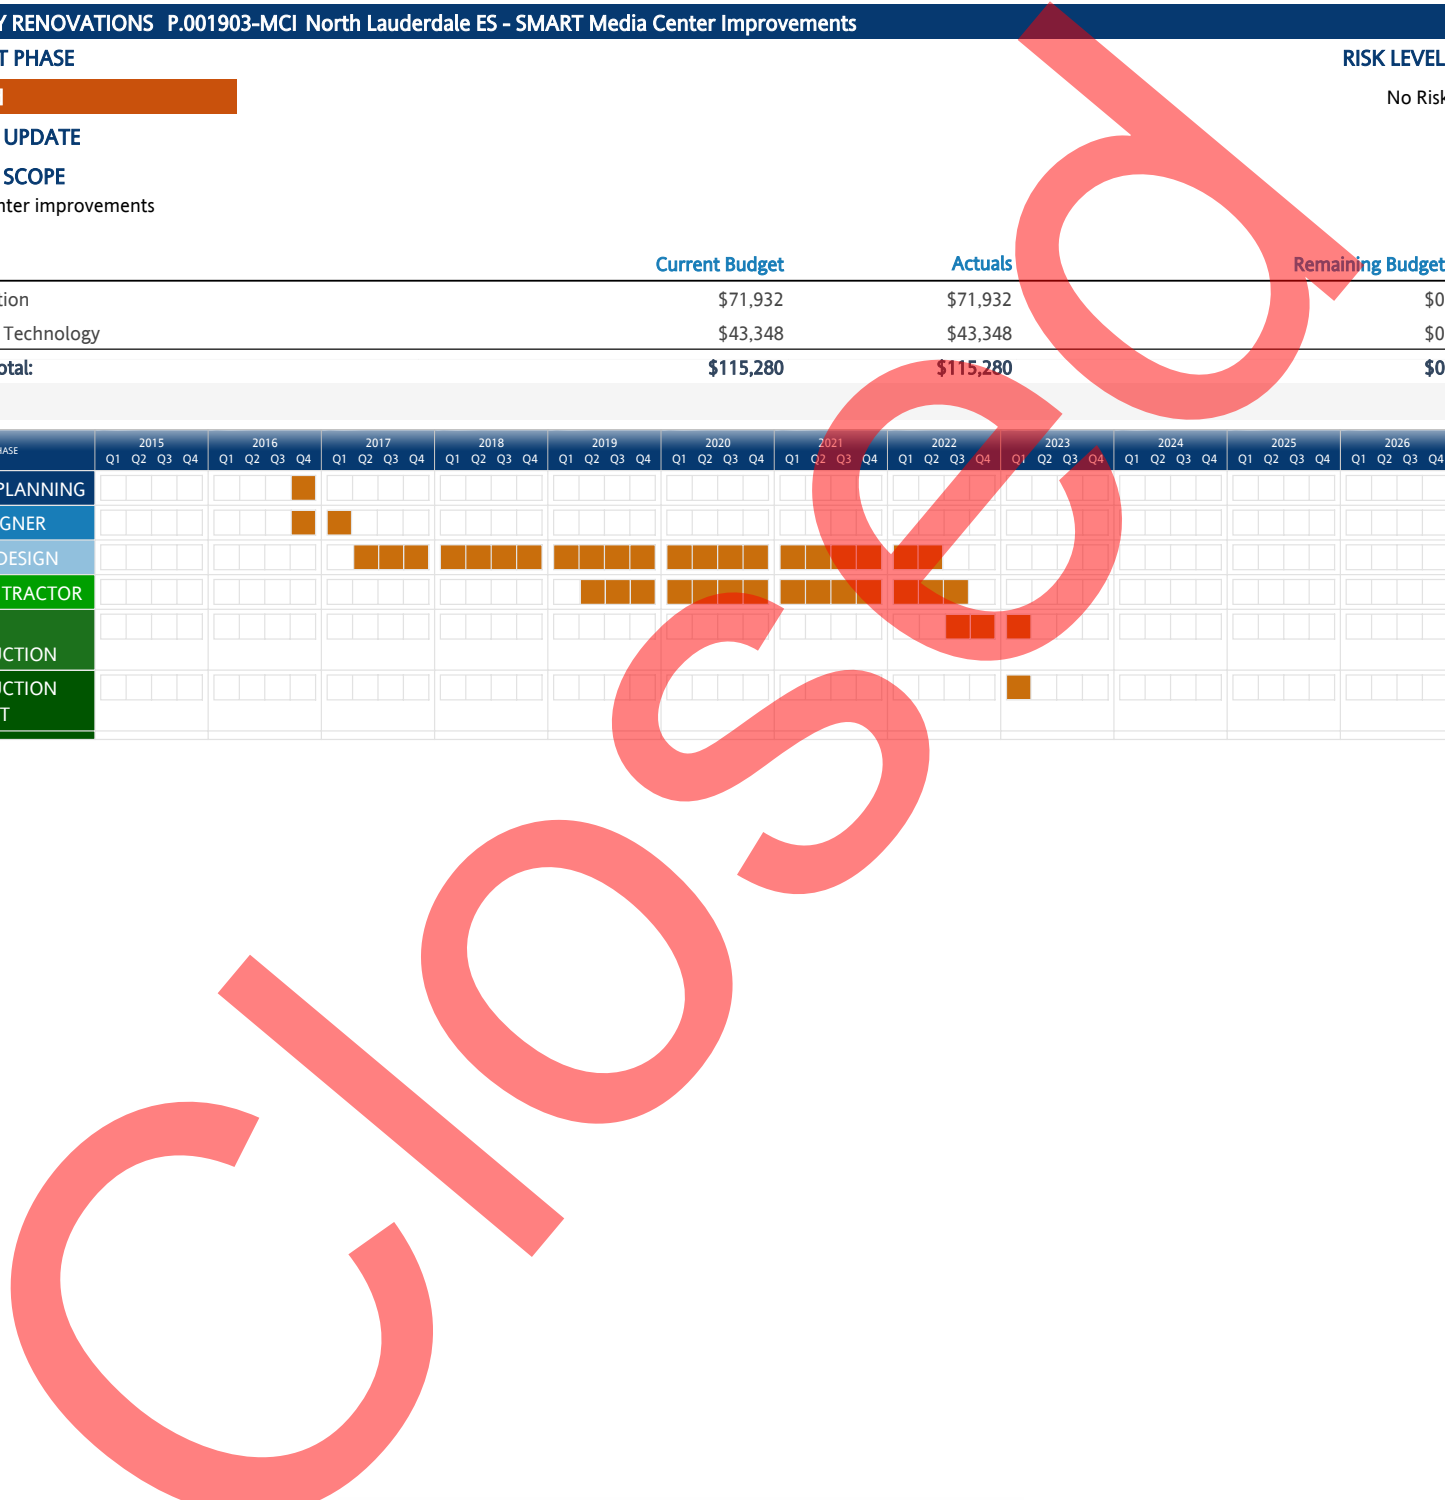

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



- HIGH:**
An issue that can impact the project's budget and/or schedule, a resolution is being determined.
- MEDIUM:**
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.
- LOW:**
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

North Lauderdale Pre K - 8 (f.k.a. North Lauderdale Elementary)



Address: 7500 KIMBERLY BOULEVARD, NORTH LAUDERDALE 33068
 Location Num: 2231
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$2,933,349
 Total Facilities Budget (Sum of Projects): \$3,541,349

PRIMARY RENOVATIONS P.002870 North Lauderdale ES - Roofing Building 2, 4 & 5 - SMART Program

CURRENT PHASE

RISK LEVEL

9-Closed

No Risk

PROJECT UPDATE

PROJECT SCOPE

Roofs carve-out, Bldgs. 2, 4 & 5 and their associated Mechanical Rooftop equipment

BUDGET

	Current Budget	Actuals	Remaining Budget
Construction	\$298,000	\$298,000	\$0
Construction Mgmt	\$30,000	\$30,000	\$0
Project Total:	\$328,000	\$328,000	\$0

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Student laptops, partial work for murals, TV screens for the front office, digital marquee, Aiphone & EDS, Shelving for the Media Center, Murals

BUDGET

\$100,000

IN PROGRESS

Murals for the media center (pending completion of renovations)

MUSIC

SCOPE

113 Instruments Delivered

TECHNOLOGY

SCOPE

209 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Pinewood Elementary School



Address: 1600 SW 83 AVENUE, NORTH LAUDERDALE 33068
 Location Num: 2811
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$4,654,756
 Total Facilities Budget (Sum of Projects): \$4,306,000

PRIMARY RENOVATIONS P.001949 Pinewood ES -SMART Program Renovations

CURRENT PHASE

9-Closed

RISK LEVEL

No Risk

PROJECT UPDATE

PROJECT SCOPE

Electrical - Disconnect & Reconnect Roof Top Units - Buildings 1, 2, 3, 4, 75 & 85 Fire Sprinkler: Building 1 HVAC Improvements, Adjust Rooftop Vents: Buildings 1, 2, 3, 4, 75 & 85 Media Center Improvements - Drywall and Painting Plumbing Vents: Buildings 1, 2, 3, 4, 75 & 85 Roof: Buildings 1, 2, 3, 4, 75 & 85 Test & Balance: Buildings 1, 2, 3, 4, 75 & 85

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$185,979	\$169,109	\$16,870
Construction	\$3,330,217	\$3,210,681	\$119,536
FF&E and Technology	\$47,966	\$47,050	\$916
Construction Mgmt	\$645,900	\$645,900	\$0
Contingency	\$92,864		\$92,864
Consultants	\$3,074	\$3,074	\$0
Project Total:	\$4,306,000	\$4,075,814	\$230,186

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Laptops, desktops, laptop carts, two-way radios, portable sound system, electric strike, digital marquee and desktops

BUDGET

\$100,000

MUSIC

SCOPE

COMPLETE 197 Instruments Delivered

TECHNOLOGY

SCOPE

COMPLETE 217 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Silver Lakes Middle School



Address: 7600 TAM O'SHANTER BOULEVARD, NORTH LAUDERDALE 33068
 Location Num: 2971
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$2,930,862
 Total Facilities Budget (Sum of Projects): \$5,450,000

PRIMARY RENOVATIONS P.002144 Silver Lakes MS - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

6-Substantial Completion

No Risk

PROJECT UPDATE

Painting completed on 7/17/23. Carpet replacement completed August 2023. Existing furniture was reinstalled until the new furniture is ordered and delivered. 12/15/23 Furniture proposals received and ordered.

PROJECT SCOPE

Media Center Renovations Building 6.

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$238,839	\$125,557	\$113,282
Construction	\$160,000	\$34,565	\$125,435
FF&E and Technology	\$67,696		\$67,696
Construction Mgmt	\$518,951	\$518,951	\$0
Contingency	\$4,514		\$4,514
Consultants	\$25,000	\$3,613	\$21,387
Utilities	\$5,000		\$5,000
Project Total:	\$1,020,000	\$682,686	\$337,314

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Silver Lakes Middle School



Address: 7600 TAM O'SHANTER BOULEVARD, NORTH LAUDERDALE 33068
 Location Num: 2971
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$2,930,862
 Total Facilities Budget (Sum of Projects): \$5,450,000

PRIMARY RENOVATIONS P.002144-FSP Silver Lakes MS - SMART Fire Sprinklers

CURRENT PHASE

5A-Construction

RISK LEVEL

No Risk

PROJECT UPDATE

Carveout project for Fire Sprinklers. 550,000 Received approval to move forward with NTP Checklist. NTP expected to be Late January, 2024. Awaiting Documents from Francis Eng, Orrett Francis. Permitting and Shop Drawings February, 2024. Flow Test Fire Line. Fire Line Tap. FDC. Project Completion expected to be August-September, 2024.

PROJECT SCOPE

P.002144-FSP Design-Build Budget in EBuilder \$680,000. Fire Sprinklers Building 7 Underground tap to fire main. Possible relocation of a hydrant in the building 5 crumple zone.

BUDGET

	Current Budget	Actuals	Remaining Budget
Construction	\$650,000		\$650,000
Contingency	\$30,000		\$30,000
Project Total:	\$680,000		\$680,000

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Silver Lakes Middle School



Address: 7600 TAM O'SHANTER BOULEVARD, NORTH LAUDERDALE 33068
 Location Num: 2971
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$2,930,862
 Total Facilities Budget (Sum of Projects): \$5,450,000

PRIMARY RENOVATIONS P.002144-RC1 Silver Lakes MS - SMART Roof Carve Out

CURRENT PHASE

RISK LEVEL

5B-Construction

No Risk

PROJECT UPDATE

-12/5/23: NTP package submitted to Procurement. -12/7/23: NTP issued to the contractor with a start date of 12/14/23. -Contractor currently preparing R01 binders.

PROJECT SCOPE

Reroofing of Bldgs 1, 6-15, & 85.

BUDGET

	Current Budget	Actuals	Remaining Budget
Construction	\$3,571,368		\$3,571,368
Contingency	\$178,632		\$178,632
Project Total:	\$3,750,000		\$3,750,000

FLAG: BUDGET, Reason: Budget Adjustment

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Window Wraps, Indoor Furniture, Electric Strikes

BUDGET

\$100,000

IN PROGRESS

Electric Strikes

MUSIC

✓ **SCOPE**

COMPLETE **122 Instruments Delivered**

TECHNOLOGY

✓ **SCOPE**

COMPLETE **71 Items Delivered**

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.
