



Established 1915

BROWARD
County Public Schools

**SAFETY
MUSIC & ART
ATHLETICS
RENOVATION
TECHNOLOGY**

District Board Member:
Torey Alston



DISTRICT 2 REPORT

For The Quarter Ending
September 30, 2023 | FY24 Q1

PREFACE

We are pleased to present the Broward County Public Schools (BCPS) **School Spotlights** specifically designed for our School Board Members serving in county-wide school districts.

SMART (**S**afety, **M**usic & **A**rt, **A**thletics, **R**enovation and **T**echnology) is the **\$800 million capital improvement program** to upgrade existing school facilities and to purchase new computer technology, athletic equipment and musical instruments to enhance the learning experience of Broward County students.

The **School Spotlight** is a quarterly report that details the progress of facilities projects at each of the 232 schools participating in the *SMART Bond Program*. This District Board Member edition provides a school-district breakdown of all approved renovation projects, projected costs, School Choice Enhancement Program initiatives and other ongoing or scheduled SMART Program projects.

These easy-to-read School Spotlights allow board members to better follow the progress of the facilities improvements within their specific school districts. The Spotlights will be updated every quarter to help board members share timely information with parents, students, school staff, volunteers, business groups, community organizations and other stakeholders as the projects progress.

Charles W. Flanagan High School



Address: 12800 TAFT STREET, PEMBROKE PINES 33028
 Location Num: 3391
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$17,903,461
 Total Facilities Budget (Sum of Projects): \$15,326,361

PRIMARY RENOVATIONS P.001847 Charles W. Flanagan HS - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

6-Substantial Completion



PROJECT UPDATE

CMAR is preparing a substitution request in order to resubmit the gate and fence permit.

PROJECT SCOPE

Aluminum Covered Walkways Replacement: Campus-wide Classroom Addition Aluminum Window Replacement: Buildings 1, 2, 3 & 9 Re-roofing: Buildings 3 (including new decking), 5 (including new decking), 7 & 8 (including new decking) HVAC Improvements: Buildings 1, (Test & Balance). 2 (Exhaust Hoods, Roof Condenser, and Test & Balance), 3 (Circulating Pump, Chiller & Cooling Tower) 4 (Test & Balance), 5 (Test & Balance), 6 (Test & Balance), 8 (Exhaust Fan & Test & Balance), 9 (Test & Balance), & 11 (Controls, Electric Heater, Window AC Unit)

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$570,064	\$570,064	\$0
Construction	\$10,365,761	\$9,395,474	\$970,287
FF&E and Technology	\$739,192	\$739,192	\$0
Direct Purchase	\$1,722,818	\$1,682,143	\$40,675
Construction Mgmt	\$1,836,895	\$1,783,895	\$53,000
Contingency	\$78,134		\$78,134
Consultants	\$13,497	\$13,497	\$0
Project Total:	\$15,326,361	\$14,184,265	\$1,142,096

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4																																												
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Floor scrubber, Hedger, Trimmer, Blower, Two-way radios, ID machine, Recordex, Golf carts, Two-way radio batteries, Digital marquee, Office furniture

BUDGET

\$100,000

ATHLETICS

✓ **SCOPE**
COMPLETE Track,Weight Room

MUSIC

✓ **SCOPE**
COMPLETE 210 Instruments Delivered

TECHNOLOGY

✓ **SCOPE**
COMPLETE 600 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Coral Cove Elementary School



Address: 5100 SW 148 AVENUE, MIRAMAR 33027
 Location Num: 2011
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$694,303
 Total Facilities Budget (Sum of Projects): \$34,296

PRIMARY RENOVATIONS P.002122 Coral Cove ES - SMART HVAC Improvements

CURRENT PHASE

9-Closed

RISK LEVEL

No Risk

PROJECT UPDATE

PROJECT SCOPE

HVAC Improvements

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4																																												
PROJECT PLANNING																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

(46) LCD projectors ceiling mounted

BUDGET

\$100,000

MUSIC

✓ COMPLETE

SCOPE

311 Instruments Delivered

✓ COMPLETE

SCOPE

536 Items Delivered

CLOSED

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Coral Cove Elementary School



Address: 5100 SW 148 AVENUE, MIRAMAR 33027
 Location Num: 2011
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$694,303
 Total Facilities Budget (Sum of Projects): \$34,296

PRIMARY RENOVATIONS P.002122 Coral Cove ES - SMART HVAC Improvements

CURRENT PHASE

9-Closed

RISK LEVEL

No Risk

PROJECT UPDATE

PROJECT SCOPE

HVAC Improvements

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4																																												
PROJECT PLANNING																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

(46) LCD projectors ceiling mounted

BUDGET

\$100,000

MUSIC

✓ COMPLETE

SCOPE

311 Instruments Delivered

✓ COMPLETE

SCOPE

536 Items Delivered

CLOSED

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Dolphin Bay Elementary School



Address: 16450 MIRAMAR PARKWAY, MIRAMAR 33027
 Location Num: 3751
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$300,718
 Total Facilities Budget (Sum of Projects):

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE	BUDGET
COMPLETE	\$100,000
DELIVERED	

Projectors, Morning Announcement Studio Equipment, Recordex, Laptops,
 New Playground Equipment Pre-K

MUSIC

COMPLETE	SCOPE
	655 Instruments Delivered

TECHNOLOGY

COMPLETE	SCOPE
	208 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Everglades High School



Address: 17100 SW 48 COURT, MIRAMAR 33027
 Location Num: 3731
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$7,625,580
 Total Facilities Budget (Sum of Projects): \$5,948,885

PRIMARY RENOVATIONS P.001985 Everglades HS - SMART Program Renovations

CURRENT PHASE

9-Closed

RISK LEVEL

No Risk

PROJECT UPDATE

PROJECT SCOPE

Building Envelope Improvements (Roof, Window, Ext Wall, etc.), HVAC Improvements

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$246,836	\$246,836	\$0
Construction	\$4,102,865	\$4,102,865	\$0
Direct Purchase	\$949,247	\$949,247	\$0
Construction Mgmt	\$649,937	\$649,937	\$0
Project Total:	\$5,948,885	\$5,948,885	\$0

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4																																												
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Laptops, (6) Printers, Aiphone & Strike

BUDGET

\$100,000

ATHLETICS

✓ COMPLETE

SCOPE

Weight Room

MUSIC

✓ COMPLETE

SCOPE

327 Instruments delivered

TECHNOLOGY

✓ COMPLETE

SCOPE

1,312 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Fairway Elementary School



Address: 7850 FAIRWAY BOULEVARD, MIRAMAR 33023
 Location Num: 1641
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$7,891,469
 Total Facilities Budget (Sum of Projects): \$7,510,899

PRIMARY RENOVATIONS P.001785 Fairway ES - SMART Program Renovations

CURRENT PHASE

6-Substantial Completion

RISK LEVEL

No Risk

PROJECT UPDATE

110b has been executed by the BD. One pending item: The keyed section of the mullion is pending delivery. 209 will be issued as soon as this is resolved The fire rated hardware is installed.

PROJECT SCOPE

Aluminum Covered Walkway Repairs Re-roofing to Buildings 1, 2, 3, 4, 5, 6, 7, 8, & 75 Mechanical Improvements: Buildings 1 (1 AHU), 2 (2 AHU & 10 VAV), 3 (4 AHU), 4 (1 AHU), 5 (2 AHU), 6 (1 AHU), 7 (1 AHU& 1 RTU), and 75 & 78 (2 BARD units, 2 AHU) Fire Alarm System Replacement: Campus-wide Emergency Lighting & Exit Signage Replacement: Campus-wide Building, Canopy, and Pole Lighting Replacement: Campus-wide Media Center Improvements

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$592,889	\$550,372	\$42,517
Construction	\$5,729,298	\$5,725,380	\$3,918
FF&E and Technology	\$30,999	\$30,999	\$0
Direct Purchase	\$438,499	\$438,499	\$0
Construction Mgmt	\$551,960	\$551,960	\$0
Contingency	\$153,248		\$153,248
Consultants	\$14,006	\$14,006	\$0
Project Total:	\$7,510,899	\$7,311,216	\$199,683

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4																																												
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Color poster, Two-way radios, Projectors, Document cameras, Morning show equipment, Sound stage projector, Cafeteria sound system, microphones for the sound system, laptops, Digital marquee, Adaptors, TV installation, Desktop

BUDGET

\$100,000

MUSIC

SCOPE

COMPLETE 450 Instruments delivered

TECHNOLOGY

SCOPE

COMPLETE 202 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Glades Middle School



Address: 16700 SW 48 COURT, MIRAMAR 33027
 Location Num: 2021
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$891,995
 Total Facilities Budget (Sum of Projects): \$386,000

PRIMARY RENOVATIONS P.001968 Glades MS - SMART Program Renovations

CURRENT PHASE

1-Planning

RISK LEVEL

No Risk

PROJECT UPDATE

PPO managed project.

PROJECT SCOPE

Building Envelope Improvements (Roof, Window, Ext Wall, etc.), HVAC Improvements

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$49,000	\$31,826	\$17,174
Construction	\$263,500	\$112	\$263,388
Construction Mgmt	\$42,460	\$42,460	\$0
Contingency	\$23,540		\$23,540
Consultants	\$7,500	\$1,882	\$5,618
Project Total:	\$386,000	\$76,280	\$309,720

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4																																												
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Apple iPads, books, tablets, Recordex, laptops, P.E. Equipment, camera for TV Production system, technology supplies & HDMI cables

BUDGET

\$100,000

MUSIC

✓ **SCOPE**

COMPLETE **78 Instruments delivered**

TECHNOLOGY

✓ **SCOPE**

COMPLETE **680 Items Delivered**

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Hawkes Bluff Elementary School



Address: 5900 SW 160 AVENUE, DAVIE 33331
 Location Num: 3131
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$7,395,850
 Total Facilities Budget (Sum of Projects): \$6,852,890

PRIMARY RENOVATIONS P.001784 Hawkes Bluff ES - SMART Program Renovations

CURRENT PHASE

5B-Construction

RISK LEVEL

No Risk

PROJECT UPDATE

Test and Balance deficiencies are being corrected as part of the commissioning of the new mechanical systems. One inspection, Plumbing Final, remains to obtain the 110B Certificate of Occupancy at this time. The inspection is scheduled for the week of 10/10/23.

PROJECT SCOPE

HVAC Improvements: Buildings 1 (1 CU & 10 FCU), 2 (2 FCU & 2 Chillers), 3 (1 RTU, 1 AHU, 3 FCU), 4 (5 Gravity Ventilators, 9 FCU), 5 (7 Gravity Ventilators, & 12 FCU), 6 (4 Gravity Ventilators, & 7 FCU), & 8 (Wall unit) Re-roofing: Buildings 1, 2, 3, 4, 5, & 75

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$573,022	\$554,509	\$18,513
Construction	\$4,593,975	\$4,438,700	\$155,275
Direct Purchase	\$902,202	\$893,505	\$8,697
Construction Mgmt	\$672,083	\$672,083	\$0
Contingency	\$91,608		\$91,608
Consultants	\$20,000		\$20,000
Project Total:	\$6,852,890	\$6,558,797	\$294,093

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4																																												
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Student chairs, LCD projector, Primary Playground Upgrades, Classroom blinds, shade structure, AC Adaptor

BUDGET

\$100,000

MUSIC

SCOPE

COMPLETE 239 Instruments delivered

TECHNOLOGY

SCOPE

COMPLETE 300 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



- HIGH:** An issue that can impact the project's budget and/or schedule, a resolution is being determined.
- MEDIUM:** An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.
- LOW:** A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Lakeside Elementary School



Address: 900 NW 136 AVENUE, PEMBROKE PINES 33028
 Location Num: 3591
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$4,891,240
 Total Facilities Budget (Sum of Projects): \$4,284,240

PRIMARY RENOVATIONS P.002070 Lakeside ES - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

5B-Construction



PROJECT UPDATE

- Test and Balance was scheduled and is currently on going. Report to be received by beginning of October. After it is completed, commissioning will be scheduled. - Pending punch out items pending on the kitchen: wall paint, 2 light fixtures' frames to be replaced by the side of the kitchen hood and patch the hole created on the wall when the push button on the kitchen was moved to another location. - PCO 5 Time Extension was reviewed by the scheduler and comment was posted on e-builder for the general contractor to provide additional information.

PROJECT SCOPE

Electrical Improvements Exterior Lighting: Campus-wide HVAC Improvements Duck Heater, AHU Building 4, Controls: Building 17 Window-mount A/C: Building 4 Re-Roofing: Building 4, 8, 9, & 10

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$245,000	\$203,282	\$41,718
Construction	\$2,974,551	\$2,353,221	\$621,330
Direct Purchase	\$389,755	\$300,556	\$89,199
Construction Mgmt	\$456,969	\$456,969	\$0
Contingency	\$206,965		\$206,965
Consultants	\$6,000		\$6,000
Utilities	\$5,000		\$5,000
Project Total:	\$4,284,240	\$3,314,028	\$970,212

FLAG: SCHEDULE, Reason:Owner Delays/Contractor Delays

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4																																												
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Promethean boards, Stools, 10-piece portable work stations, Flexible chairs, Digital Marquee. Laptops

BUDGET

\$100,000

MUSIC

✓ **SCOPE**

COMPLETE **361 Instruments delivered**

TECHNOLOGY

✓ **SCOPE**

COMPLETE **372 Items Delivered**

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Miramar High School



Address: 3601 SW 89 AVENUE, MIRAMAR 33025
 Location Num: 1751
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$23,199,935
 Total Facilities Budget (Sum of Projects): \$21,538,560

PRIMARY RENOVATIONS P.002003 Miramar HS - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

5B-Construction



PROJECT UPDATE

The Fire sprinkler and fire alarm work is in progress campus wide. The band room renovation is in progress, ceiling grid installation was complete, new lights installation was complete, doors were installed, paint was complete, sound panels were installed, flooring was complete. pending Mill work installation. The roof work is in 99% complete, pending final inspections The aviation lab renovation is in progress, interior windows have been installed, bathroom in progress, painting in progress. Electrical panels replacement is in progress AHUs replacement is in progress Cooling towers replacement is in progress, CT2 was installed, the structural support for CT1 is in progress A meeting was held with SGM to discuss the MDP clearance issue at the chiller room

PROJECT SCOPE

Fire Alarm System: Campus-wide, Fire Sprinklers Building 2, Re-Roofing Buildings 2, 3, 9, & 10, Rooftop Cabling Buildings 1, 2, 4, 5, 7, 8, and 14. Window replacement Building 4 & 12, Door replacement Buildings 1, 4, 9, & 12. Restroom renovations Buildings 2 & 4, Remodel of Band Room. Media Center, & Art Room Building 1. Repair of Fume Hoods Building 7. HVAC Improvements: Campus-wide. Electrical Improvements Building 7 & 8.

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$854,075	\$747,664	\$106,411
Construction	\$14,559,000	\$7,643,368	\$6,915,632
FF&E and Technology	\$310,000	\$252,931	\$57,069
Direct Purchase	\$3,267,258	\$3,025,455	\$241,803
Construction Mgmt	\$2,121,800	\$2,121,800	\$0
Contingency	\$348,427		\$348,427
Consultants	\$55,000	\$13,945	\$41,055
Utilities	\$23,000		\$23,000
Project Total:	\$21,538,560	\$13,805,163	\$7,733,397

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4																																												
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

BUDGET

\$100,000

DELIVERED

Golf cart, security cameras, scrubber machine, protective mats for gym floor, canopy fabric, auditorium painting and signage for gym & stadium, additional parking spaces

ATHLETICS

SCOPE

Track, Weight Room

MUSIC

SCOPE

656 Instruments delivered

TECHNOLOGY

SCOPE

1,035 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

New Renaissance Middle School



Address: 10701 MIRAMAR BOULEVARD, MIRAMAR 33027
 Location Num: 3911
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$4,045,999
 Total Facilities Budget (Sum of Projects): \$5,283,000

PRIMARY RENOVATIONS P.002143 New Renaissance MS - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

5A-Construction



PROJECT UPDATE

The project is on the October 2023 board for additional funding. The Project manager working with the CSMP to prepare the NTP.

PROJECT SCOPE

Exterior stucco repair - Bldg 1, 2, 3, and 4. Exterior painting - Bldg 1, 2, 3, and 4. HVAC component replacement - Bldg 1, 2, 3, and 4. HVAC test and balance - Bldg 1, 2, and 3.

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$296,150	\$226,343	\$69,807
Construction	\$40,000	\$2,711	\$37,289
Construction Mgmt	\$778,250	\$778,250	\$0
Contingency	\$69,600		\$69,600
Consultants	\$20,000	\$1,008	\$18,992
Project Total:	\$1,204,000	\$1,008,312	\$195,688

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4																																												
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

New Renaissance Middle School



Address: 10701 MIRAMAR BOULEVARD, MIRAMAR 33027
 Location Num: 3911
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$4,045,999
 Total Facilities Budget (Sum of Projects): \$5,283,000

PRIMARY RENOVATIONS P.002143-RC1 New Renaissance MS - SMART Roof Carve Out

CURRENT PHASE

5B-Construction

RISK LEVEL

No Risk

PROJECT UPDATE

- The design phase is in progress. Final design - binders are expected to be delivered by GC as on 10/25/23.

PROJECT SCOPE

This Roof Carve Out project consists of the removal and replacement of the existing roofs on the Buildings # 1, 2, 3, & 4, and the related roof top mechanical equipment.

BUDGET

	Current Budget	Actuals	Remaining Budget
Construction	\$3,979,000		\$3,979,000
Contingency	\$100,000		\$100,000
Project Total:	\$4,079,000		\$4,079,000

FLAG: BUDGET, Reason: Budget Adjustment

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4																																												
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Aiphone and Strike, Locks replacement, Digital Marquee, Printer, Apple Chargers, Media Furniture, Projectors

BUDGET

\$100,000

MUSIC

✓ **SCOPE**

COMPLETE 158 Instruments Delivered

TECHNOLOGY

✓ **SCOPE**

COMPLETE 447 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Palm Cove Elementary School



Address: 11601 WASHINGTON STREET, PEMBROKE PINES 33025
 Location Num: 3311
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$3,888,326
 Total Facilities Budget (Sum of Projects): \$3,450,590

PRIMARY RENOVATIONS P.001885 Palm Cove ES - SMART Program Renovations

CURRENT PHASE

9-Closed

RISK LEVEL

No Risk

PROJECT UPDATE

PROJECT SCOPE

Building Envelope Improvements (Roof, Window, Ext Wall, etc.), HVAC Improvements

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$270,973	\$270,973	\$0
Construction	\$2,790,646	\$2,790,646	\$0
Construction Mgmt	\$388,300	\$388,300	\$0
Consultants	\$671	\$671	\$0
Project Total:	\$3,450,590	\$3,450,590	\$0

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4																																												
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Projector, Aiphone (including strike) at the SPE, cafeteria sound system & murals, Outdoor Furniture, Facilities Equipment, Projectors, Label Maker, Facilities Equipment, Murals

BUDGET

\$100,000

IN PROGRESS

Laminator, Portable PA, Microphone

MUSIC

SCOPE

COMPLETE

308 Instruments Delivered

TECHNOLOGY

COMPLETE

336 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Panther Run Elementary School



Address: 801 NW 172 AVENUE, PEMBROKE PINES 33029
 Location Num: 3571
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$3,986,929
 Total Facilities Budget (Sum of Projects): \$3,531,930

PRIMARY RENOVATIONS P.002069 Panther Run ES - SMART Program Renovations

CURRENT PHASE

9-Closed

RISK LEVEL

No Risk

PROJECT UPDATE

PROJECT SCOPE

HVAC Improvement, Controls, Chiller Pumps. Re-roofing: Buildings 1 & 3 Joint Sealant Repair and Brick Restoration

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$126,477	\$126,477	\$0
Construction	\$2,369,226	\$2,369,226	\$0
Direct Purchase	\$514,022	\$514,022	\$0
Construction Mgmt	\$423,827	\$391,927	\$31,900
Contingency	\$95,428		\$95,428
Consultants	\$2,950	\$2,950	\$0
Project Total:	\$3,531,930	\$3,404,602	\$127,328

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4																																												
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Two-way radios, Aiphone, TV, ActivPanels promethean boards, Digital marquee, laptops, desktops, Recordex, TV wall mount, Portable PA, Printers, Apple Computer Accessories

BUDGET

\$100,000

IN PROGRESS

Audio Visual parts, Portable PA

MUSIC

SCOPE

COMPLETE 272 Instruments Delivered

TECHNOLOGY

SCOPE

COMPLETE 213 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Pembroke Lakes Elementary School



Address: 11251 TAFT STREET, PEMBROKE PINES 33026
 Location Num: 2661
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$5,236,857
 Total Facilities Budget (Sum of Projects): \$4,911,900

PRIMARY RENOVATIONS P.001842 Pembroke Lakes ES - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

5B-Construction



PROJECT UPDATE

1. GC/HVAC Sub connected Temporary Cooling Unit to existing ductwork for AHU-7 and started operations. 2. GC/HVAC Sub demolished original AHU-7 and removed debris from room. 3. GC poured new concrete housekeeping pad for new AHU-7. 4. GC/HVAC Sub install new AHU-7 included chilled-water piping, ductwork, electrical & partially completed the control wiring. 4. GC/Elect Sub continued Fire Alarm device installation during this period. 5. GC/Elect Sub continued installation of the new Main Fire Panel during this period.

PROJECT SCOPE

Restroom Renovations: ADA Restrooms #151 (Female) & #152 (Male) Aluminum Walkway Repairs New Fire Alarm System Mechanical Improvements: Buildings 1 (10 AHU, 10 Duct heaters, 2 Gravity vents, 2 CHW circulation pumps, 1 MAU, & 1 KEF), 2 (2 Gravity Ventilators) Kitchen Work (Electrical, HVAC ductwork & Ceiling)

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$258,056	\$218,445	\$39,611
Construction	\$1,701,497	\$1,228,347	\$473,150
FF&E and Technology	\$70,458	\$69,875	\$583
Direct Purchase	\$166,820	\$135,565	\$31,255
Construction Mgmt	\$366,669	\$366,669	\$0
Contingency	\$84,900		\$84,900
Consultants	\$8,500	\$2,152	\$6,348
Project Total:	\$2,656,900	\$2,021,053	\$635,847

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4																																												
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Pines Middle School



Address: 200 NW DOUGLAS ROAD, PEMBROKE PINES 33024
 Location Num: 1881
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$1,163,728
 Total Facilities Budget (Sum of Projects): \$701,730

PRIMARY RENOVATIONS P.002130 Pines MS - SMART Program Renovations

CURRENT PHASE

6-Substantial Completion

RISK LEVEL

No Risk

PROJECT UPDATE

Project is complete! The 110b was submitted to the Building Department and has been fully executed

PROJECT SCOPE

Installing a new roof on Building 6 including removing and reinstalling the existing mechanical equipment. Test and balance the air handling systems in Buildings 5 & 11.

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$43,500	\$34,918	\$8,582
Construction	\$553,577	\$490,181	\$63,396
Direct Purchase	\$26,546		\$26,546
Construction Mgmt	\$50,602	\$49,722	\$880
Contingency	\$25,804		\$25,804
Consultants	\$1,701	\$1,701	\$0
Project Total:	\$701,730	\$576,522	\$125,208

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4																																												
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Generator, Traffic cones, Golf carts, Micro scrubber, Signage, Athletic equipment, Morning show equipment, Chairs, Microphones, TVs, Projectors, Signage, Chair, Scores Table & Gym chairs, Tables, ThinkStation, Desktops, Laptop wiring, Thinkpads

BUDGET

\$100,000

IN PROGRESS

ThinkPads

MUSIC

SCOPE

COMPLETE 124 Instruments Delivered

TECHNOLOGY

SCOPE

COMPLETE 603 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Sea Castle Elementary School



Address: 9600 MIRAMAR BOULEVARD, MIRAMAR 33025
 Location Num: 2871
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$4,767,829
 Total Facilities Budget (Sum of Projects): \$4,319,154

PRIMARY RENOVATIONS P.001632 Sea Castle ES - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

5B-Construction



PROJECT UPDATE

Working on getting the additional fire alarm devices and in getting resolution for fans added through ASI. * A/E Notice to Cure - A/E delays in not willing to process CCD for additional Scope - A/E refuses to sign ATP because to don't agree with the sum BLD 5 Environmental Report - deficiencies in systems and maintenance that could contribute to decreased indoor air quality.

PROJECT SCOPE

HVAC Improvements inclusive of (42) FCUs, (9) AHUs, and RTU replacements, Campus-wide Fire Alarm Replacement, Building Envelope Improvements inclusive of reroofing of bldg. 80 and exterior painting, ADA chair lift installation.

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$287,252	\$273,155	\$14,097
Construction	\$3,100,350	\$3,045,134	\$55,216
FF&E and Technology	\$890	\$890	\$0
Direct Purchase	\$309,354	\$308,883	\$471
Construction Mgmt	\$468,202	\$442,178	\$26,024
Contingency	\$139,606		\$139,606
Consultants	\$13,500	\$6,004	\$7,496
Project Total:	\$4,319,154	\$4,076,244	\$242,910

FLAG: SCHEDULE, Reason: Owner Delays

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4																																												
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Furniture, office furniture, digital marquee, shade structure, science tables, projector, cafeteria sound system, laptops chargers, High Back Executive Chair

BUDGET

\$100,000

MUSIC

✓ **SCOPE**
COMPLETE 131 Instruments Delivered

TECHNOLOGY

✓ **SCOPE**
COMPLETE 420 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Silver Lakes Elementary School



Address: 2300 SW 173 AVENUE, MIRAMAR 33029
 Location Num: 3371
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$2,788,779
 Total Facilities Budget (Sum of Projects): \$2,252,383

PRIMARY RENOVATIONS P.002009 Silver Lakes ES - SMART Program Renovations

CURRENT PHASE

9-Closed

RISK LEVEL

No Risk

PROJECT UPDATE

PROJECT SCOPE

Building Envelope Improvements (Roof, Window, Ext Wall, etc.), HVAC Improvements

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$162,736	\$162,736	\$0
Construction	\$1,636,846	\$1,636,846	\$0
Direct Purchase	\$218,873	\$218,873	\$0
Construction Mgmt	\$233,928	\$233,928	\$0
Project Total:	\$2,252,383	\$2,252,383	\$0

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4																																												
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

New Pre k-2 playground with shade and PIP surfacing

BUDGET

\$100,000

IN PROGRESS

MUSIC

SCOPE

COMPLETE 634 Instruments Delivered

TECHNOLOGY

SCOPE

COMPLETE 260 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Silver Palms Elementary School



Address: 1209 NW 155 AVENUE, PEMBROKE PINES 33028
 Location Num: 3491
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$4,149,285
 Total Facilities Budget (Sum of Projects): \$3,616,400

PRIMARY RENOVATIONS P.002146 Silver Palms ES - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

8-Financial Closeout

No Risk

PROJECT UPDATE

The Architect has a balance of Allowances/Supplemental Services and a Closeout Purchase Order request was sent for them to reply with a closeout date which they did not respond to. To ensure that this was not an oversight on their behalf a second comment was submitted and an email to ensure the balance could be cleared from the budget awaiting their response. At this time no change to the phase will be made.

PROJECT SCOPE

Site: Cleaning and unclogging drainage of the existing aluminum walkway covers. Re-roofing: Buildings 1, 2, and 75. HVAC improvement: Buildings 1, 2, and 75. Exterior Stucco Replacement: Building 75. Exterior Painting: Building 75.

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$150,000	\$117,093	\$32,907
Construction	\$2,702,367	\$2,702,382	(\$15)
Direct Purchase	\$187,866	\$187,609	\$257
Construction Mgmt	\$434,000	\$434,000	\$0
Contingency	\$141,873		\$141,873
Consultants	\$294	\$294	\$0
Project Total:	\$3,616,400	\$3,441,378	\$175,022

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4																																												
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Retrofitting the existing digital marquee , school beautification; media center/ school Improvements furniture, Shade Structure, Printers, Projectors

BUDGET

\$100,000

IN PROGRESS

Mircophone System

MUSIC

SCOPE

COMPLETE 205 Instruments Delivered

TECHNOLOGY

SCOPE

COMPLETE 306 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Silver Shores Elementary School



Address: 1701 SW 160 AVENUE, MIRAMAR 33027
 Location Num: 3581
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$2,610,522
 Total Facilities Budget (Sum of Projects): \$2,265,560

PRIMARY RENOVATIONS P.001906 Silver Shores ES - SMART Program Renovations

CURRENT PHASE

9-Closed

RISK LEVEL

No Risk

PROJECT UPDATE

PROJECT SCOPE

Building Envelope Improvements (Roof, Window, Ext Wall, etc.), HVAC Improvements

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$148,840	\$148,839	\$1
Construction	\$1,804,496	\$1,804,496	\$0
Construction Mgmt	\$271,800	\$249,211	\$22,589
Contingency	\$40,424		\$40,424
Project Total:	\$2,265,560	\$2,202,546	\$63,014

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4																																												
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Student laptops, classroom furniture, furniture for computer lab and related arts, electric strike and proximity pad, Shades & Student furniture for the media center, Computer Accessories, Think Center

BUDGET

\$100,000

IN PROGRESS

Think Center

MUSIC

SCOPE

✓ COMPLETE 155 Instruments Delivered

TECHNOLOGY

SCOPE

✓ COMPLETE 202 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Silver Trail Middle School



Address: 18300 SHERIDAN STREET, PEMBROKE PINES 33331
 Location Num: 3331
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$7,653,149
 Total Facilities Budget (Sum of Projects): \$6,808,150

PRIMARY RENOVATIONS P.001406 Silver Trail MS - SMART GOB Renovations

CURRENT PHASE

RISK LEVEL

7-Final Completion



PROJECT UPDATE

The General Contractor tax reconciliation was submitted and the amount concords with the remaining commitments of their budget. The Time Impact analysis documents were sent to the Architect and are in their court for review.

PROJECT SCOPE

Building Envelope Improvements inclusive of reroofing of Buildings 2 and 3, HVAC Improvements are inclusive of the replacement of heat pump AHUs, cooling towers, and exhaust fans.

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$480,230	\$469,109	\$11,121
Construction	\$4,470,398	\$4,431,007	\$39,391
Direct Purchase	\$481,200	\$481,200	\$0
Construction Mgmt	\$651,456	\$651,456	\$0
Contingency	\$110,866		\$110,866
Consultants	\$9,000		\$9,000
Project Total:	\$6,203,150	\$6,032,772	\$170,378

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4																																												
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Whispering Pines Education Center



Address: 3609 SW 89TH AVENUE, MIRAMAR 33025
 Location Num: 1752
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$5,599,046
 Total Facilities Budget (Sum of Projects): \$4,849,580

PRIMARY RENOVATIONS P.002089 Whispering Pines Education Center - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

5B-Construction



PROJECT UPDATE

1. Demo and install AHU building 5. 2. Excavation of trench and connection of U/G piping inspection passed. 3. Roofs completed building 2,3,4,5.

PROJECT SCOPE

Exterior Stucco Painting: Buildings 1, 2 & 3 Exterior Stucco Repair: Buildings 1, 2 & 3 Fire Alarm System: Campus-wide Fire Sprinklers: Building 2 Fire Main for New Fire Sprinkler System HVAC Improvements: Buildings 1 & 2 Reroofing: Covered Walkway, Buildings 1, 2 & 3 Test & Balance: Buildings 1, 2 & 3

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$237,000	\$182,407	\$54,593
Construction	\$3,726,109	\$886,650	\$2,839,459
Direct Purchase	\$192,539	\$39,755	\$152,784
Construction Mgmt	\$464,000	\$459,000	\$5,000
Contingency	\$209,432		\$209,432
Consultants	\$14,410	\$8,441	\$5,969
Utilities	\$6,090		\$6,090
Project Total:	\$4,849,580	\$1,576,253	\$3,273,327

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4																																												
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

K-2 sand replacement with PIP, Media Center Furniture

BUDGET

\$100,000

IN PROGRESS

Media Center Furniture, PIP

MUSIC

✓ COMPLETE

SCOPE

No Program

TECHNOLOGY

✓ COMPLETE

SCOPE

No Items

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Sunset Lakes Elementary School



Address: 18400 SW 25 STREET, MIRAMAR 33027
 Location Num: 3661
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$3,235,007
 Total Facilities Budget (Sum of Projects): \$2,799,009

PRIMARY RENOVATIONS P.001971 Sunset Lakes ES - SMART Program Renovations

CURRENT PHASE

9-Closed

RISK LEVEL

No Risk

PROJECT UPDATE

PROJECT SCOPE

Building Envelope Improvements (Roof, Window, Ext Wall, etc.), HVAC Improvements

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$91,778	\$91,778	\$0
Construction	\$1,959,145	\$1,959,145	\$0
Direct Purchase	\$452,083	\$452,083	\$0
Construction Mgmt	\$296,003	\$296,003	\$0
Project Total:	\$2,799,009	\$2,799,009	\$0

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4																																												
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

New PreK-2 playground, shades for 3-5 play area & fencing to separate the two play areas

BUDGET

\$100,000

IN PROGRESS

MUSIC

SCOPE

COMPLETE 228 Instruments Delivered

TECHNOLOGY

SCOPE

COMPLETE 549 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Sunshine Elementary School



Address: 7737 W LASALLE BOULEVARD, MIRAMAR 33023
 Location Num: 1171
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$4,382,232
 Total Facilities Budget (Sum of Projects): \$3,948,449

PRIMARY RENOVATIONS P.002079 Sunshine ES - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

5B-Construction



PROJECT UPDATE

The Contractor this period has made HVAC advancements in Building No. 14 replacing both AHUs. Ongoing work continues with demolition of Building No. 03 and replacement of the FA Control Panel.

PROJECT SCOPE

Fire Alarm Panel Replacement HVAC Improvements: Buildings 1 (AHU, Controls, & Distribution System), 2 (Exhaust Fan), 4 (Backdraft Dampers)8 (Exhaust Fan), 9 (Exhaust Fans, & HVAC Controls), & 14 (Exhaust Fan). Demolish Building: Building 3 (Bid alternate 1). Roofing Roof: Building 4, 10, 11, and 13. Fire Sprinkler System: Building 4. Building Expansion Joint Replacement: Building 4.

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$158,000	\$130,443	\$27,557
Construction	\$3,245,349	\$2,280,846	\$964,503
FF&E and Technology	\$5,104		\$5,104
Direct Purchase	\$104,459	\$104,459	\$0
Construction Mgmt	\$264,090	\$262,490	\$1,600
Contingency	\$148,599		\$148,599
Consultants	\$20,848	\$11,910	\$8,938
Utilities	\$2,000		\$2,000
Project Total:	\$3,948,449	\$2,790,148	\$1,158,301

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4																																												
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Poster maker, headphones, laminator, classrooms rugs, portable blowers, laptops, Earthwalk cart, staff desktop, student desktop, student chairs, shelving, bookcase, pro pencil sharpeners, Ellison machine, Recordex, Athletic Equipment, Indoor Furniture, Projectors

BUDGET

\$100,000

IN PROGRESS

Projectors

MUSIC

✓ COMPLETE

SCOPE

438 Instruments Delivered

TECHNOLOGY

✓ COMPLETE

SCOPE

335 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Walter C. Young Middle School



Address: 901 NW 129 AVENUE, PEMBROKE PINES 33028
 Location Num: 3001
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$16,569,553
 Total Facilities Budget (Sum of Projects): \$15,885,560

PRIMARY RENOVATIONS P.002010 Walter C. Young MS - SMART Program Renovations

CURRENT PHASE

6-Substantial Completion

RISK LEVEL

No Risk

PROJECT UPDATE

CMAR is preparing to submit the complete closeout package. Trade Deficiency list has been issued by the Building Department 110b has been executed by the Superintendent.

PROJECT SCOPE

Re-roofing: Buildings 1 - 14 Window & Door Replacements: Buildings 10 & 16 HVAC Improvements: Buildings 1 - 13 Electrical Improvements (HVAC related): Buildings 1 - 13 Painting: Buildings 1 - 3, 6 - 10, 13, 16

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$675,000	\$578,636	\$96,364
Construction	\$11,066,443	\$10,186,289	\$880,154
Direct Purchase	\$1,907,370	\$1,742,566	\$164,804
Construction Mgmt	\$1,548,700	\$1,548,700	\$0
Contingency	\$645,047		\$645,047
Consultants	\$25,000	\$17,837	\$7,163
Utilities	\$18,000		\$18,000
Project Total:	\$15,885,560	\$14,074,028	\$1,811,532

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4																																												
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Golf Cart/3 repairs, cafeteria tables, TVs for Exceptional Student Ed. Program upgrades, Printers, Facilities/Janitorial equipment, technology items, two-way radios, vertical blinds, carpet in room 925, repair dinner theater bleachers, and LCD projectors, Murals, Headphones, Chairs

BUDGET

\$100,000

IN PROGRESS

Chairs

MUSIC

✓ COMPLETE **SCOPE**

125 Instruments Delivered

TECHNOLOGY

✓ COMPLETE **SCOPE**

654 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

West Broward High School



Address: 500 NW 209 AVENUE, PEMBROKE PINES 33029
 Location Num: 3971
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$2,016,394
 Total Facilities Budget (Sum of Projects): \$49,764

PRIMARY RENOVATIONS P.002087 West Broward HS - SMART HVAC Improvements

CURRENT PHASE

9-Closed

RISK LEVEL

No Risk

PROJECT UPDATE

PROJECT SCOPE

HVAC Improvements

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4																																												
PROJECT PLANNING																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Athletic equipment, CDs/DVDs, projectors, picnic benches, Black Magic Studio system, auditorium sound system, floor mats and wall wraps

BUDGET

\$100,000

ATHLETICS

COMPLETE

SCOPE

Track, Weight Room

MUSIC

COMPLETE


SCOPE

238 Instruments Delivered

COMPLETE

SCOPE

773 Items Delivered

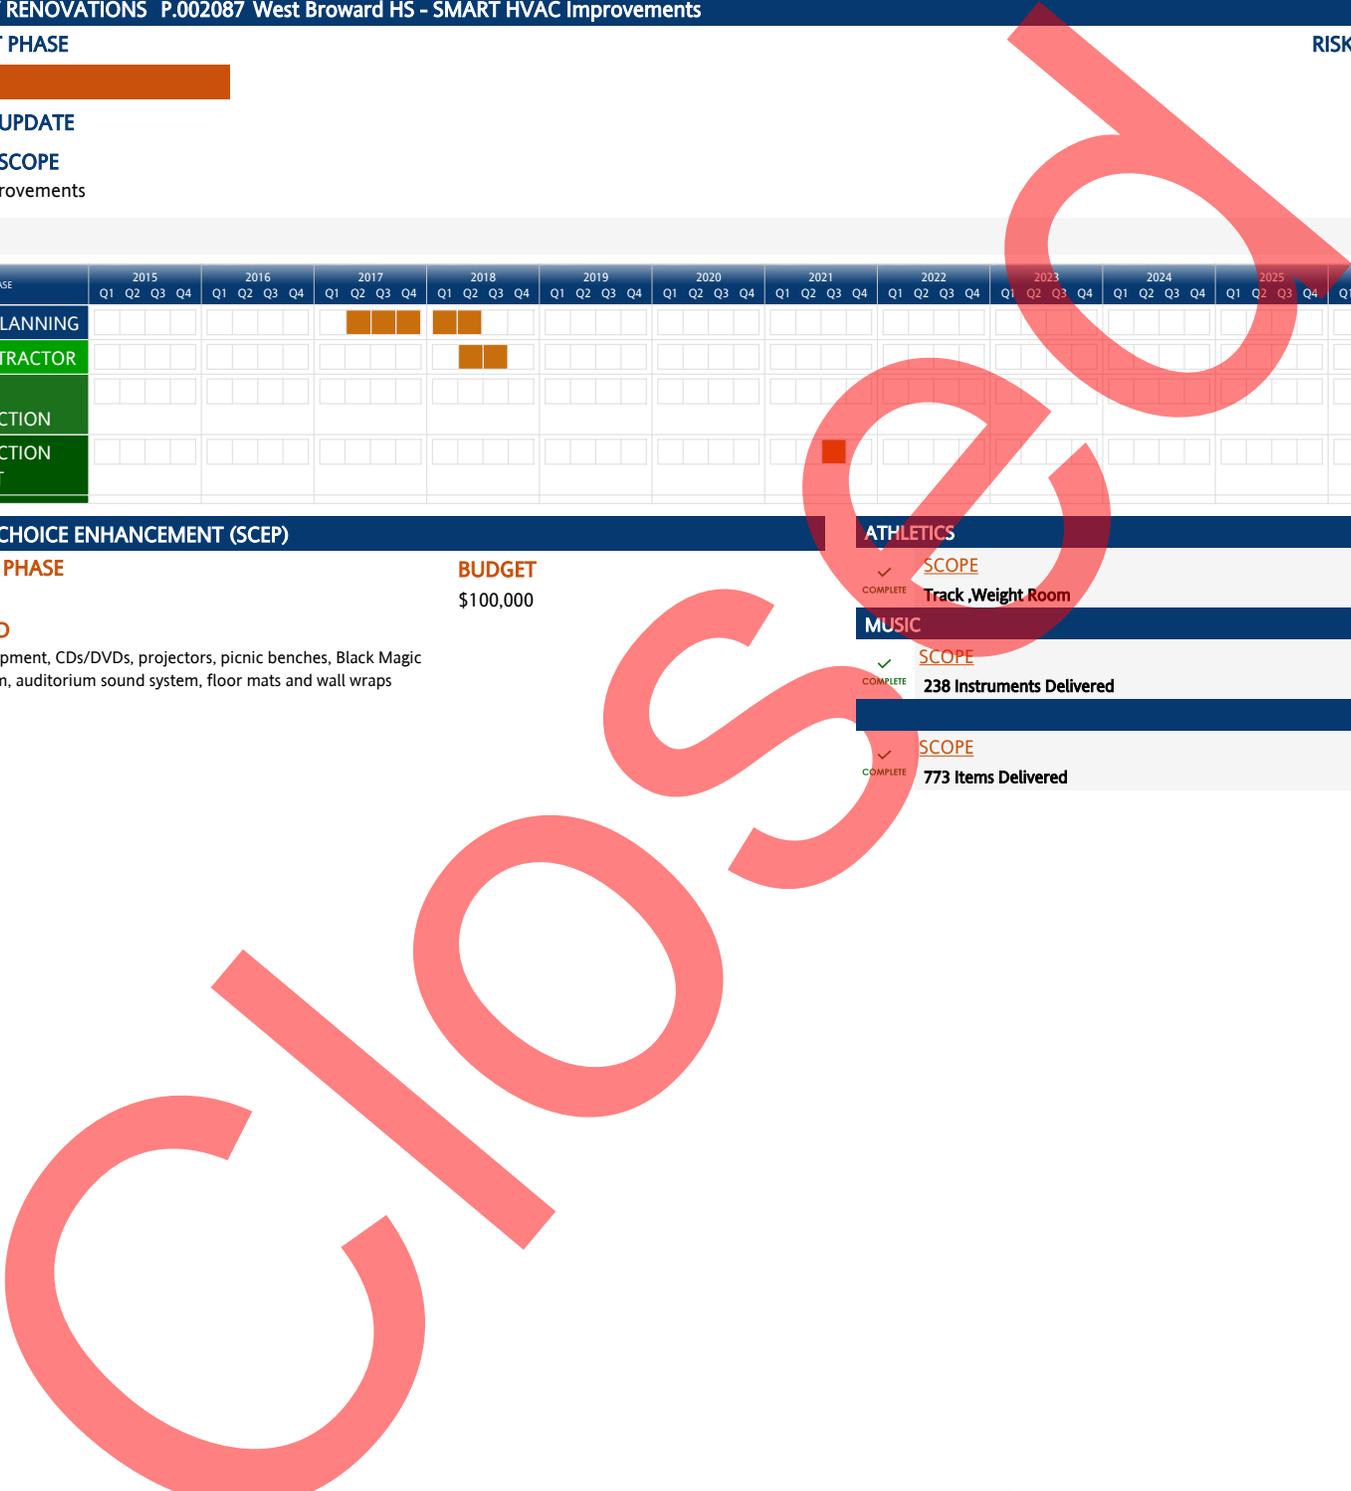

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Whispering Pines Education Center



Address: 3609 SW 89TH AVENUE, MIRAMAR 33025
 Location Num: 1752
 Board District: 2
 Board Member: Torey Alston
 ADEFP Budget: \$5,599,046
 Total Facilities Budget (Sum of Projects): \$4,849,580

PRIMARY RENOVATIONS P.002089 Whispering Pines Education Center - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

5B-Construction



PROJECT UPDATE

1. Demo and install AHU building 5. 2. Excavation of trench and connection of U/G piping inspection passed. 3. Roofs completed building 2,3,4,5.

PROJECT SCOPE

Exterior Stucco Painting: Buildings 1, 2 & 3 Exterior Stucco Repair: Buildings 1, 2 & 3 Fire Alarm System: Campus-wide Fire Sprinklers: Building 2 Fire Main for New Fire Sprinkler System HVAC Improvements: Buildings 1 & 2 Reroofing: Covered Walkway, Buildings 1, 2 & 3 Test & Balance: Buildings 1, 2 & 3

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$237,000	\$182,407	\$54,593
Construction	\$3,726,109	\$886,650	\$2,839,459
Direct Purchase	\$192,539	\$39,755	\$152,784
Construction Mgmt	\$464,000	\$459,000	\$5,000
Contingency	\$209,432		\$209,432
Consultants	\$14,410	\$8,441	\$5,969
Utilities	\$6,090		\$6,090
Project Total:	\$4,849,580	\$1,576,253	\$3,273,327

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4																																												
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

K-2 sand replacement with PIP, Media Center Furniture

BUDGET

\$100,000

IN PROGRESS

Media Center Furniture, PIP

MUSIC

✓ COMPLETE

SCOPE

No Program

TECHNOLOGY

✓ COMPLETE

SCOPE

No Items

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.
