



 **SMART** INVESTMENTS
LEAD TO SMART STUDENTS.



MUNICIPAL REPORT

For The Quarter Ending
September 30, 2023 | FY24 Q1



Established 1915

BROWARD
County Public Schools

PREFACE

We are pleased to present the updated Broward County Public Schools (BCPS) **School Spotlight** editions specifically designed for city administrators, city commissioners, council-representatives and Broward County School Board Members.

The School Spotlight is a quarterly report that details the progress of facilities projects at each of the 232 schools participating in the SMART Bond Program. This “City Edition” of The School Spotlight provides a municipal breakdown of all approved renovation projects, projected costs, School Choice Enhancement Program initiatives and other ongoing or scheduled SMART Program projects.

These easy-to-read School Spotlights allow board members and city officials to better follow the progress of the facilities improvements within specific municipalities. The Spotlights will be updated every quarter to help city officials and school board members share timely information with business groups, community organizations, homeowners’ associations and other key constituents as ongoing SMART Program projects continue to progress.

SMART (**S**afety, **M**usic & **A**rt, **A**thletics, **R**enovation and **T**echnology) is the **\$800 million capital improvement** program to upgrade existing school facilities and to purchase new computer technology, athletic equipment and musical instruments to enhance the learning experience of Broward County students.

Boyd H. Anderson High School



Address: 3050 NW 41 STREET, LAUDERDALE LAKES 33309
 Location Num: 1741
 Board District: 5
 Board Member: Dr. Jeff Holness
 ADEFP Budget: \$12,820,525
 Total Facilities Budget (Sum of Projects): \$12,162,404

PRIMARY RENOVATIONS P.001360 Boyd Anderson HS - Media Ctr Remodeling

CURRENT PHASE

9-Closed

RISK LEVEL

No Risk

PROJECT UPDATE

PROJECT SCOPE


Renovation of the existing Media Center including select demolition, removal of existing interior stair, new interior wall, etc.

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$190,112	\$190,112	\$0
Construction	\$914,543	\$914,543	\$0
FF&E and Technology	\$181,090	\$181,090	\$0
Direct Purchase	\$33,769	\$33,769	\$0
Construction Mgmt	\$222,017	\$222,017	\$0
Consultants	\$28,770	\$28,770	\$0
Project Total:	\$1,570,301	\$1,570,301	\$0

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING	■																																															
HIRE DESIGNER	■																																															
PROJECT DESIGN	■																																															
HIRE CONTRACTOR					■	■																																										
ACTIVE CONSTRUCTION						■	■	■																																								
CONSTRUCTION CLOSEOUT									■	■	■	■	■	■	■	■																																

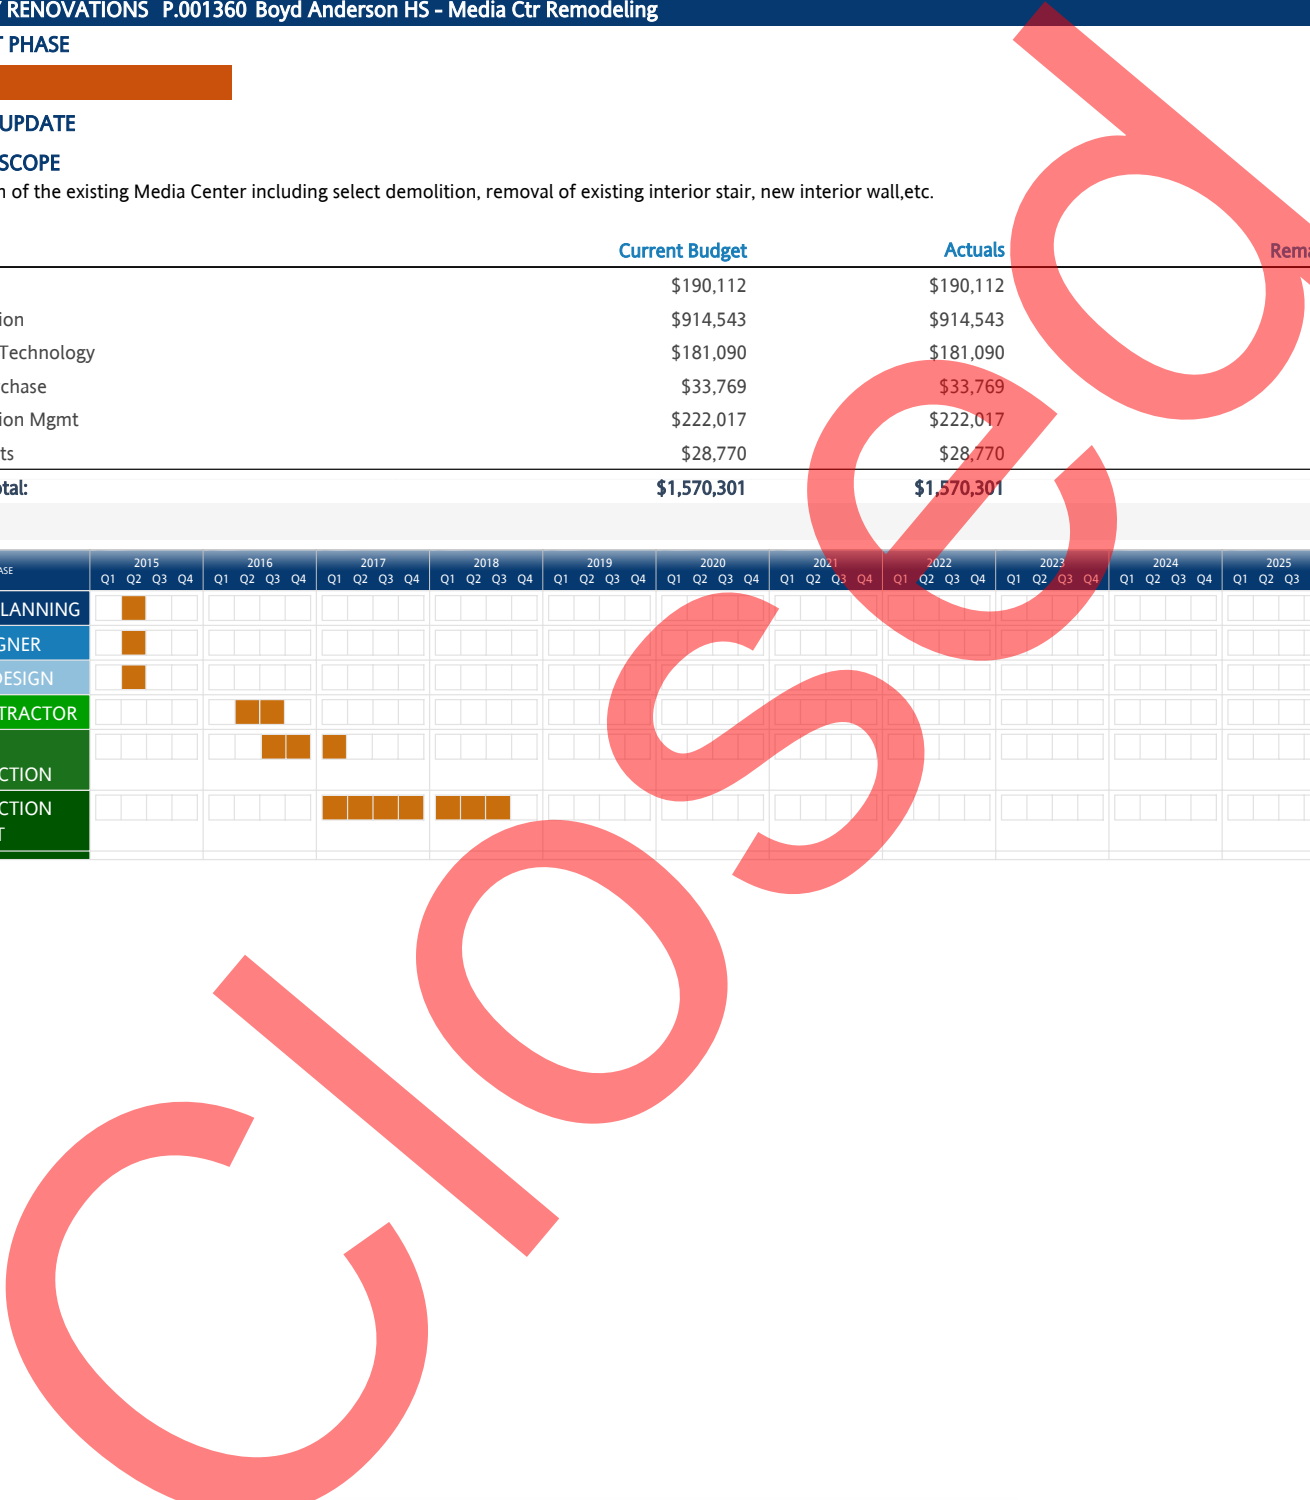

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Boyd H. Anderson High School



Address: 3050 NW 41 STREET, LAUDERDALE LAKES 33309
 Location Num: 1741
 Board District: 5
 Board Member: Dr. Jeff Holness
 ADEFP Budget: \$12,820,525
 Total Facilities Budget (Sum of Projects): \$12,162,404

PRIMARY RENOVATIONS P.001846 Boyd H. Anderson HS - SMART Program Renovation

CURRENT PHASE

RISK LEVEL

5B-Construction



PROJECT UPDATE

Building 1, 2: Interior renovations completed. Campus-wide Roofing: Curbs and ARBS metal is being installed on the rooftop in preparation of the placement of light weight concrete.

PROJECT SCOPE

Roofing: Buildings 1, 2, 3, 6, 8, 9, 10, 11, 12 & 13 ADA Restroom Renovations: Building 1: Rooms 102H, 102J, 106, and 166, and Building 2: Rooms 291 and 292 STEM Lab Renovations: Building 1: Business Technology Center (Rooms 223, 224, 225, and 227) and Aviation (Room 194) and Building 2: Health and Wellness (Room 2001 and 2002). 4) Safety and Security Upgrade: Exit Signs in - Buildings 1, 5, and 6

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$486,160	\$460,740	\$25,420
Construction	\$7,673,655	\$4,410,771	\$3,262,884
FF&E and Technology	\$196,177	\$191,382	\$4,795
Direct Purchase	\$1,173,480	\$443,165	\$730,315
Construction Mgmt	\$1,029,000	\$1,029,000	\$0
Consultants	\$33,631	\$25,270	\$8,361
Project Total:	\$10,592,103	\$6,560,328	\$4,031,775

FLAG: BUDGET, Reason: Budget Adjustment

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Recordex, Sound system for the Gymnasium, Laptop cart with 30 laptops, Portable sound system, Roof for visitor's dugout, lockers, Golf carts and Gym wall pads.

BUDGET

\$100,000

ATHLETICS

✓ COMPLETE SCOPE
Weight Room

MUSIC

✓ COMPLETE SCOPE
284 Instruments Delivered

TECHNOLOGY

✓ COMPLETE SCOPE
580 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Lauderdale Lakes Middle School



Address: 3911 NW 30 AVENUE, LAUDERDALE LAKES 33309
 Location Num: 1701
 Board District: 5
 Board Member: Dr. Jeff Holness
 ADEFP Budget: \$8,468,146
 Total Facilities Budget (Sum of Projects): \$8,102,170

PRIMARY RENOVATIONS P.001637 Lauderdale Lakes MS - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

5B-Construction



PROJECT UPDATE

- A meeting was done with PMOR/GC/Building Department Chief and Building Department Inspector to clarify deficiency list presented by the inspector and get the pending inspections closed. Additional information was requested from the GC and documents were sent to Senior Building Inspector for his review and approval. - Mechanical final inspection was closed. - PMOR worked with GC to obtain additional documents requested by BCPS Legal for the PCO 20, before it is presented to the Board. - PCO 20: Final Change order for the 1% Bond money from all previous change orders for Bonded subs & GC, was approved by CORP. BCPS lawyer asked for additional information from the GC before presenting to the Board.

PROJECT SCOPE

Fire Alarm: Building 1, 2, 3, & 4 Fire Sprinklers: Building 1 Media Center Improvements: Building 1 Re-Roofing: Building 1, 2, 3, & 4 Stucco, Waterproofing, and Interior Repairs: Building 1 HVAC System Replacement: Building 1 & 2 Test & Balance: Building 1 & 2

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$433,718	\$416,385	\$17,333
Construction	\$5,482,997	\$5,319,140	\$163,857
FF&E and Technology	\$101,138	\$89,147	\$11,991
Direct Purchase	\$581,427	\$581,427	\$0
Construction Mgmt	\$700,000	\$590,000	\$110,000
Consultants	\$122,390	\$106,894	\$15,496
Project Total:	\$7,421,670	\$7,102,993	\$318,677

FLAG: SCHEDULE, Reason:Owner Delays/Errors and Omissions

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Park Lakes Elementary School



Address: 3925 NORTH STATE ROAD 7, LAUDERDALE LAKES 33319
 Location Num: 3761
 Board District: 5
 Board Member: Dr. Jeff Holness
 ADEFP Budget: \$1,315,892
 Total Facilities Budget (Sum of Projects): \$732,377

PRIMARY RENOVATIONS P.001988 Park Lakes ES - SMART Program Renovations

CURRENT PHASE

8-Financial Closeout

RISK LEVEL

No Risk

PROJECT UPDATE

Financial Closeout, all POs are being closed out.

PROJECT SCOPE

Art and Music Room Renovations: Building 1 Roof Replacement: Buildings 78 & 80 Equipment Rooftop Tie-downs: Building 1, 2, & 4.

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$72,268	\$72,268	\$0
Construction	\$461,842	\$461,842	\$0
FF&E and Technology	\$82,165	\$81,714	\$451
Construction Mgmt	\$116,102	\$116,102	\$0
Project Total:	\$732,377	\$731,926	\$451

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Outdoor Benches, digital marquee & K-2 & 3-5 playground structures

BUDGET

\$100,000

MUSIC

✓ COMPLETE

SCOPE

208 Instruments Delivered

TECHNOLOGY

✓ COMPLETE

SCOPE

633 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.
