



 **SMART** INVESTMENTS
LEAD TO SMART STUDENTS.



MUNICIPAL REPORT

For The Quarter Ending
September 30, 2023 | FY24 Q1



Established 1915

BROWARD
County Public Schools

PREFACE

We are pleased to present the updated Broward County Public Schools (BCPS) **School Spotlight** editions specifically designed for city administrators, city commissioners, council-representatives and Broward County School Board Members.

The School Spotlight is a quarterly report that details the progress of facilities projects at each of the 232 schools participating in the SMART Bond Program. This “City Edition” of The School Spotlight provides a municipal breakdown of all approved renovation projects, projected costs, School Choice Enhancement Program initiatives and other ongoing or scheduled SMART Program projects.

These easy-to-read School Spotlights allow board members and city officials to better follow the progress of the facilities improvements within specific municipalities. The Spotlights will be updated every quarter to help city officials and school board members share timely information with business groups, community organizations, homeowners’ associations and other key constituents as ongoing SMART Program projects continue to progress.

SMART (**S**afety, **M**usic & **A**rt, **A**thletics, **R**enovation and **T**echnology) is the **\$800 million capital improvement** program to upgrade existing school facilities and to purchase new computer technology, athletic equipment and musical instruments to enhance the learning experience of Broward County students.

Lake Forest Elementary School



Address: 3550 SW 48 AVENUE, PEMBROKE PARK 33023
 Location Num: 0831
 Board District: 1
 Board Member: Daniel P. Foganholi
 ADEFP Budget: \$3,923,117
 Total Facilities Budget (Sum of Projects): \$3,542,155

PRIMARY RENOVATIONS P.001484 Lake Forest ES - Repair Roof on Bldg 4

CURRENT PHASE

9-Closed

RISK LEVEL

No Risk

PROJECT UPDATE

PROJECT SCOPE


Re-roof of Building #4 in accordance with all applicable Codes and Standards.

BUDGET

	Current Budget	Actuals	Remaining Budget
Construction	\$279,249	\$279,249	\$0
Direct Purchase	\$56,945	\$56,945	\$0
Construction Mgmt	\$34,800	\$34,800	\$0
Project Total:	\$370,994	\$370,994	\$0

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING	■																																															
ACTIVE CONSTRUCTION	■	■	■	■	■	■	■	■																																								

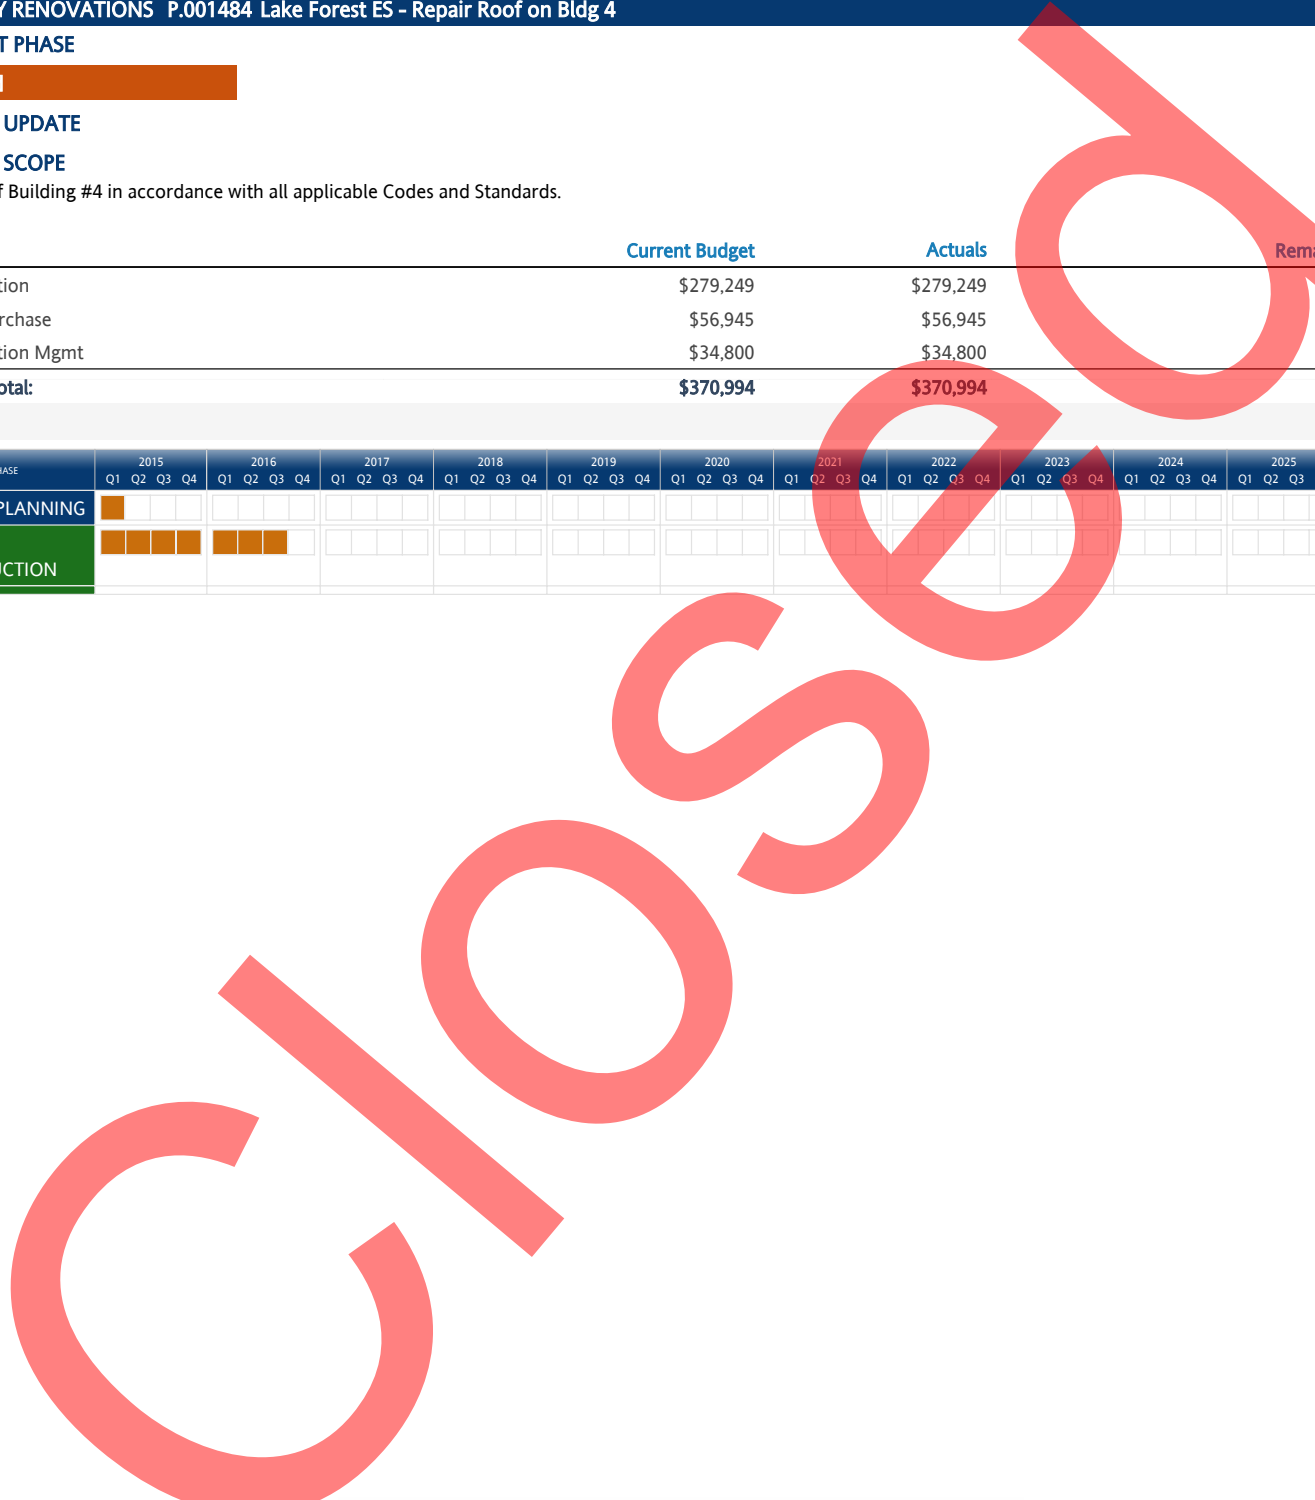

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Lake Forest Elementary School



Address: 3550 SW 48 AVENUE, PEMBROKE PARK 33023
 Location Num: 0831
 Board District: 1
 Board Member: Daniel P. Foganholi
 ADEFP Budget: \$3,923,117
 Total Facilities Budget (Sum of Projects): \$3,542,155

PRIMARY RENOVATIONS P.001886 Lake Forest ES - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

6-Substantial Completion



PROJECT UPDATE

The Construction Project Manager is processing PCO 11, that is cleared to go to Pre Corp.

PROJECT SCOPE

Reroofing: Buildings 01, 03, 05, 06, 07, 09, 10, & 13 HVAC Improvements: Controls, Condenser Units and Air Handlers to Buildings 01, 03, 04, 05, 06, & 07

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$304,979	\$295,833	\$9,146
Construction	\$2,181,440	\$1,986,637	\$194,803
Direct Purchase	\$197,031	\$195,530	\$1,501
Construction Mgmt	\$412,666	\$412,666	\$0
Contingency	\$67,744		\$67,744
Consultants	\$3,840		\$3,840
Utilities	\$3,461		\$3,461
Project Total:	\$3,171,161	\$2,890,666	\$280,495

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Projector, Cafeteria projection system, Teacher chairs, Blinds, Studio equipment, Office chairs, Traffic cones, Cone bars, Cone cart, Single cassette recorders, Headphones, Stools, Safety cones, Portable cooler, Canopy, Digital scanner, Desktops, Computer mice, Tablet, Benches/tables, Blinds, Web cams, Projector, Sanitizing electrostatic sprayer, Earthwalk Cart, Radio Accessories, Book cases, Two-Way Radios

BUDGET

\$100,000

IN PROGRESS

Two-Way Radios, Book cases

MUSIC

SCOPE

COMPLETE 608 Instruments delivered

TECHNOLOGY

SCOPE

COMPLETE 456 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

Watkins Elementary School



Address: 3520 SW 52 AVENUE, PEMBROKE PARK 33023
 Location Num: 0511
 Board District: 1
 Board Member: Daniel P. Foganholi
 ADEFP Budget: \$3,443,840
 Total Facilities Budget (Sum of Projects): \$2,998,912

PRIMARY RENOVATIONS P.002074 Watkins ES - SMART Program Renovations

CURRENT PHASE

9-Closed

RISK LEVEL

No Risk

PROJECT UPDATE

PROJECT SCOPE

Re-Roofing of Buildings 1 & 2. Painting of Buildings 1 & 2.

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$84,364	\$84,364	\$0
Construction	\$2,168,435	\$2,168,435	\$0
Direct Purchase	\$356,473	\$356,473	\$0
Construction Mgmt	\$387,922	\$339,942	\$47,980
Consultants	\$1,718	\$1,718	\$0
Project Total:	\$2,998,912	\$2,950,932	\$47,980

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Laptops, Digital Marquee, Printers, Document Cameras, Projectors, Indoor Furniture, Two-Way Radios, Morning Show Equipment

BUDGET

\$100,000

IN PROGRESS

Document Cameras, Projectors, Indoor Furniture, Morning Show Equipment, Printer Package, Radios

TECHNOLOGY

✓ COMPLETE

SCOPE

288 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.
