

North Lauderdale Pre K - 8 (f.k.a. North Lauderdale Elementary)



Address: 7500 KIMBERLY BOULEVARD, NORTH LAUDERDALE 33068
 Location Num: 2231
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$2,933,349
 Total Facilities Budget (Sum of Projects): \$3,541,349

PRIMARY RENOVATIONS P.001903 North Lauderdale ES - SMART Program Renovations

CURRENT PHASE

RISK LEVEL

5A-Construction

No Risk

PROJECT UPDATE

All scopes are in the following P numbers (no work remains in P.001903) Phase 1 - Fire Sprinklers: Building 1 (P.001903-FSP) status LOR - Fire Alarm Replacement: Building 1 (P.001903-FA1) - in award stage - ADA Restroom Upgrades: Building 1 (Rooms 155 and 156) (P.001903-ADA) in award stage - Test & Balance: Buildings 1, 5, 75, and 78. (P.001903-HVC) in bid phase

PROJECT SCOPE

All scopes are in the following P numbers (no work remains in P.001903) Phase 1 - Fire Sprinklers: Building 1 (P.001903-FSP) status LOR - Fire Alarm Replacement: Building 1 (P.001903-FA1) - in award stage - ADA Restroom Upgrades: Building 1 (Rooms 155 and 156) (P.001903-ADA) in award stage - Test & Balance: Buildings 1, 5, 75, and 78. (P.001903-HVC) in bid phase

BUDGET

	Current Budget	Actuals	Remaining Budget
Design	\$183,551	\$130,866	\$52,685
Construction	\$809,019		\$809,019
Construction Mgmt	\$233,764	\$233,764	\$0
Contingency	\$31,735		\$31,735
Consultants	\$5,000	\$106	\$4,894
Project Total:	\$1,263,069	\$364,736	\$898,333

FLAG: BUDGET, Reason: Budget Adjustment

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

North Lauderdale Pre K - 8 (f.k.a. North Lauderdale Elementary)



Address: 7500 KIMBERLY BOULEVARD, NORTH LAUDERDALE 33068
 Location Num: 2231
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$2,933,349
 Total Facilities Budget (Sum of Projects): \$3,541,349

PRIMARY RENOVATIONS P.001903-FA1 North Lauderdale ES - SMART Fire Alarm

CURRENT PHASE

RISK LEVEL

5A-Construction

No Risk

PROJECT UPDATE

Additional funding is required, this request is scheduled for the January 2024 board meeting. Meanwhile, the NTP/PO package has been prepared.

PROJECT SCOPE

Design Build for the replacement of the campus-wide fire alarm system

BUDGET

	Current Budget	Actuals	Remaining Budget
Construction	\$1,010,000		\$1,010,000
Contingency	\$55,000		\$55,000
Project Total:	\$1,065,000		\$1,065,000

FLAG: BUDGET, Reason: Budget Adjustment

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

North Lauderdale Pre K - 8 (f.k.a. North Lauderdale Elementary)



Address: 7500 KIMBERLY BOULEVARD, NORTH LAUDERDALE 33068
 Location Num: 2231
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$2,933,349
 Total Facilities Budget (Sum of Projects): \$3,541,349

PRIMARY RENOVATIONS P.001903-FSP North Lauderdale ES - SMART Fire Sprinklers

CURRENT PHASE

5B-Construction

RISK LEVEL

No Risk

PROJECT UPDATE

Building department review complete. Waiting on city of North Lauderdale permit for work in their jurisdiction. After receipt of N. Lauderdale permit BCPS will issue building permit

PROJECT SCOPE

Scope of work - Design Build North Lauderdale ES Building 1 install Fire Sprinklers (59,956 SF). Action Item: 1. Design Build - Fire Sprinklers Building #1 (59,956 SF) and connection to City water. 2. Prepare and submit a City of North Lauderdale Plumbing /Civil application for the permit: a. 2 signed and sealed Civil drawings sets

BUDGET

	Current Budget	Actuals	Remaining Budget
Construction	\$770,000	\$54,530	\$715,470
Project Total:	\$770,000	\$54,530	\$715,470

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



- HIGH:**
An issue that can impact the project's budget and/or schedule, a resolution is being determined.
- MEDIUM:**
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.
- LOW:**
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

North Lauderdale Pre K - 8 (f.k.a. North Lauderdale Elementary)



Address: 7500 KIMBERLY BOULEVARD, NORTH LAUDERDALE 33068
 Location Num: 2231
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$2,933,349
 Total Facilities Budget (Sum of Projects): \$3,541,349

PRIMARY RENOVATIONS P.001903-MCI North Lauderdale ES - SMART Media Center Improvements

CURRENT PHASE

RISK LEVEL

9-Closed

No Risk

PROJECT UPDATE

PROJECT SCOPE


Media Center improvements

BUDGET

	Current Budget	Actuals	Remaining Budget
Construction	\$71,932	\$71,932	\$0
FF&E and Technology	\$43,348	\$43,348	\$0
Project Total:	\$115,280	\$115,280	\$0

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
PROJECT PLANNING																																																
HIRE DESIGNER																																																
PROJECT DESIGN																																																
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

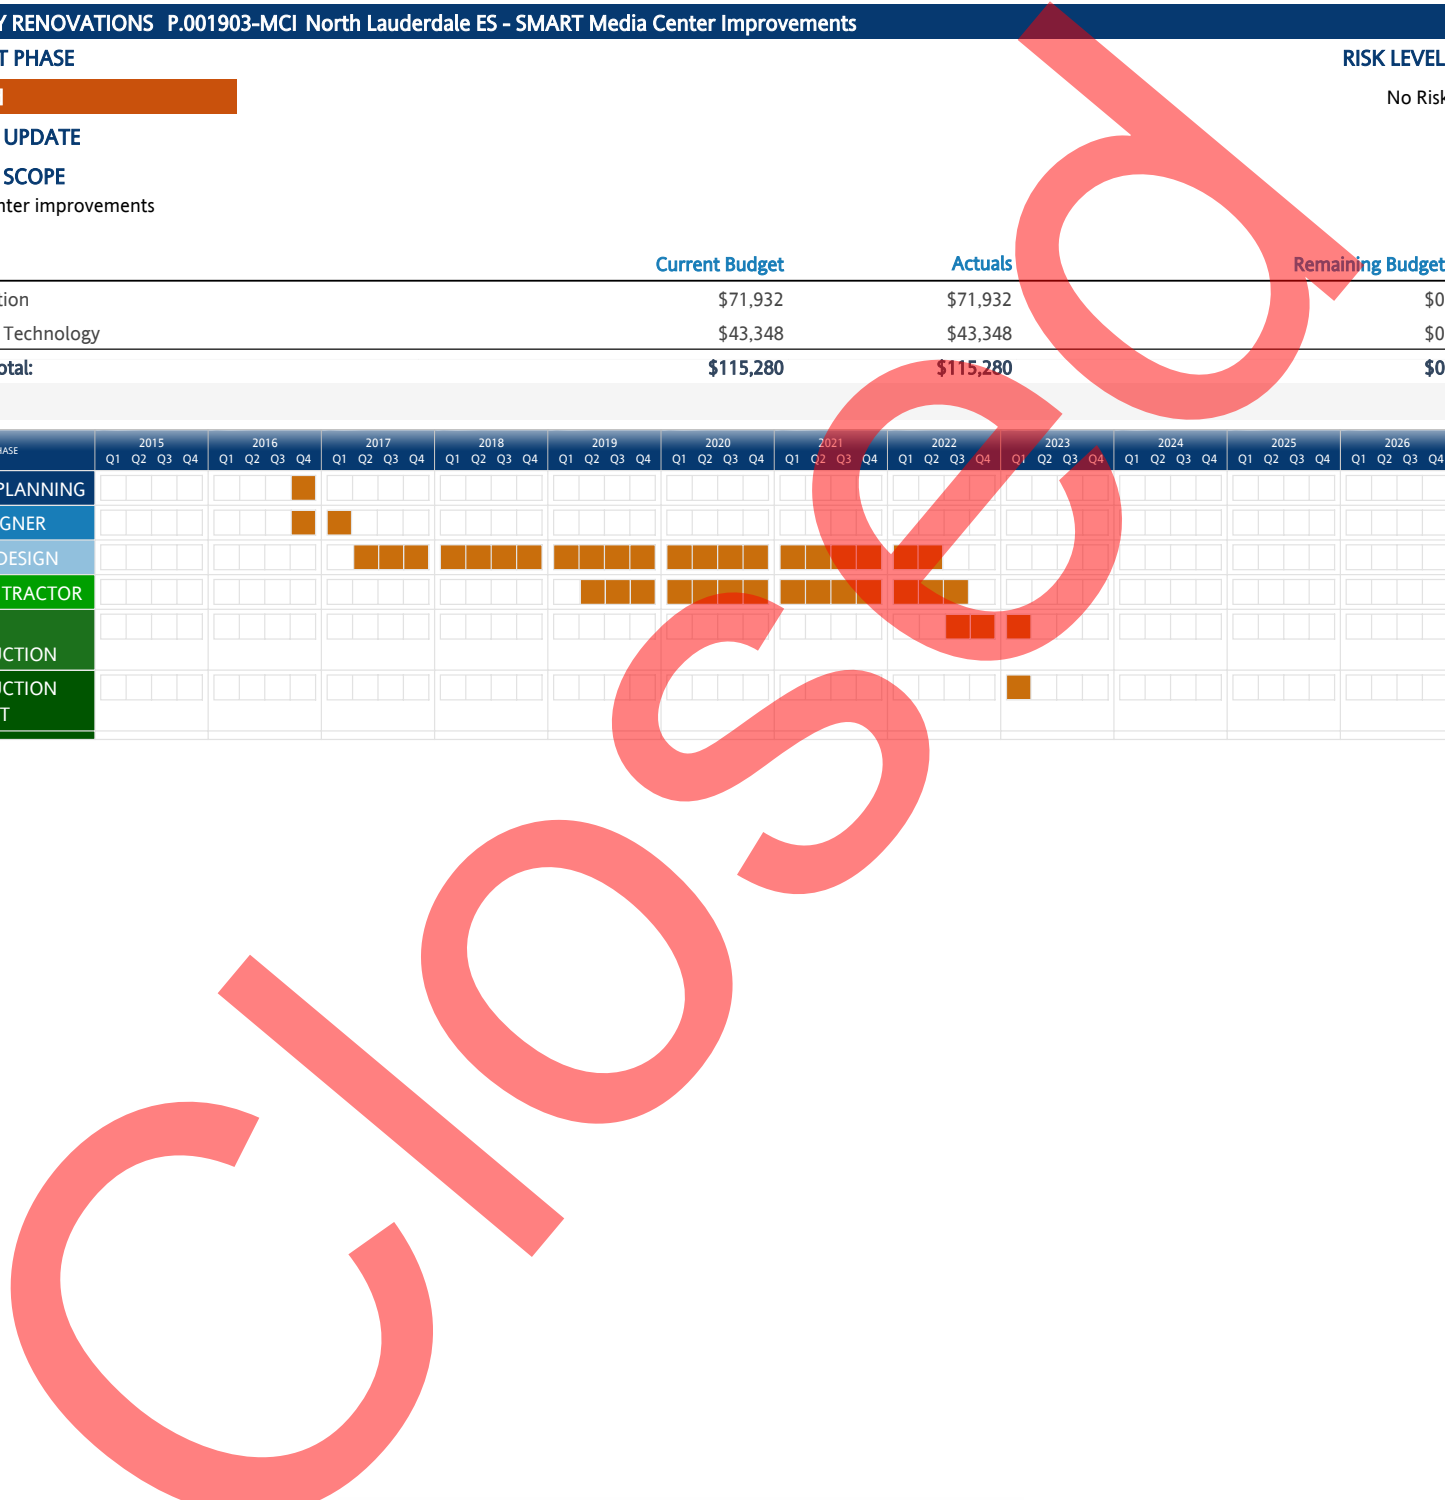

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



- HIGH:**
An issue that can impact the project's budget and/or schedule, a resolution is being determined.
- MEDIUM:**
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.
- LOW:**
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

North Lauderdale Pre K - 8 (f.k.a. North Lauderdale Elementary)



Address: 7500 KIMBERLY BOULEVARD, NORTH LAUDERDALE 33068
 Location Num: 2231
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$2,933,349
 Total Facilities Budget (Sum of Projects): \$3,541,349

PRIMARY RENOVATIONS P.002870 North Lauderdale ES - Roofing Building 2, 4 & 5 - SMART Program

CURRENT PHASE

9-Closed

RISK LEVEL

No Risk

PROJECT UPDATE

PROJECT SCOPE

Roofs carve-out, Bldgs. 2, 4 & 5 and their associated Mechanical Rooftop equipment

BUDGET

	Current Budget	Actuals	Remaining Budget
Construction	\$298,000	\$298,000	\$0
Construction Mgmt	\$30,000	\$30,000	\$0
Project Total:	\$328,000	\$328,000	\$0

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Student laptops, partial work for murals, TV screens for the front office, digital marquee, Aiphone & EDS, Shelving for the Media Center, Murals

BUDGET

\$100,000

IN PROGRESS

Murals for the media center (pending completion of renovations)

MUSIC

✓ COMPLETE

SCOPE

113 Instruments Delivered

TECHNOLOGY

✓ COMPLETE

SCOPE

209 Items Delivered

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:

An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:

An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:

A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.

North Lauderdale Pre K - 8 (f.k.a. North Lauderdale Elementary)



Address: 7500 KIMBERLY BOULEVARD, NORTH LAUDERDALE 33068
 Location Num: 2231
 Board District: 4
 Board Member: Lori Alhadeff
 ADEFP Budget: \$2,933,349
 Total Facilities Budget (Sum of Projects): \$3,541,349

PRIMARY RENOVATIONS P.001903-ADA North Lauderdale ES - SMART ADA Restrooms

CURRENT PHASE

5A-Construction

RISK LEVEL

No Risk

PROJECT UPDATE

The Project Manager is negotiating with a CSMP for an agreeable cost, narrative (scope of work), and schedule to be completed in January 2024.

PROJECT SCOPE

ADA Restroom Upgrades: Building 1 (Rooms 155 and 156)

FLAG:

PHASE	2015				2016				2017				2018				2019				2020				2021				2022				2023				2024				2025				2026			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4								
HIRE CONTRACTOR																																																
ACTIVE CONSTRUCTION																																																
CONSTRUCTION CLOSEOUT																																																

TRAFFIC LIGHT SCHEDULE RISK LEVEL INDICATOR



HIGH:
An issue that can impact the project's budget and/or schedule, a resolution is being determined.

MEDIUM:
An issue that may result in risks, causing an impact on the project budget and/or schedule, with a resolution planned and in process.

LOW:
A low-rated issue with little or no impact on the project budget and/or schedule but is still being tracked.
